

EDO Board Prep Study Guide



LCDR Victor Lee, USN, PMP

Guide Updated: 2025-11-20

EDO Coursebook Version: 2025-09-19

Contents

LIST OF FIGURES	VII
-----------------	-----

LIST OF TABLES	IX
----------------	----

1	ORGANIZATION	1
1.1	Command Chains and Governance	1
1.1.1	Operations Chain (Title 10)	1
1.1.2	Acquisition Governance (Department of the Navy)	3
1.1.3	Approving Authorities	5
1.2	Technical Authority and Engineering Agents	5
1.2.1	What Technical Authority Is	5
1.2.2	What EAs Do (and Do Not Do)	6
1.2.3	Where Engineering Agent Authority Comes From	6
1.2.4	Waterfront Triage: What Engages Whom	7
1.3	NAVSEA Organization and Warfare Centers	7
1.3.1	HQ Codes (must-know one-liners)	7
1.3.2	Warfare Centers (alphabetical)	8
1.3.3	NWC Locations	9
1.4	NAVWAR Enterprise and Warfare Centers	10
1.4.1	HQ Directorates and FRD	10
1.4.2	Warfare Centers (alphabetical)	11
1.5	NAVAIR Warfare Centers	12
1.6	Navy PEOs (Program Executive Offices)	12
1.6.1	PEO/Warfare Center Interaction Model	15
2	PPBE	16
2.1	PPBE (Planning, Programming, Budgeting, and Execution)	16
2.1.1	What PPBE does	16
2.1.2	Timeline (annual rhythm)	16
2.1.3	Congressional Enactment (Regular Order)	17
2.1.4	Key Terms and Definitions	18
2.1.5	Programming v.s. Budgeting	19
2.1.6	PPBE Programming	19
2.1.7	Appropriations Life-cycle (Colors of Money)	19
2.1.8	IGT (Intragovernmental Transactions)	20
2.1.9	Common Ordering Instruments	20

2.1.10	Fiscal Law (Know These Cold)	20
2.1.11	Reprogramming: Moving Resources After Enactment	21
2.1.12	From Enactment to Field Authority	21
2.2	NWCF Essentials: Rates, Results, and Execution	21
2.2.1	Key Definitions (Execution)	22
2.2.2	Flow: PMO Purchase Request to Treasury Payment	22
2.2.3	NWCF Metrics and Equations	22
2.2.4	NWCF Corpus v.s. Appropriations	22
2.2.5	Stabilized Rates and SLR	23
2.2.6	NWCF v.s. Mission-Funded (Appropriation) Commands	23
2.2.7	Standing Up or Modifying a NWCF Business Area	23
2.2.8	NWCF Cycle of Operations (Order to Cash)	24
2.2.9	Operating During a Continuing Resolution	24
2.2.10	Why Use a Warfare Center (Organic)	24
2.3	Congressional Enactment	25
2.3.1	Foundations and core definitions	25
2.3.2	Who drafts what	25
2.3.3	Regular-order timeline	25
2.3.4	The 12 regular appropriations bills	26
2.3.5	Continuing Resolution	27
2.3.6	Sequestration	27
2.4	Program Funding and Execution	27
2.4.1	BA, commitment, obligation, expenditure, outlay	27
2.4.2	Appropriation categories, scope, obligation windows	28
2.4.3	Funding policies	28
2.4.4	Navy Sustainment Funding: TYCOM v.s. Fleet (O&S)	29
2.4.5	Which money when (by acquisition phase)	30
2.4.6	MILCON v.s. O&M sustainment v.s. OPN modernization	30
2.4.7	Field Activity Financial Management (NWCF quick hits)	31
2.5	Cost Elements, Estimates, and Learning Curves	31
2.5.1	Direct v.s. Indirect Costs	31
2.5.2	Program Cost Terms (Know the Stack)	31
2.5.3	Why the LCCE Matters	32
2.5.4	Estimating Methods (Types, When, and Why)	33
2.5.5	Products and Players	33
2.5.6	Learning Curve (Production Efficiency)	34
2.5.7	Cost Escalation (Inflation Indices)	34
2.5.8	Will-Cost / Should-Cost	34
3	CONTRACTING AND SOLICITATION	35
3.1	Intro to Contracting Fundamentals	35
3.1.1	Why the Navy Uses Contracts	35
3.1.2	Essential Elements of a Binding Contract	35
3.1.3	Government Relationship to Contractors	35
3.1.4	FAR System and NAVSEA Overlays	36

3.1.5	<i>Types of Contracting Officers (Know All Three)</i>	36
3.1.6	<i>PM and KO Partnership</i>	36
3.1.7	<i>Competition in Contracting Act Requirements</i>	37
3.1.8	<i>Responsiveness, Responsibility, and Key Determinations</i>	37
3.1.9	<i>J&A v.s. D&F</i>	37
3.1.10	<i>Who Signs D&Fs (and When)</i>	38
3.2	Solicitation Preparation	38
3.2.1	<i>Summary</i>	38
3.2.2	<i>Practitioner Steps</i>	39
3.2.3	<i>Checklist</i>	39
3.2.4	<i>Navy Overlays and Tailoring</i>	40
3.2.5	<i>Industry Engagement & Communications</i>	40
3.2.6	<i>Documentation & Approvals to Capture</i>	40
3.2.7	<i>Competitive Method Selection: Sealed Bidding v.s. Negotiated Procurement</i>	40
3.2.8	<i>Contract Type Landscape and Risk Allocation</i>	41
3.2.9	<i>Fixed-Price Incentive (Firm Target) Mechanics</i>	43
3.2.10	<i>Indefinite & Flexible Contract Forms</i>	44
3.2.11	<i>Debriefings and Protests (Forums and Timelines)</i>	44
3.2.12	<i>Why Cost-Plus After Low-Rate Initial Production? (PD and O&S Exceptions)</i>	44
3.2.13	<i>Simplified Acquisition and Small Business Programs</i>	45
3.2.14	<i>Alternative Acquisition Authorities</i>	45
3.2.15	<i>Technical Data Rights Overview</i>	45
3.2.16	<i>Uniform Contract Format Essentials</i>	45
3.3	Cost and Price Evaluation	46
3.3.1	<i>Summary</i>	46
3.3.2	<i>Practitioner Steps</i>	46
3.3.3	<i>Proposed Price, Cost, Profit, and Fee</i>	46
3.3.4	<i>Direct and Indirect Cost Structure</i>	47
3.3.5	<i>Other Direct Costs and Cost Allowability</i>	47
3.3.6	<i>Cost and Price Analysis</i>	48
3.3.7	<i>Forward Pricing Rates and Fully Burdened Labor</i>	48
3.3.8	<i>Indirect Rate Math and Profitability Checks</i>	49
3.3.9	<i>Oversight and Field Pricing Support</i>	49
3.3.10	<i>Checklist</i>	49
3.4	Earned Value Management (EVM)	50
3.4.1	<i>What EVM is</i>	50
3.4.2	<i>Key Components of EVM</i>	50
3.4.3	<i>When to Use EVM</i>	51
3.4.4	<i>EVM Compliance</i>	51
3.4.5	<i>EVM Compliance</i>	51
3.4.6	<i>EVM Principal Players</i>	52
3.4.7	<i>PMB</i>	52
3.4.8	<i>EVM Reviews and Reports</i>	54
3.4.9	<i>EVM Data Analysis</i>	55

4	DEFENSE ACQUISITIONS	58
4.1	Acquisition Policy	58
4.1.1	Summary	58
4.1.2	Practitioner Steps (Board Prep Focus)	59
4.1.3	Policy Stack and Authorities	60
4.1.4	Acquisition Players and Decision Forums	60
4.1.5	Adaptive Acquisition Framework Pathways	61
4.1.6	Warfighting Acquisition System Imperatives (2025)	64
4.1.7	Urgent Operational Needs Governance	65
4.1.8	Security Cooperation and Capital Alignment (2025 Reforms)	65
4.1.9	Acquisition Categories and Delegated Decision Authority	66
4.1.10	Project Overmatch Status	67
4.1.11	Navy Overlays and Touchpoints	67
4.2	Milestones and Phases	67
4.2.1	Defense Acquisition System Overview	68
4.2.2	Adaptive Acquisition Framework Pathways (Board Snapshot)	68
4.2.3	Baseline Discipline: Acquisition Program Baselines, Deviations, and Nunn-McCurdy	68
4.2.4	JCIDS Flow into the Defense Acquisition System	69
4.2.5	KPPs v.s. KSAs (Know the Difference)	69
4.2.6	Acquisition Strategy Essentials	69
4.2.7	International Acquisition Objectives	69
4.2.8	Navy Two-Pass / Seven-Gate Review	70
4.2.9	Technology Readiness Levels	70
4.2.10	T&E Organizations and Roles	71
4.2.11	Major Capability Acquisition Lifecycle Overview	71
4.2.12	Materiel Development Decision	75
4.2.13	Materiel Solution Analysis Phase Essentials	75
4.2.14	Milestone A Focus Areas	75
4.2.15	Technology Maturation and Risk Reduction Phase Essentials	75
4.2.16	Milestone B Focus Areas	76
4.2.17	Engineering and Manufacturing Development Phase Essentials	76
4.2.18	Milestone C Focus Areas	76
4.2.19	Production and Deployment Phase Essentials	76
4.2.20	Operations and Support Phase Essentials	77
5	REQUIREMENTS	78
5.1	Joint Capabilities Integration & Development System	78
5.1.1	Requirements Demand Versus Acquisition Supply	78
5.1.2	Capability Requirements and the Capability-Based Assessment Cadence	79
5.1.3	Strategy-to-Requirement Synchronization	80
5.1.4	Major Capability Acquisition Requirement Set	80
5.1.5	How KPPs Stay Integrated with DAS	81
5.1.6	Prioritizing Materiel and Non-Materiel Solutions	81
5.1.7	Governance Roles and Validation Chain	82
5.1.8	IT, C4I, and Coalition Interoperability Implications	82

5.1.9	Warfighting Acquisition System (JCIDS Replacement)	83
5.1.10	What EDOs Must Master Under WAS	84
5.1.11	Current Events: SECWAR Acquisition Transformation Strategy	85
5.2	Test & Evaluation	85
5.2.1	Board Prep Summary	85
5.2.2	Definition and Relationship to Verification and Validation	86
5.2.3	Statutory Requirements and Key Roles	86
5.2.4	Developmental Test Activities	87
5.2.5	Live Fire Test and Evaluation	88
5.2.6	Operational Test Phases	88
5.2.7	Fundamental Test and Evaluation Terms	88
5.2.8	Critical Technical Parameters and Technical Performance Measures	89
5.2.9	Test and Evaluation Master Plan	89
5.2.10	Modeling and Simulation	89
5.2.11	Navy Overlays and Integration	90
5.2.12	Fiscal and PPBE Touchpoints	90
5.2.13	Assumptions and Uncertainties	90
6	MAINTENANCE	91
6.1	Fleet Maintenance Assets	91
6.1.1	Echeloned Maintenance Levels	91
6.1.2	Shore Maintenance Organizations and Roles	91
6.1.3	Command, Funding, and Technical Authority Chains	92
6.1.4	Workforce Readiness and Assessments	92
6.2	Navy Modernization Program	93
6.2.1	Modernization vs. Maintenance	93
6.2.2	Governance, Roles, and Documentation	93
6.2.3	Process Flow and Funding Integration	93
6.2.4	Execution Enablers and Lessons Learned	94
6.3	Fleet Maintenance Policy and Implementation	94
6.3.1	Policy Baseline	94
6.3.2	Strategy Frameworks	95
6.3.3	Availability Approval and Execution Discipline	95
6.3.4	Trends, Risks, and Talking Points	95
6.4	AIT Fundamentals and Lessons Learned	96
6.4.1	Purpose and Advantages	96
6.4.2	Roles and Responsibilities	96
6.4.3	Planning Controls and MOA Discipline	97
6.4.4	Lessons Learned for Board Prep	97
6.5	Waterfront Organizations, Work Controls, and Safety	97
6.5.1	Naval Propulsion Program Oversight	97
6.5.2	SUBSAFE and Submergence Systems Controls	98
6.5.3	Work Authorization and Tag-out Discipline	98
6.5.4	Waterfront Organization Insights	98

6.6	Battle Damage Assessment and Repair	99
6.6.1	Strategic Context	99
6.6.2	BDAR Continuum	99
6.6.3	Command, Control, and Technical Authority	100
6.6.4	Logistics, Contracting, and Fiscal Readiness	100
6.6.5	Maritime Support Plan Force Packages	100
6.7	CNO Availability Planning	101
6.7.1	Balancing Requirements, Resources, and Readiness	101
6.7.2	Availability Work Package Development	101
6.7.3	Planning Teams and Integration Forums	101
6.7.4	Risk Controls and Board-Ready Talking Points	102
6.8	CNO Availability Execution	102
6.8.1	Project Teams and Responsibilities	102
6.8.2	Execution Phases	103
6.8.3	Governance, Quality, and Work Control	103
6.8.4	Lessons Learned	104
Appendices		106
A	PLATINUM CARD	106
B	KEY ROLES IN ACQUISITION AND MODERNIZATION	112
B.1	EDO Flag Officers (snapshot)	112
B.2	Key Roles in Acquisition and Modernization	113
B.3	Combatant Commands (Reference)	120
B.4	Current Events Relevant to EDOs and Acquisition	120
B.4.1	Project Overmatch and Digital Modernization	120
B.4.2	EDO Community Updates	121
B.4.3	Acquisition Policy and Industrial Base Highlights	121
LIST OF ACRONYMS		123

List of Figures

1.1	Title 10 Chain of Command	2
1.2	Organization Command Structure	3
1.3	Acquisition Governance Chain of Command	4
1.4	Technical Authority v.s. Program Authority	5
1.5	Geographic locations of Navy Warfare Center	10
2.1	PPBE Timeline for multiple fiscal years	17
2.2	Congressional Enactment Timeline	18
2.3	Colors of Money Timeline	20
2.4	Congressional Enactment Timeline	26
2.5	Life Cycle Costs	32
2.6	Lif-Cycle Cost	32
3.1	Fixed Price Contracts	41
3.2	Cost Reimbursement Contracts	42
3.3	Contract-type emphasis across the Major Capability Acquisition phases.	43
3.4	Direct v.s. Indirect Costs	47
3.5	PMB “S”-Curve	53
3.6	PMB Development Flow	53
3.7	EVM Variances	55
4.1	Cost, Schedule, Performance	58
4.2	Trade Space, Performance v.s. Cost	59
4.3	Adaptive Acquisition Pathways	61
4.4	Major Capability Acquisition	62
4.5	MCA Lifecycle View	74
5.1	JCIDS to DAS Relationship	79
5.2	Concept to Requirement Flow	80
5.3	JCIDS Artifacts within MCA	81
5.4	MCA T&E Touchpoints	86
5.5	Notional Department of War(DoW) test and evaluation governance chain.	87
A.1	Platinum Card: Life Cycle Cost Composition	106

A.2	Platinum Card: Cost Estimating Requirements	107
A.3	Platinum Card: PPBE Planning Phase (Lead by USD (P))	107
A.4	Platinum Card: Concurrent Program/Budget Review	108
A.5	Platinum Card: Below Threshold Reprogramming	109
A.6	Platinum Card: Resource Allocation Process	109
A.7	Platinum Card: Congressional Enactment Timeline	110
A.8	Platinum Card: Funding for Product Improvements	110
A.9	Platinum Card: Appropriation Life Cycle	111

List of Tables

1.1	NAVSEA Warfare Centers	8
1.2	NAVWAR HQ Directorates and FRDs	10
1.3	NAVWAR Warfare Centers	11
1.4	NAVAIR Warfare Centers	12
2.1	Key PPBE Terms	18
2.2	Programming v.s. Budgeting	19
2.3	Colors of Money	28
2.4	Exceptions to Full Funding	29
2.5	Appropriations per Phase	30
2.6		33
4.1	TRL reference	70

1 Organization

1.1 Command Chains and Governance

Refs:

1.1.1 Operations Chain (Title 10)

Chain flow. President → Secretary of War (SECDEF) → Combatant Commander (CCDR). The Chairman of the Joint Chiefs of Staff (CJCS) is the principal military adviser; service chiefs are *not* in the operational chain of Title 10.

Board cue. Boards love the contrast with acquisition authority; avoid conflating operational and acquisition chains.

Echelons. Counted from the Chief of Naval Operations (CNO) (e.g., CNO is Echelon I, Systems Commands (SYSCOMs) are Echelon II, etc.).

Figure 1.1 shows the Title 10 chain of command. Figure 1.2 shows the Chain of Command from the President to Echelon III commands.

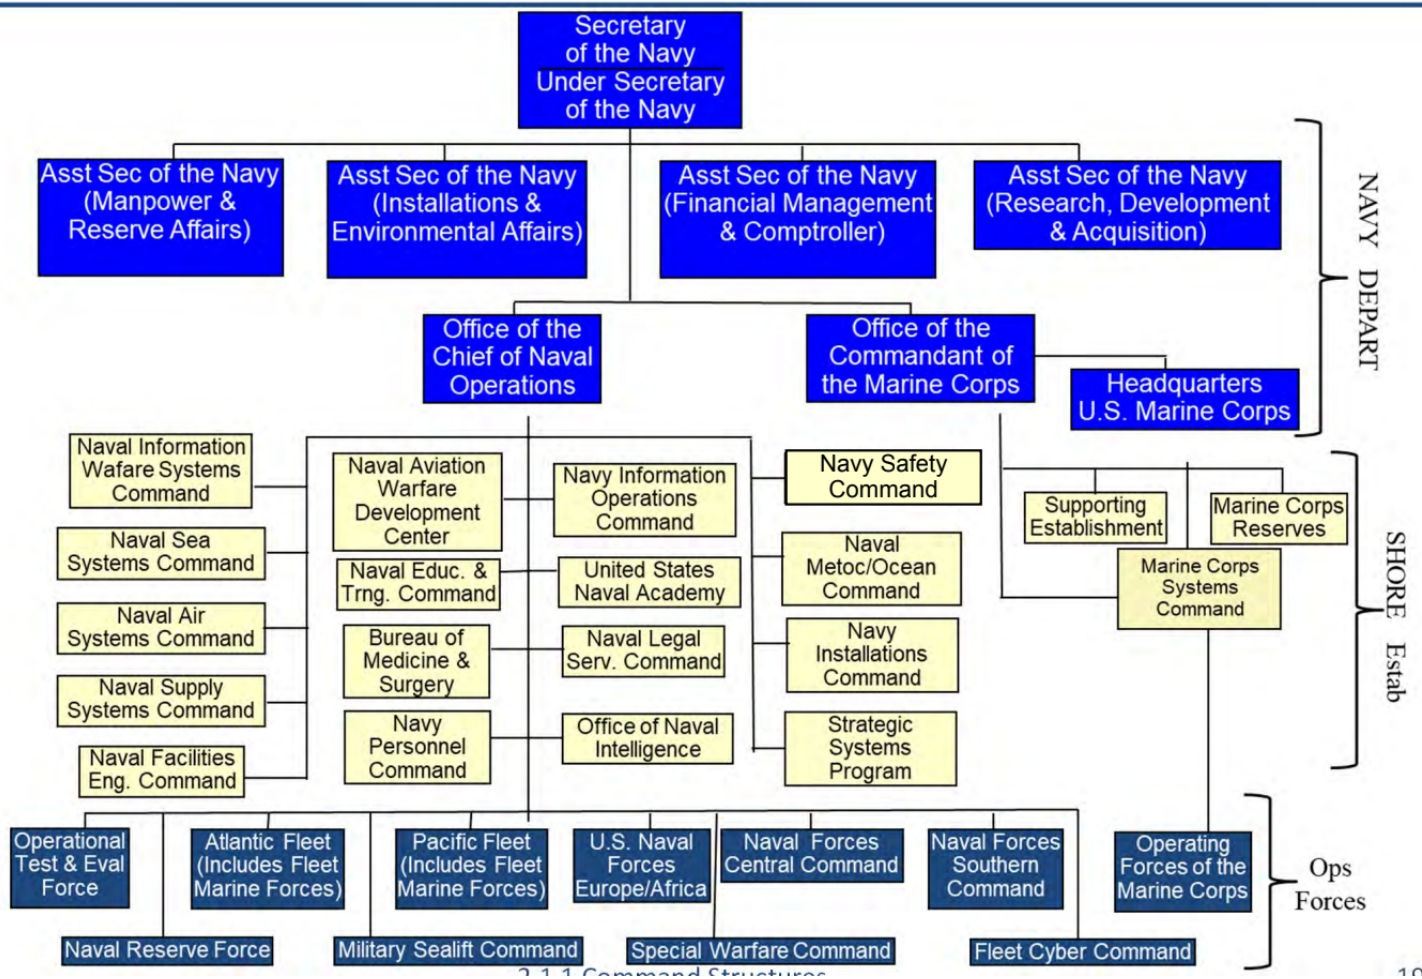


Figure 1.1. Title 10 Chain of Command. Source: edo-2-1-1-command-structures-2025, edo-2-1-1-command-structures-2025 [edo-2-1-1-command-str...

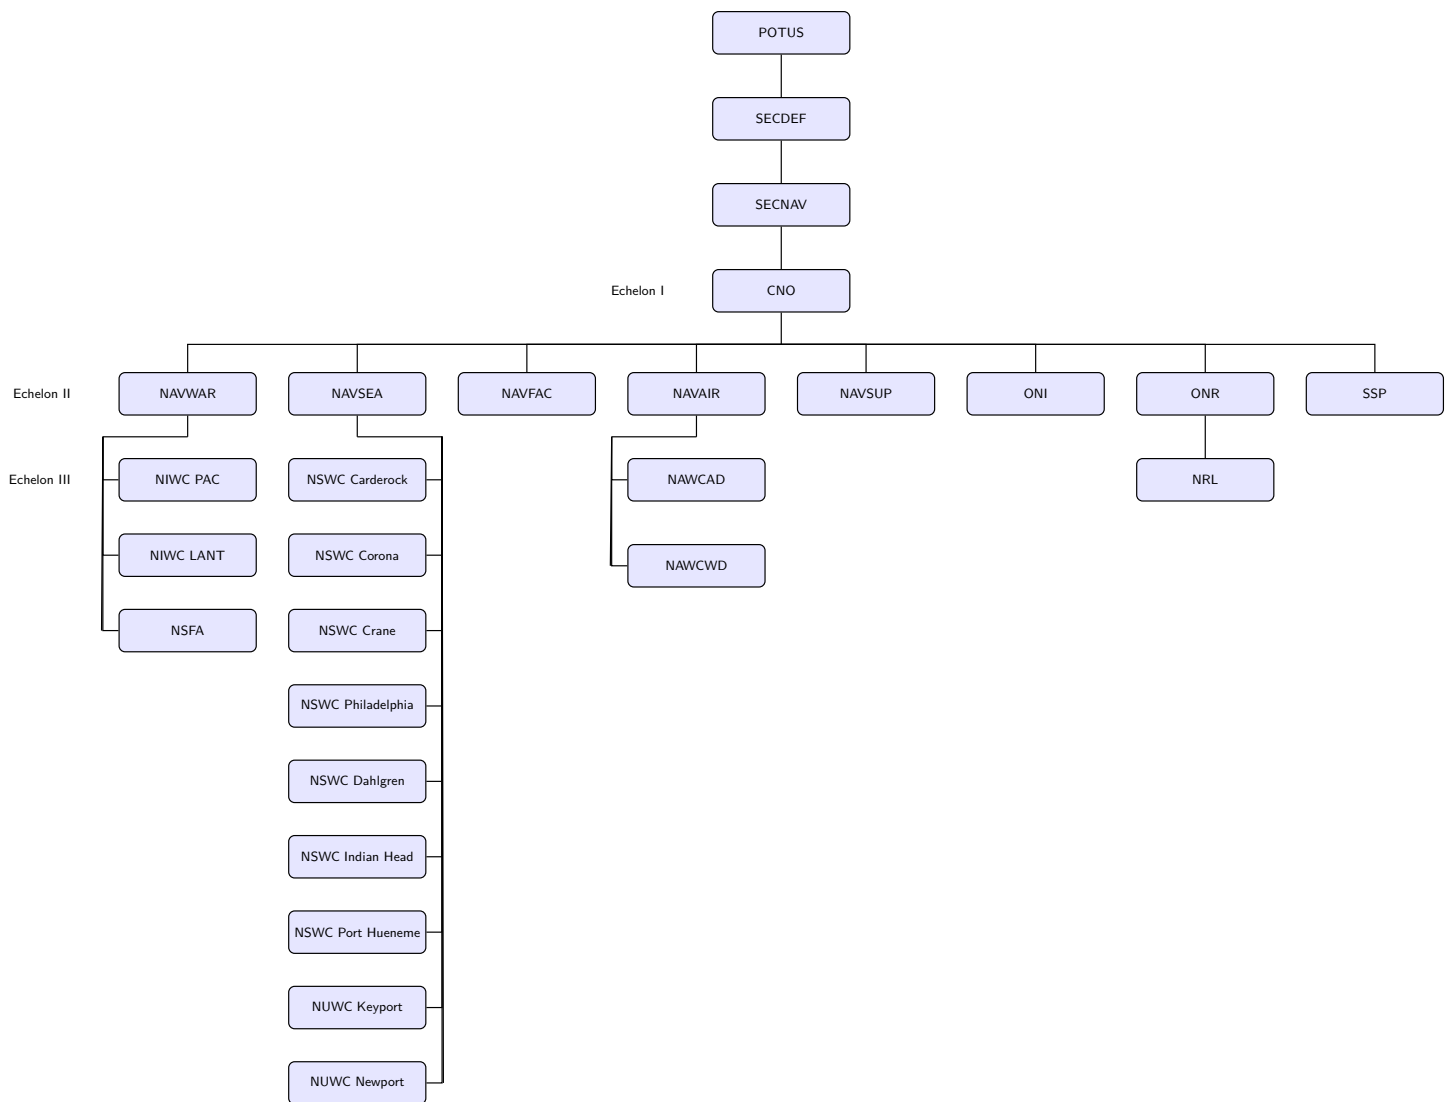



Figure 1.2. Organization Command Structure

1.1.2 Acquisition Governance (Department of the Navy)

Policy authority. Assistant Secretary of the Navy for Research, Development and Acquisition (ASN(RD&A)) is the Service Acquisition Executive (SAE) for the Department of the Navy (DON) and sets policy for Program Executive Offices (PEOs) and Direct Reporting Program Managers (DRPMs) [SECNAV5400-15D, SECNAV5000-2G].

Matrix execution. PEOs hold program authority; SYSCOMs (Naval Sea Systems Command (NAVSEA), Naval Information Warfare Systems Command (NAWWAR), Naval Air Systems Command (NAVAIR)) provide the Technical Authority (TA) warrants and workforce; Naval Warfare Centers (NWCs) deliver research, development, test, and engineering support [SECNAV5400-15D].

Figure 1.3 shows the Navy acquisition governance chain of command.

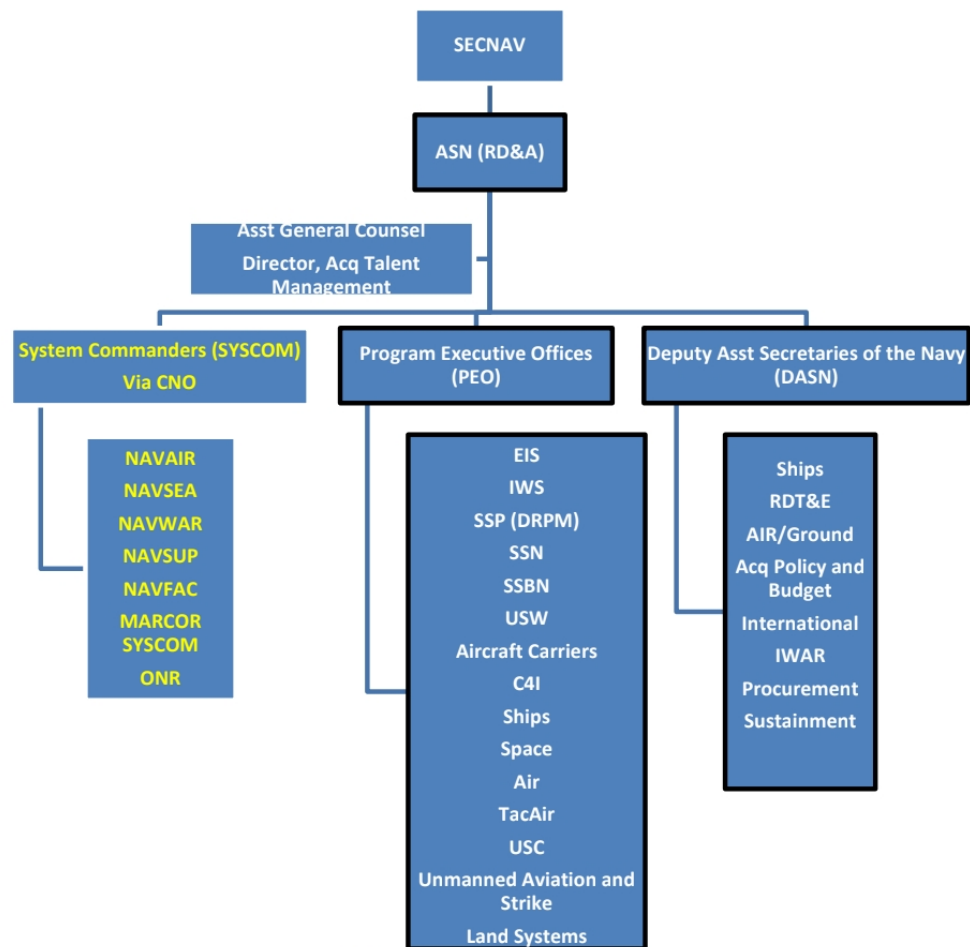

2.1.1 Command Structures

Figure 1.3. Acquisition Governance Chain of Command. Source: edo-2-1-1-command-structures-2025, edo-2-1-1-command-structures-2025 [edo-2-1-1-1]

1.1.3 Approving Authorities

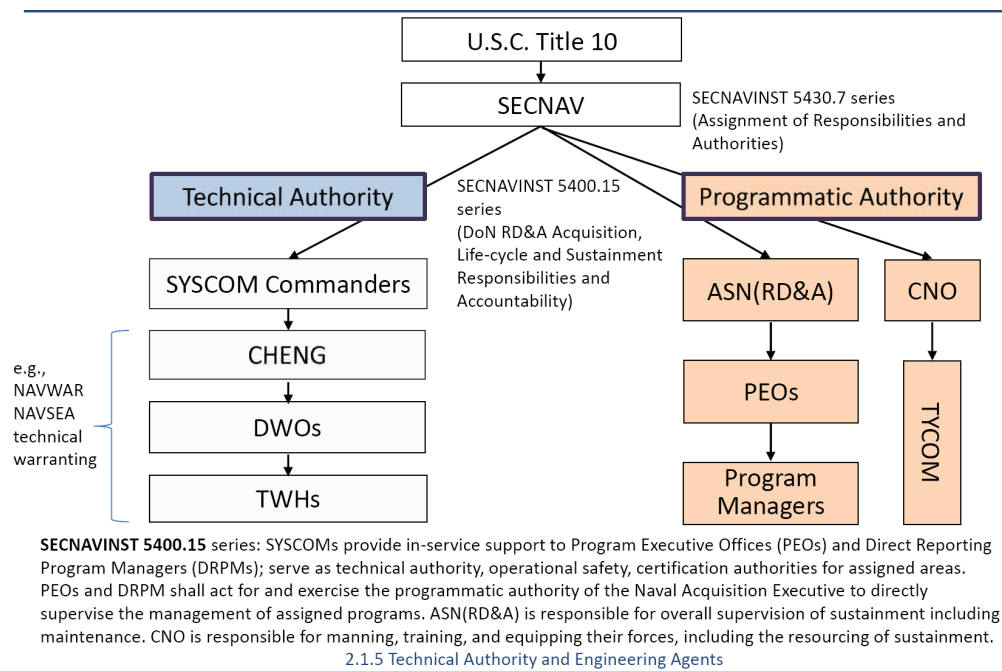


Figure 1.4. Technical Authority v.s. Program Authority alignment. Source: edo-2-1-5-technical-authority-2025, edo-2-1-5-technical-authority-2025 [edo-2-1-5-technical-authority-2025]

Figure 1.4 contrasts the roles of TA and Program Authority (PA) in Navy acquisition.

1.2 Technical Authority and Engineering Agents

Refs:

1.2.1 What Technical Authority Is

TA. Independent engineering authority to set, maintain, and certify conformance to technical standards and baselines across the lifecycle [SECNAV5400-15D].

Ultimate Technical Authority (UTA). Executed at the SYSCOM level (e.g., NAVSEA); resides with the Commander and flows through the Chief Engineer via a formal warranting system [edo-2-1-5-technical-authority-2025].

Delegated TA. Technical Warrant Holders (TWHs) (*Lead/Local/Warranted* TA) receive domain-specific authority across hull, mechanical, and electrical systems, combat systems, cybersecurity, and airworthiness or seaworthiness [edo-2-1-5-technical-authority-2025].

Core TA duties. Must-know responsibilities:

1. Establish and approve technical requirements, standards, and certification criteria;
2. Control the authoritative technical baseline (drawings, specs, interface control);
3. Adjudicate departures and waivers from specification and safety-critical changes; and
4. Certify readiness, readiness for service, and technical acceptability.

Independence. TA remains separate from cost, schedule, and programmatic authority to protect warfighter safety and mission assurance [SECNAV5400-15D].

1.2.2 What EAs Do (and Do Not Do)

Engineering Agents (EAs) perform lifecycle engineering under TA governance. They are *not* TA unless they hold a TA warrant [edo-2-1-5-technical-authority-2025]. Common EA roles include:

In-Service Engineering Agent (ISEA). Lifecycle systems engineering for *fielded* systems (e.g., fleet introduction, distance support, troubleshooting/Casualty Report (CASREP) support, maintenance planning, obsolescence, technical manuals/data, configuration of the in-service baseline).

Design Agent (DA). Develops detailed design and configuration documentation for a system or platform (e.g., ship detail design, Initial Capabilities Documents (ICDs), drawings, Technical Data Packages (TDPs)) to TA-approved standards.

Alteration Engineering Agent (AEA). Produces alteration packages (e.g., installation drawings, test procedures, logistics updates) and supports fleet introduction for ship or system changes.

Systems Integration Agent (SIA). Orchestrates system-of-systems integration (e.g., interfaces, interoperability, cybersecurity in the integration space) across combat system elements and platforms.

Technical Direction Agent (TDA). Issues and maintains technical work direction for installations and maintenance (e.g., Technical Work Document (TWD), local instructions) consistent with the TA-approved baseline.

1.2.3 Where Engineering Agent Authority Comes From

Statutory basis. [SECNAV5400-15D] assigns DON acquisition responsibilities, directing SYSCOMs to execute TA and to designate Warfare Centers as EAs that support PEOs and Program Managers (PMs).

Delegations from TA. NAVSEA, NAVAIR, and NAVWAR Chief Engineers issue written warrants or designation letters (Lead/Lab/Local TA) that flow requirements to specific Warfare Center codes; EA charters reference those warrants [edo-2-1-5-technical-authority-2025].

Execution orders. PEOs and PMs provide technical direction letters, project orders, and statements of work that scope the EA's tasks while preserving independence for specification compliance and certification [edo-2-1-4-warfare-centers-2024].

Accountability. EAs report to the SYSCOM Chief Engineer for technical rigor and to the sponsoring PM for cost and schedule; loss of a warrant or charter terminates their authority to issue technical documentation [edo-2-1-5-technical-authority-2025].

1.2.4 Waterfront Triage: What Engages Whom

Spec/drawing nonconformance (build or repair). Generate a departure or waiver request for the proper TA warrant holder; minor deviations may be approved by Local or Lead TA, while major or safety-critical issues go to the Chief Engineer/UTA.

In-service failure (CASREP/technical assist). ISEA opens a support case, provides immediate workarounds and troubleshooting, coordinates root-cause analysis, updates technical data, and recommends permanent fixes (engineering change or alteration).

Change to configuration. If a permanent change is needed, the AEA develops the alteration package; SIA validates interfaces; DA updates drawings and TDPs; TA approves and certifies.

Principle to remember. EAs execute engineering; TA sets the rules and certifies compliance.

1.3 NAVSEA Organization and Warfare Centers

Refs:

1.3.1 HQ Codes (must-know one-liners)

SEA 01 – Comptroller. Budget Submitting Office (BSO); leads NAVSEA financial governance.

SEA 02 – Contracts. Contracting authority and policy.

SEA 03 – Cyber Engineering and Digital. Enterprise cyber engineering and digital transformation.

SEA 04 – Industrial Operations. Shipyards, logistics, and quality-assurance oversight.

SEA 05 – Chief Engineer (TA). Sets engineering standards and certifies designs.

SEA 06 – Sustainment. Life-cycle product support.

SEA 07 – Undersea Warfare. Dual-hatted as Program Executive Office, Undersea Warfare Systems (PEO UWS); provides life-cycle support for in-service submarine and undersea forces.

SEA 08 – Nuclear Propulsion. Manages all technical matters pertaining to naval reactors. Triple-hat duties:

SEA 08 Deputy Commander. Leads nuclear propulsion activities within NAVSEA.

- Director, Naval Nuclear Propulsion (Office of the Chief of Naval Operations (OPNAV) 00N).** Serves as the Navy’s principal nuclear propulsion authority.
- Deputy Administrator for Naval Reactors.** Interfaces with the National Nuclear Security Administration and the Department of Energy.
- SEA 09 – Safety and Regulatory Compliance.** Strengthens and aligns safety oversight and reporting.
- SEA 10 – Total Force and Corporate Operations.** Manages the workforce, corporate services, and governance.
- SEA 21 – In-Service Ships (dual-hat Commander, Navy Regional Maintenance Center (CNRMC)).** Oversees fleet surface-ship sustainment and modernization. Program Management Offices (PMOs) under SEA 21:
- PMS 321.** Unmanned small combatants and amphibious ships.
 - PMS 326.** International fleet support.
 - PMS 339.** Surface training systems.
 - PMS 421.** Large surface combatant modernization and sustainment.
 - PMS 443.** Bridge integration and HM&E sustainment.
 - PMS 451.** Destroyer Modernization 2.0 portfolio.
- SEA 21I.** Inactive Ships Directorate.
- Surface Maintenance Engineering Planning Program (SURFMEPP) Activity.** Surface Maintenance Engineering Planning Program.

1.3.2 Warfare Centers (alphabetical)

Table 1.1 lists NAVSEA Warfare Centers with locations and descriptions.

TABLE 1.1: NAVSEA WARFARE CENTERS WITH LOCATIONS AND DESCRIPTIONS.

CENTER	LOCATION	DESCRIPTION
NSWC Carderock	West Bethesda, MD	Ship design and engineering.
NSWC Corona	Corona, CA	Analytics and data driven performance assessments.
NSWC Crane	Crane, IN	Electronic/expeditionary warfare; strategic system components.
NSWC Dahlgren	Dahlgren, VA	Surface ship weapons system development and integration .
NSWC Dam Neck	Virginia Beach, VA	Combat-system software, training/testing.
NSWC Indian Head	Indian Head, MD	Energetics, explosive-ordnance-disposal technologies.

Continued on next page

TABLE 1.1: NAVSEA WARFARE CENTERS WITH LOCATIONS AND DESCRIPTIONS. (Continued)

CENTER	LOCATION	DESCRIPTION
NSWC Panama City	Panama City, FL	Mine warfare and littoral warfare systems.
NSWC Philadelphia	Philadelphia, PA	Surface and undersea machinery, power, controls, and auxiliary ship systems.
NSWC Port Hueneme	Port Hueneme, CA	Integrated logistics and test and evaluation for surface warfare combat systems.
NUWC Keyport	Keyport, WA	Sustaining undersea warfare systems and vehicles.
NUWC Newport	Newport, RI	Undersea, subsea, and seabed warfare weapons systems development and integration.

Source: edo-2-1-4-warfare-centers-2024, edo-2-1-4-warfare-centers-2024 [edo-2-1-4-warfare-centers-2024]
navsea_warfare_centers, navsea_warfare_centers [navsea_warfare_centers]

Hint: Remember that for Naval Surface Warfare Centers (NSWCs) there are 3-C's, 2-D's, and 3-P's plus 1-I. There are only two "Ports" for Naval Undersea Warfare Centers (NUWCs).

Note: NSWC Dam Neck is a detachment of Dahlgren.

1.3.3 NWC Locations

Figure 1.5 shows the geographic locations of NWCs. For the Engineering Duty Officer (EDO) board, most recommend drawing the US to show where the NWCs are located. The other option is to list them out, but a map is more visual.



Figure 1.5. Geographic locations of Navy Warfare Centers.Source: edo-2-1-4-warfare-centers-2024, edo-2-1-4-warfare-centers-2024 [edo-2-1-4-warfare-centers-2024]

1.4 NAVWAR Enterprise and Warfare Centers

Refs:

1.4.1 HQ Directorates and FRD

Table 1.2 lists NAVWAR HQ directorates and Fleet Readiness Directorates (FRDs) with one-line roles.

TABLE 1.2: NAVWARHQ DIRECTORATES AND FIELD READINESS DIRECTORATES – ONE-LINE ROLES.

CODE	OFFICE	ONE-LINER
1.0	Comptroller	Budget formulation/execution; BSO duties; funds control and financial reporting.

Continued on next page

TABLE 1.2: NAVWARHQ DIRECTORATES AND FIELD READINESS DIRECTORATES – ONE-LINE ROLES. (Continued)

CODE	OFFICE	ONE-LINER
2.0	Contracts	Contracting policy/oversight; acquisition strategy; award/administration of instruments.
3.0	Counsel	Legal counsel for acquisition/ethics; protests, claims, agreements, and compliance.
4.0	Logistics & Fleet Support	Life-cycle logistics; sustainment planning; supply/tech data; fleet support integration.
5.0	Chief Engineer / TA (Cyber)	Technical standards/architecture; interoperability; cyber TA; certification/air-gapping where required.
6.0	Program Management	Program governance; milestone readiness; portfolio integration; interface with PEOs.
7.0	Science & Technology	S&T portfolio; experimentation/prototyping; tech transition to programs of record.
8.0	Corporate Operations	Workforce, security, facilities, enterprise information-technology/chief-information-officer services, PAO, and other corporate enablers.
FRD-100	Fleet Support	Sustainment services and distance support; field engineering and readiness assistance.
FRD-200	Installations	C4I installation planning/execution; shore/afloat integration and cutover support.

Source: edo-2-1-3-navwar-enterprise-2024, edo-2-1-3-navwar-enterprise-2024 [edo-2-1-3-navwar-enterprise-2024]

1.4.2 Warfare Centers (alphabetical)

Table 1.3 lists NAVWAR Warfare Centers with locations and descriptions.

TABLE 1.3: NAVWAR WARFARE CENTERS WITH LOCATIONS AND DESCRIPTIONS.

CENTER	LOCATION	DESCRIPTION
NIWC LANT	Charleston, SC	Enterprise information-technology solutions; cradle-to-grave C4ISR.
NIWC PAC	San Diego, CA	C4ISR RDT&E; Navy/Joint/Allied support.
NSFA	Chantilly, VA	Navy link to the NRO; space research and development coordination.

Source: edo-2-1-3-navwar-enterprise-2024, edo-2-1-3-navwar-enterprise-2024 [edo-2-1-3-navwar-enterprise-2024]

NIWC LANT detachments

- HQ: Charleston, SC.
- New Orleans, LA.
- Norfolk, VA.
- Naples, Italy.
- Manama, Bahrain.

NIWC PAC detachments

- **HQ:** San Diego, CA.
- Everett, WA.
- Pearl City, HI.
- Santa Rita, Guam.
- Yokosuka, Japan.

1.5 NAVAIR Warfare Centers

Refs:

Table 1.4 lists NAVAIR Warfare Centers with locations and descriptions. This is an optional item to know for the EDO board, not as critical as NAVSEA/NAVWAR.

TABLE 1.4: NAVAIR WARFARE CENTERS WITH LOCATIONS AND DESCRIPTIONS.

CENTER	LOCATION	DESCRIPTION
NAWCAD	Patuxent River, MD	Aircraft/engines/avionics RDT&E; Test Pilot School.
NAWCWD	China Lake / Point Mugu, CA	Weapons systems, ranges, guided-missile integration.

Source: edo-2-1-4-warfare-centers-2024, edo-2-1-4-warfare-centers-2024 [edo-2-1-4-warfare-centers-2024]

1.6 Navy PEOs (Program Executive Offices)

Refs:

Program Executive Office, Aircraft Carriers (PEO CVN). Designs, builds, delivers, and sustains nuclear-powered aircraft carriers.

- PMS 312.** In-service aircraft carrier program management.
- PMS 378.** Nuclear-Powered Aircraft Carrier (CVN)-78 class program management.
- PMS 379.** CVN-79/80 program management.

Program Executive Office, Integrated Warfare Systems (PEO IWS). Develops and sustains ship and submarine combat systems.

- IWS 1.0.** Aegis combat system lead.

IWS 1.0F. Aegis fleet readiness.

IWS 2.0. Above-water sensors portfolio.

IWS 3.0. Surface ship weapons integration.

IWS 4.0. International and foreign military sales.

IWS 5.0. Undersea systems.

IWS 6.0. Command-and-control systems.

IWS 9.0. DDG-1000, littoral combat ship, and patrol craft combat systems.

IWS 11.0. Terminal defense systems.

IWS 12.0. NATO Seasparrow programs.

IWS 80.0. Atalanta combat systems.

IWS X. Integrated combat-system document center.

Program Executive Office, Ships (PEO Ships). Oversees surface combatant and amphibious ship construction and modernization.

Program Executive Office, Unmanned and Small Combatants (PEO USC). Manages littoral combat ships, frigates, expeditionary platforms, and unmanned surface/undersea portfolios.

Team Submarines. Integrates strategic and attack submarine acquisition and sustainment.

Program Executive Office, Attack Submarines (PEO SSN). Attack submarine programs.

PMS 351. New attack submarine acquisition.

PMS 390. Undersea special mission systems.

PMS 391. In-service submarine sustainment.

PMS 394. Advanced undersea systems development.

PMS 450. Virginia class program management.

Program Executive Office, SSBN (PEO SSBN). Strategic deterrent submarine portfolio.

PMS 396. In-service Ballistic Missile Submarine, Nuclear (SSBN) sustainment.

PMS 397. Columbia class program management.

Submarine Maintenance Engineering Planning Program (SUBMEPP). Surface maintenance engineering planning program support to ballistic submarine availabilities.

PEO UWS. Submarine combat, cyber, and sensor systems.

PMS 401. Submarine acoustic systems.

PMS 404. Undersea weapons.

PMS 415. Undersea defensive warfare systems.

PMS 425. Combat and weapon control systems.

PMS 435. Electromagnetic systems.

PMS 485. Maritime surveillance systems.

Program Executive Office, Command, Control, Communications, Computers, and Intelligence (PEO C4I). Delivers fleet Command, Control, Communications, Computers, and Intelligence (C4I) capabilities.

PMW 120. Battlespace awareness and information operations.

PMW 130. Information Assurance (IA) and cybersecurity programs.

PMW 150. Navy command-and-control systems.

PMW 160. Tactical networks.

PMW 170. Communications and Global Positioning System (GPS) navigation.

PMW 740. International C4I integration.

PMW 750. Carrier strike and air integration.

PMW 760. Ship integration.

PMW 770. Undersea integration.

PMW 790. Shore and expeditionary integration.

PMW series focus. Two PMW series within PEO C4I have distinct roles:

PMW 1XX. Major capability development portfolios (new platforms and end-to-end networks) where PEO C4I owns the baseline capabilities document, acquisition strategy, and milestone execution; Warfare Centers supply lead systems integration, test ranges, and engineering agents via tailored project orders [SECNAV5400-15D, edo-2-1-4-warfare-centers-2024].

PMW 7XX. Fleet integration portfolios synchronizing new capabilities into existing hulls, aircraft, and shore nodes; emphasizes installation planning, logistics, and interoperability packages coordinated through regional Warfare Centers and type commanders [SECNAV5400-15D, edo-3-1-5-field-activity-fm-2025].

Program Executive Office, Digital and Enterprise Services (PEO Digital). Provides enterprise digital services (e.g., Flank Speed collaboration environment).

Program Executive Office, Manpower, Logistics and Business IT (PEO MLB). Modernizes manpower, logistics, and business information-technology systems.

1.6.1 PEO/Warfare Center Interaction Model

Role Designation. PEOs charter Warfare Centers as EAs (ISEA, DA, SIA) via technical direction letters aligned with [SECNAV5400-15D]; the Warfare Center executes under Navy Working Capital Fund (NWCF) funding while reporting performance to the PM [edo-2-1-4-warfare-centers-2024].

Requirements Translation. PM Integrated Product Teams (IPTs) decompose Capabilities Development Documents (CDDs) into technical requirements that Warfare Center TA holders validate and flow down through alteration packages, interface control documents, and test plans [edo-2-1-4-warfare-centers-2024].

Funding Mechanisms. PEO PMOs issue project orders or Economy Act orders using their appropriations; Warfare Centers accept into NWCF, schedule Work Breakdown Structures (WBSes), and recover rates through Stabilized Labor Rates (SLRs) while keeping the PM apprised of burn rates and Net Operating Result (NOR) impacts [edo-3-1-5-field-activity-fm-2025].

Governance Rhythm. Monthly technical reviews focus on requirements churn, test results, and configuration control; quarterly business reviews reconcile execution to SLR assumptions and assess workforce mix, drawing on Warfare Center cost visibility [SECNAV5400-15D, edo-3-1-5-field-activity-fm-2025].

Acquisition Decision Events. Warfare Centers provide independent readiness assessments (test status, technical risk) for PEO milestone decisions, often serving as certifying authorities for safety releases or flight clearances prior to fielding [SECNAV5400-15D, edo-2-1-4-warfare-centers-2024].

2 PPBE

2.1 PPBE (Planning, Programming, Budgeting, and Execution)

Refs:

2.1.1 What PPBE does

Aligns strategy to resources across the Future Years Defense Program (FYDP). *Planning* (strategy → guidance), *Programming* (balanced force/program → Program Objective Memorandum (POM)), *Budgeting* (validated request → President's Budget (PB)), *Execution* (obligations/outlays → performance feedback) [edo-3-1-1-ppbe-2025].

2.1.2 Timeline (annual rhythm)

Figure 2.1 shows the Planning, Programming, Budgeting and Execution (PPBE) timeline across multiple fiscal years with key milestones during each calendar year.

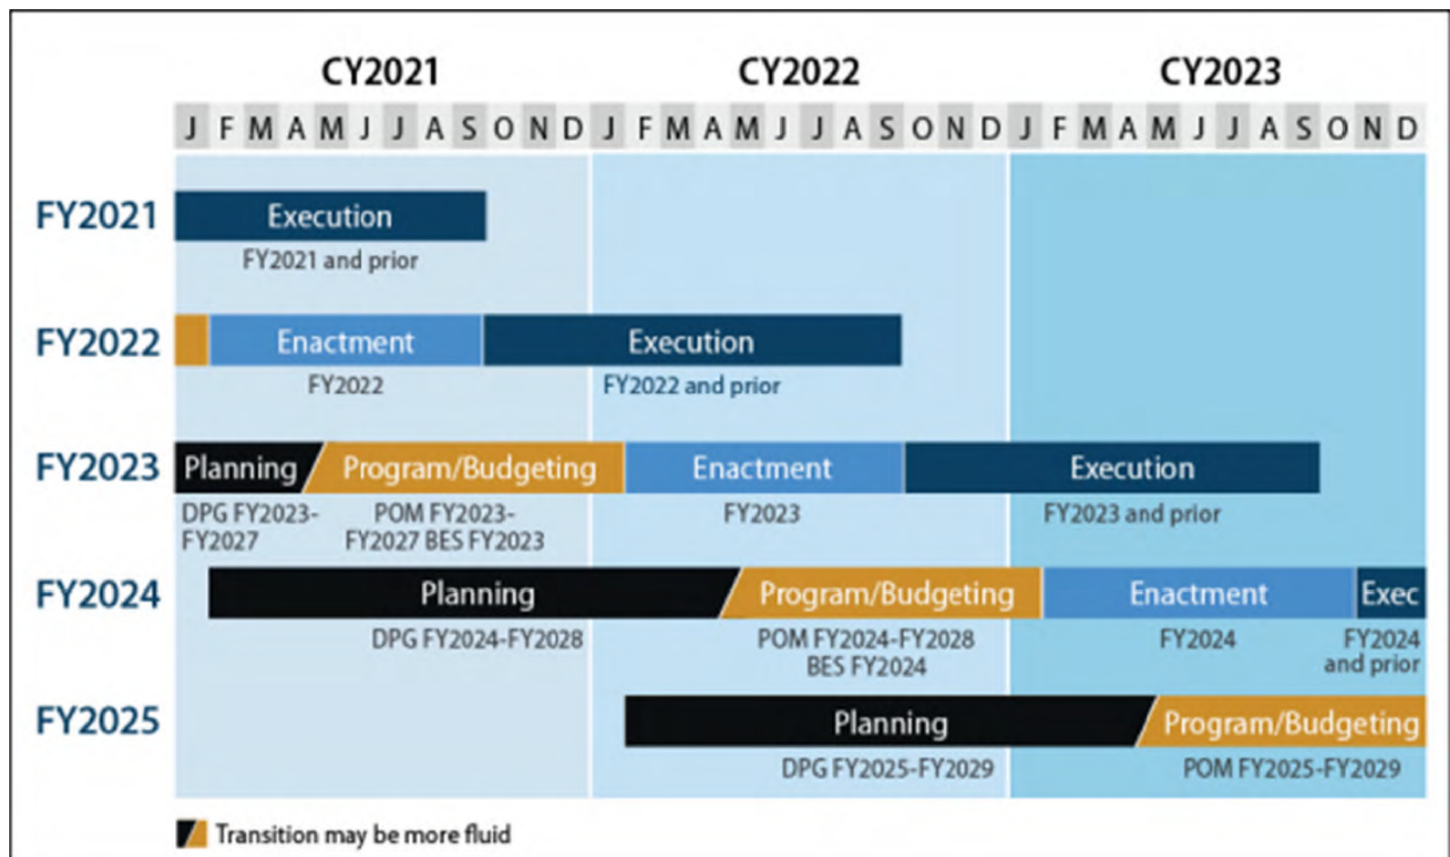


Figure 2.1. PPBE Timeline for multiple fiscal years. Source: edo-3-1-1-ppbe-2025, edo-3-1-1-ppbe-2025 [edo-3-1-1-ppbe-2025].

2.1.3 Congressional Enactment (Regular Order)

Figure 2.2 highlights how Congress moves from the PB submission through authorization and appropriations when operating on-time without a Continuing Resolution (CR). Being able to walk this chart helps bridge PPBE milestones with Hill activity.

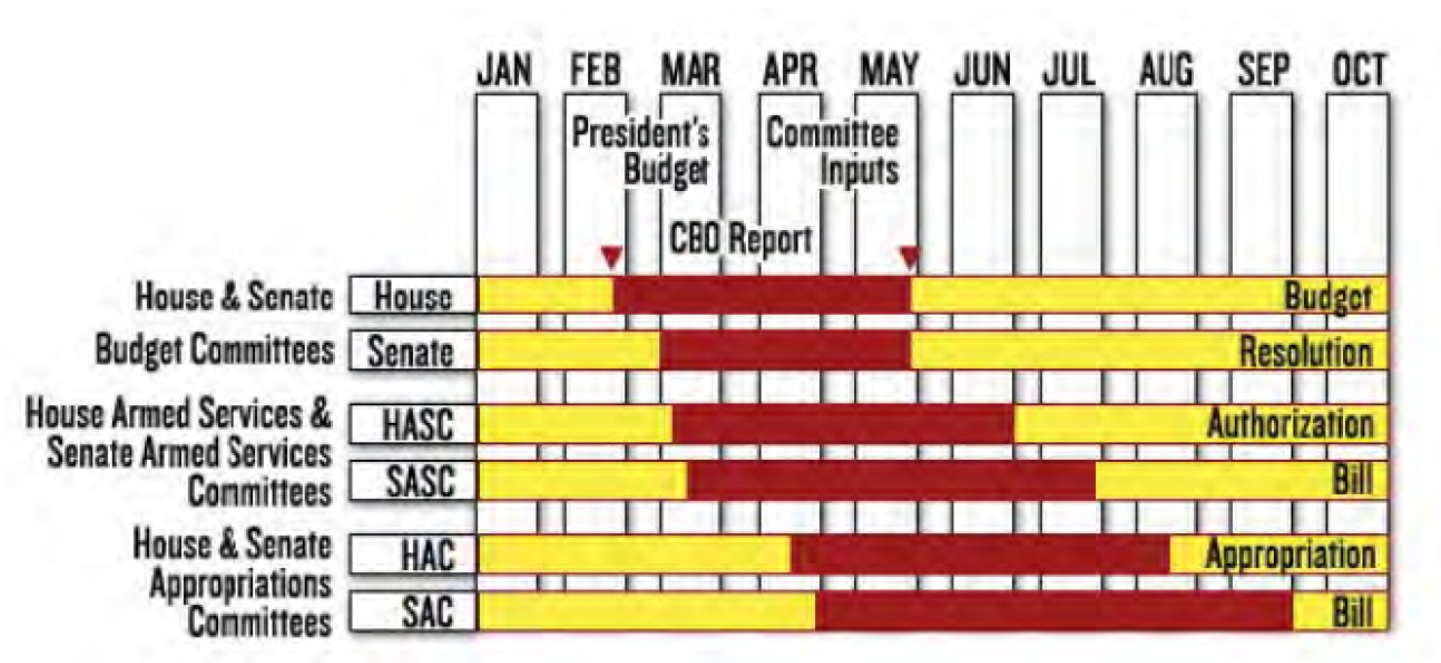


Figure 2.2. Congressional Enactment Timeline. Source: edo-3-1-2-congressional-enactment-2025, edo-3-1-2-congressional-enactment-2025 [edo-3-1-

2.1.4 Key Terms and Definitions

Table 2.1 lists key terms and definitions.

TABLE 2.1: KEY TERMS IN PPBE	
TERM	ONE-LINER
PY	Last completed FY: execution look-back and CR baselines.
CY	Ongoing FY: execution and mid-year reviews.
BY	Next FY in submission.
POM	Service’s balanced force/program across the FYDP.
FYDP	5-year program structure and resources.

Source: DoDFMR-Vol3, DoDFMR-Vol3 [DoDFMR-Vol3]

Other terms and definitions from [edo-3-1-1-ppbe-2025].

- Cost Assessment and Program Evaluation (CAPE).** Provides independent cost assessment and program evaluation.
- Program Decision Memorandum (PDM).** Records SECDEF program decisions at the end of Program Review.
- OPNAV Integration of Capabilities and Resources (N8).** Builds the Navy POM; trades across portfolios with cost/risk realism.
- OPNAV Warfare Systems (N9).** Validates/advocates warfare requirements; integrates by mission area.

Warfare Integration Directorate (N91). Manages cross-domain mission integration and architecture; orchestrates POM issue papers and mission engineering. *Office designators can shift; verify current subcodes week-of.*

2.1.5 Programming v.s. Budgeting

Table 2.2 compares key differences between Programming and Budgeting. One way to think about this: (1) Budgeting is for the money for this year and (2) Programming is for the 5-year FYDP.

TABLE 2.2: PROGRAMMING V.S. BUDGETING

	PROGRAMMING	BUDGETING
Purpose	Build a balanced force across FYDP	Price/validate an executable BY request
Lead	N8 with supporting codes/PEOs/SYSCOMs	FMB/Office of the Secretary of War (Comptroller)/Office of Management and Budget
Key products	POM, PDM	Budget estimate, reclama, President’s Budget

Source: edo-3-1-1-ppbe-2025, edo-3-1-1-ppbe-2025 [edo-3-1-1-ppbe-2025]

2.1.6 PPBE Programming

3-Star v.s. 4-Star Reviews: During Office of the Secretary of War (OSD)’s Program Review, issues raised on the Services’ POMs move first to a 3-Star Programmers Panel (staff-level, chaired by Director, CAPE (DCAPE)) that vets issue papers, builds options (with offsets), and forwards recommendations. Unresolved or strategy-level trades go to the 4-Star forum, the Deputy’s Management Action Group (DMAG) co-led by the Deputy SECDEF (with the Vice-Chairman of the Joint Chiefs of Staff (VCJCS)), for senior adjudication. Decisions at this stage are documented as a PDM or (in recent cycles) a programmatic Resource Management Decision (RMD), which updates the FYDP and hands off to the Comptroller’s Budget Review that culminates in budgetary RMDs.

2.1.7 Appropriations Life-cycle (Colors of Money)

Figure 2.3 visualizes when each major appropriation category is Current, Expired, or Cancelled. Pair this with the obligation windows discussion so you can sketch the chart quickly at the board.

YEARS											
Appropriation Categories	1	2	3	4	5	6	7	8	9	10	11
O&M											
RDT&E											
Procurement											
Ships											
MILCON											
MILPERS											

LEGEND		
Current		Available for new obligations, obligation adjustments, expenditures, and outlays.
Expired		Available for obligation adjustments, expenditures, and outlays.
Cancelled		Unavailable for obligations, obligation adjustments, expenditures, and outlays.

Figure 2.3. Colors of Money Timeline. Source: edo-3-1-3-program-funding-2025, edo-3-1-3-program-funding-2025 [edo-3-1-3-program-funding-2025]

2.1.8 IGT (Intragovernmental Transactions)

Definition. Orders and collections between federal entities using Treasury’s G-Invoicing: 7600A (order), 7600B (agreement/performance), Intra-Governmental Payment and Collection (IPAC) for collections [Treasury-GInvoicing].

Why it matters. Intragovernmental Transaction (IGT) acceptance *is an obligation* on the customer side and the *revenue recognition driver* for the performing Working Capital Fund (WCF) activity.

2.1.9 Common Ordering Instruments

Work Order. Internal directive used within a command to control scope/cost/schedule.

Project Order. Statutory order for a *definite, specific, and entire* project; obligatory on acceptance; performs like a contract between DoW activities. (41 U.S.C. § 6307) [USC-6307-ProjectOrder]

Military Interdepartmental Purchase Request (MIPR)/IPR (DD Form 448). Economy Act order between federal entities; obligatory when accepted; performed by the servicing agency. (31 U.S.C. § 1535) [USC-1535-EconomyAct, Treasury-GInvoicing]

2.1.10 Fiscal Law (Know These Cold)

Purpose Statute (“Misappropriation”). Funds must be used only for their appropriated purpose (31 U.S.C. § 1301(a)) [USC-1301-Purpose].

Bona Fide Needs Rule. Use current-year appropriations only for legitimate needs of that fiscal year (31 U.S.C. § 1502(a)) [USC-1502-BFN].

Anti-Deficiency Act. Do not obligate/expend in excess of available amounts or before funds are available (31 U.S.C. § 1341, § 1517) [USC-1341-ADA].

2.1.11 Reprogramming: Moving Resources After Enactment

Four mechanisms (high level).

1. **Congressional Prior Approval Reprogramming (PA Reprog):** Actions above statutory/committee thresholds or affecting congressional special-interest items or new starts. Requires approval from all four defense committees; timing driven by committee cycles [DoDFMR-Vol3].
2. **Internal Reprogramming (IR):** Realignment within an appropriation that do not cross thresholds or trigger congressional interest; used for proper purpose alignment without changing totals. Notice sent to committees [DoDFMR-Vol3].
3. **Below-Threshold Reprogramming (BTR):** Component-level authority to move funds below set dollar/percent limits within the same appropriation/fiscal year; limits reset annually by appropriations acts/committee guidance [DoDFMR-Vol3].
4. **Letter Transfer (LT):** Treasury non-expenditure transfer moving budgetary resources between appropriations/treasury symbols when authorized (e.g., statute or enacted language) [DoDFMR-Vol3].

Hint

General rules of thumb—cannot change color-of-money or extend time; must complete before funds' obligation period ends; expired-year accounts limited to valid upward/downward adjustments only [DoDFMR-Vol3].

2.1.12 From Enactment to Field Authority

1. Treasury *warrants* the appropriation; Office of Management and Budget (OMB) *apportions* on Standard Form 132.
2. OSD (Comptroller) issues allocations to components such as the DON.
3. OPNAV (Financial Management Budget (OPNAV) (FMB) / OPNAV Programming Division (N82)) allocates to SYSCOM BSOs (Echelon II), which suballocate to Warfare Centers (Echelon III), followed by *allowances/allotments* to the Enterprise Resource Planning (ERP) system [DoDFMR-Vol3].
4. Commands record commitments, obligations, and expenses, and request outlays via Defense Finance and Accounting Service (DFAS).

2.2 NWCF Essentials: Rates, Results, and Execution

Refs:

2.2.1 Key Definitions (Execution)

Commitment. Administrative reservation of funds in anticipation of an obligation; reduces available authority but is not yet a legal liability [DoDFMR-Vol3] (e.g., National Reconnaissance Office (NRO)’s Request for Contract Action (RCA) process).

Obligation. Legal liability incurred that encumbers funds [DoDFMR-Vol3] (e.g., award of a contract, acceptance of an IGT order).

Expenditure/Expense. Recording of cost when goods/services are received/accepted (accrual basis) [DoDFMR-Vol3] (e.g., sending check to pay an invoice).

Outlay/Disbursement. Treasury cash payment to a vendor or performing activity [DoDFMR-Vol3] (e.g., payment check is cashed in).

2.2.2 Flow: PMO Purchase Request to Treasury Payment

1. PMO *commits* funds (approved in the ERP system).
2. Contract award or IGT order acceptance creates the *obligation* [DoDFMR-Vol3, Treasury-GInvoicing].
3. Performance/acceptance posts *expense* (accrual).
4. DFAS schedules the invoice for payment; Treasury disburses (*outlay*) via IPAC (for IGT) or commercial EFT [Treasury-GInvoicing].

2.2.3 NWCF Metrics and Equations

NOR (annual profit/loss).

$$\text{NOR} = \text{Revenue} - \text{Total Expenses}$$

Target performance remains near break-even over time (small NOR) [DoDFMR-Vol3].

Accumulated Operating Result (AOR) (retained earnings/equity over time).

$$\text{AOR}_t = \text{AOR}_{t-1} + \text{NOR}_t \pm \text{Other Adjustments}$$

Represents the *corpus* (net position) of the fund [DoDFMR-Vol3].

2.2.4 NWCF Corpus v.s. Appropriations

AOR (working capital). Revolving cash and retained earnings authorized under 10 U.S.C. § 2208 [USC-2208-NWCF]; remains available without fiscal year limitation to finance operations until recovered through stabilized rates [DoDFMR-Vol3-Ch19].

Customer Appropriations. Mission-funded (e.g., Operation and Maintenance, Navy (OMN), Research, Development, Test, and Evaluation (RDT&E), Shipbuilding and Conversion, Navy (SCN)) dollars obligated by the customer when a

project order or inter/intra-governmental order is accepted; purpose, time, and amount statutes still apply to the customer [DoDFMR-Vol3].

Capital Investment Program (CIP). Financed by NWCF corpus but budgeted in the capital budget exhibit; used for plant/equipment modernization and amortized back through rates, not through a separate appropriation [DoDFMR-Vol3-Ch19].

No Augmentation. NWCF activities cannot augment customer appropriations; corpus only bridges cash timing between expense recognition and reimbursement [DoDFMR-Vol3-Ch19].

2.2.5 Stabilized Rates and SLR

Stabilized Rates. Customer prices set in the budget build to recover expected full costs (labor, material, overhead, depreciation/C CIP) with a near-zero NOR goal [DoDFMR-Vol3].

SLR. Published labor \$/hr for a shop/code; recovers direct labor + fringe + overhead + G&A + capital depreciation recovery [DoDFMR-Vol3]. The rate is:

$$\text{SLR} = \frac{\text{Direct Labor} + \text{Fringe} + \text{OH} + \text{G\&A} + \text{Depreciation Recovery}}{\text{Direct Labor Hours}}$$

Adjustment Battle Rhythm. Rates are established two years ahead during the PPBE budget build and held constant throughout budget year execution; mid-year changes require Office of the Under Secretary of War (Comptroller) (OUSW(C)) approval when earned rates diverge materially from planned costs, and Navy BSOs typically review SLR accuracy monthly/quarterly to recommend any out-of-cycle adjustments [DoDFMR-Vol3-Ch19].

2.2.6 NWCF v.s. Mission-Funded (Appropriation) Commands

Which billets at NWCF are mission-funded. Military administration and leadership billets (CO/XO/Admin) are funded by **Military Personnel (MILPERS)** and treated as mission-funded within NWCF; certain command/HQ oversight billets may also be OMN funded by policy, so verify locally. These costs are not recovered in stabilized rates. Others that are assigned to NWCF will bill hours towards work and the NWCF will reimburse MILPERS [DoDFMR-Vol3].

2.2.7 Standing Up or Modifying a NWCF Business Area

1. **Business Case Development:** Sponsor (e.g., ASN(RD&A) or SYSCOM) prepares analytical justification showing workload, demand signal, and ability to operate on a revolving basis without violating purpose/-time/amount [DoDFMR-Vol3-Ch19].
2. **DON Approval Chain:** Secretary of the Navy (SECNAV) (delegated to ASN (FM&C)) endorses the concept and forwards to OUSW(C) while coordinating with Navy Comptroller to align PPBE exhibits [DoDFMR-Vol3-Ch19].
3. **OUSW(C)/OMB Review:** DoW Chief Financial Officer (CFO) validates cash requirements, rate methodology, and capital plan, then seeks OMB alignment for the PB [DoDFMR-Vol3-Ch19].

4. **Congressional Notification:** Congress must be notified (and, when required, explicitly authorize in appropriations or authorizations) before execution; 10 U.S.C. § 2208 [**USC-2208-NWCF**] restricts creation of new WCFs without legislative awareness [**DoDFMR-Vol3-Ch19**].
5. **Implementation:** Once approved, the new business area is issued an NWCF business unit code, begins PPBE rate build two years out, and transitions legacy appropriated accounts via opening balance adjustments [**DoDFMR-Vol3-Ch19**].

2.2.8 NWCF Cycle of Operations (Order to Cash)

1. **Customer order.** IGT 7600A or project order is received and *accepted*, creating the customer's obligation.
2. **Work in process.** Labor and material are applied; costs accumulate; billing events are scheduled per percent complete or delivery.
3. **Revenue recognition and billing.** The NWCF recognizes revenue and bills via IPAC (IGT) or a commercial invoice if authorized.
4. **Collection (cash).** Treasury IPAC/electronic funds transfer posts; NWCF cash increases; NOR/AOR update through the period close [**DoDFMR-Vol3, Treasury-GInvoicing**].

2.2.9 Operating During a Continuing Resolution

Customer Funding Limits. Appropriated customers remain bound by prior-year obligation rates and anti-deficiency constraints; NWCF orders cannot exceed apportioned CR amounts until an appropriations act is passed [**CRS-CR**].

Cash Cushion. Existing NWCF corpus allows Warfare Centers to keep executing accepted orders (labor continues, suppliers paid) even if reimbursements lag, provided cash balances stay within the FMR's upper/lower operating limits [**DoDFMR-Vol3-Ch19**].

No New Starts. CR guidance prohibits new start projects, major capital investments, or rate changes absent explicit exception; NWCF managers defer new workloads that would obligate customer funds beyond CR allowances [**CRS-CR**].

Rate Discipline. Stabilized rates remain frozen; only emergency OUSW(C)-approved rate adjustments may occur, so BSOs focus on expense control to avoid large NOR swings during the CR period [**DoDFMR-Vol3-Ch19**].

2.2.10 Why Use a Warfare Center (Organic)

Things PMOs/industry can't do. Inherently governmental TA warrants, certification authority, certain safety releases; highly classified or nuclear workspaces.

Things they shouldn't do. Independent test/assessment, spec adjudication, tech baseline control, blue-&-gold separation to avoid Organizational Conflict of Interest (OCI).

Things they won't do. Sustainment engineering at scale, depot-level organic repair, fleet distance support.

2.3 Congressional Enactment

Refs:

2.3.1 Foundations and core definitions

Power of the purse. U.S. Constitution, Article I.

Section 8.

“The Congress shall have power to... provide for the Common Defense... and general welfare...”

Section 9.

“No money shall be drawn from Treasury, but in consequence of Appropriations made by law...”

Key terms. Budget Authority (BA) (legal authority to incur obligations), Total Obligational Authority (TOA), obligations, outlays, Legislative Proposal (LEGPROP).

Authorization v.s. Appropriation. National Defense Authorization Act (NDAA) authorizes programs/policy; appropriations provide BA.

2.3.2 Who drafts what

Authorization. House Armed Services Committee (HASC) /Senate Armed Services Committee (SASC).

Appropriations. House Appropriations Committee (HAC) /Senate Appropriations Committee (SAC).

Budget Resolution. House Budget Committee (HBC) /Senate Budget Committee (SBC) (sets topline aggregates and 302 allocations; not a law).

Independent analysis/oversight. Congressional Budget Office (CBO) (scoring), Congressional Research Service (CRS) (research), Government Accountability Office (GAO) (audits/oversight).

2.3.3 Regular-order timeline

Figure 2.4 shows the timeline from the PB → Appropriation Bill with approximate timelines assuming no CR.

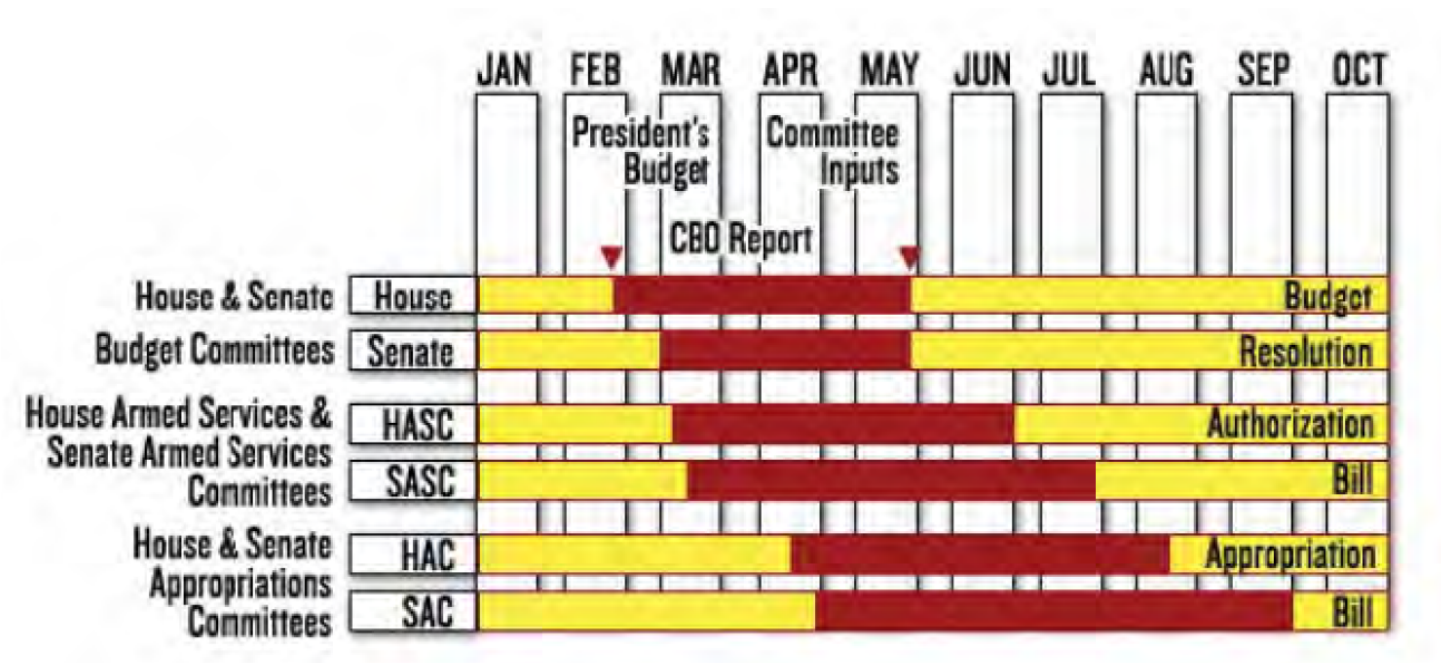


Figure 2.4. Congressional Enactment Timeline. Source: edo-3-1-2-congressional-enactment-2025, edo-3-1-2-congressional-enactment-2025 [edo-3-1-

2.3.4 The 12 regular appropriations bills

- Defense.** Department of War appropriations.
- Military Construction and Veterans Affairs.** Military construction, housing, and Department of Veterans Affairs programs.
- Energy and Water.** Department of Energy, Army Corps of Engineers, and related infrastructure programs.
- Homeland Security.** Department of Homeland Security operations and components.
- Interior and Environment.** Department of the Interior and Environmental Protection Agency activities.
- Labor, Health and Human Services, Education.** Departments of Labor, Health and Human Services, and Education, plus related agencies.
- Legislative Branch.** U.S. Congress and supporting legislative branch agencies.
- Financial Services and General Government.** Treasury, judiciary, Small Business Administration, and other independent agencies.
- Transportation and Housing and Urban Development.** Departments of Transportation and Housing and Urban Development.
- Commerce, Justice, Science.** Departments of Commerce and Justice plus science agencies such as NASA and the National Science Foundation.

State and Foreign Operations. Department of State, U.S. Agency for International Development, and foreign assistance programs.

Agriculture and Food and Drug Administration (FDA). Department of Agriculture and Food and Drug Administration activities.

Note

The bills that EDO's care about the most are Defense, Military Construction (MILCON) & Department of Veterans Affairs (VA) and Energy & Water. This because those bills directly affect funding for our acquisitions.

Hint

These bills are sometimes packaged into minibuses or a single omnibus appropriations act.

2.3.5 Continuing Resolution

Continuing resolution rules (board one-liner). *No new starts*; rate/quantity changes generally constrained unless specified; execution limited by OMB apportionment, CR anomalies, and any authorities Congress adds in the joint explanatory statement [CRS-CR].

2.3.6 Sequestration

Automatic, across-the-board reductions if statutory caps/triggers are breached; applied by account unless modified by law.

2.4 Program Funding and Execution

Refs:

2.4.1 BA, commitment, obligation, expenditure, outlay

1. *BA* available (legal authority).
2. *Commitment* (administrative reservation).
3. *Obligation* (legal liability via contract/order).
4. *Expenditure* (payment recorded).
5. *Outlay* (cash disbursed/Treasury).

Source references [DoDFMR-Vol3, Treasury-GInvoicing].

2.4.2 Appropriation categories, scope, obligation windows

Table 2.3 shows the Colors of Money with their spending categories and obligation windows. Figure 2.3 from § 2.1.7 visually shows when each category is Current, Expired, or Cancelled.

TABLE 2.3: APPROPRIATION CATEGORIES, SCOPE, OBLIGATION WINDOWS

CATEGORY	TYPICAL SCOPE	OBLIGATION WINDOW
RDT&E	Science & technology; development; test & evaluation	2 years
OPN ^a	End items/modernization and spares	3 years
OMN	Operations, maintenance, training, minor mods	1 year
MILCON	Facilities construction and real property	5 years
MILPERS	Personnel pay	1 year

^a SCN is a specific procurement with a 5-year obligation window.

Source: DoDFMR-Vol3, DoDFMR-Vol3 [DoDFMR-Vol3]

2.4.3 Funding policies

Annual OMN/MILPERS. Fund only bona fide needs of the fiscal year.

RDT&E. Fund work as it occurs by fiscal year.

Full-funding. (Procurement/MILCON). Fund the total usable end-item at award.¹

Common techniques/exceptions: Advance Procurement (long-lead items), Multiyear Procurement, Economic Order Quantity, Cost-to-Complete when provided in law.

Exceptions to the Full Funding Policy

Below is the list of the key exceptions to the Full Funding Policy, what they allow, and the must-know rules/approvals (Table 2.4 shows full details).

¹ Exceptions to Full funding are select SCN programs (CVNs, SSBNs, and LHD/LHAs) with Congressional approval.

TABLE 2.4: KEY EXCEPTIONS TO THE FULL FUNDING POLICY: WHAT THEY ALLOW AND WHAT TO REMEMBER

EXCEPTION	TYPICAL APPROPRIATION	WHAT IT ALLOWS	MUST-KNOW RULES / APPROVALS
MYP	APN, OPN, SCN	Single contract covering multiple fiscal years of buys to achieve predictable demand and unit-cost savings; may include EOQ purchases common across years.	Requires specific congressional authorization; stable requirements/design; credible savings; low technical risk; term generally up to 5 years; plan/budget any cancellation liability.
Advance Procurement (incl. LLTM/EOQ)	APN, OPN, SCN	Limited <i>early</i> funding (often 1–2 years before the main “buy” year) for long-lead components or EOQ lots to protect schedule or achieve price breaks.	Narrow and part-specific; must be justified in budget docs; EOQ commonly tied to MYP (or explicit block authority); does <i>not</i> equal full funding of the end item.
BB	Primarily SCN	A single contract buying multiple ships (or end items) across fiscal years to gain tooling/learning-curve efficiencies.	Requires explicit congressional authorization; funds still obligated year-by-year; not under the MYP statute, so oversight mechanics differ.
CTC	SCN	Additional funds in a later FY to finish an item (e.g., ship) when matured estimates exceed prior appropriations.	Completes original approved scope (not added capability); appears as a distinct request/justification; common in long-duration shipbuilding.
RCOH for CVN	SCN (with prior Advance Procurement)	Mid-life refueling and major overhaul funded incrementally over multiple years; early procurement of nuclear fuel/critical components.	Recognized exception due to size/complexity; incremental SCN with advance procurement years ahead of the principal execution.

Note:

- (i) Economic Order Quantity (EOQ) purchases are commonly approved within Multiyear Procurement (MYP) or other explicit multi-year constructs;
- (ii) Block Buy resembles MYP in intent (savings) but uses program-specific authorization;
- (iii) Plan for cancellation liability under MYP when required.

Source: USC-3501, DFARS217-172, DoDFMR-Vol3, USC-3501, DFARS217-172, DoDFMR-Vol3 [USC-3501, DFARS217-172, DoDFMR-Vol3]

2.4.4 Navy Sustainment Funding: TYCOM v.s. Fleet (O&S)

Who holds O&M,N. Type Commanders (*TYCOMs*; e.g., COMNAVSURFOR, COMNAVAIRFOR, COMSUBFOR) are the primary executors of OMN for unit readiness: flying hours, steaming days, intermediate-level maintenance, training, and afloat/ashore support.

Fleet Commanders. PACFLT and USFF set operational priorities and readiness goals, adjudicate contingencies, and may centrally manage certain Fleet-wide initiatives; they influence TYCOM allocations but most execution occurs at the TYCOM.

Program Office (SYSCOM/PEO). Funds in-service engineering, tech data, Diminishing Manufacturing Sources, and modernization using Other Procurement, Navy (OPN)/Aircraft Procurement, Navy (APN) (end items/kits) and RDT&E/OMN

(installation, trials) as appropriate; manages sustainment Indefinite-Delivery, Indefinite-Quantities (IDIQs)/PBL with color-of-money compliance.

Who pays what. OPN/APN: hardware/software upgrade kits, initial spares; OMN: installs, fleet introduction/training, minor mods, repair parts consumption; RDT&E: development/test of engineering changes. NAVSUP/NWCF activities recover costs via rates for supply/repair.

Board cue. In O&S, TYCOMs execute most OMN; Program Managers fund modernization and in-service support from OPN/APN/RDT&E. Align funding lines with the WBS and the Colors-of-Money rules to avoid Anti-Deficiency Act risk.

Quick information regarding exceptions to the full funding policy:

MYP. Up to 5 years; stable design; verifiable savings; cancellation liability planned.

Advance Procurement Long-Lead Time Material (LLTM)/EOQ. Focused early buys for schedule/savings; not full funding.

Block Buy (BB). Congressionally authorized multi-ship buys; obligate by Fiscal Year (FY); not the MYP statute.

Cost-to-Complete (CTC). Complete original scope when estimates mature upward; separate SCN request.

Refueling and Complex Overhaul (RCOH). Planned mid-life overhaul; incremental SCN with advance procurement of cores/critical material.

2.4.5 Which money when (by acquisition phase)

Table 2.5 shows the nominal types of appropriation used for Materiel Solution Analysis (MSA), Technology Maturation and Risk Reduction (TMRR), Engineering and Manufacturing Development (EMD), Production and Deployment Phase (P&D), and Operations and Support Phase (O&S)

TABLE 2.5: APPROPRIATION TYPES PER PHASE

PHASE	TYPICAL APPROPRIATION(S)
MSA	RDT&E (analyses, prototyping); small OMN for studies
TMRR	RDT&E (risk reduction, development, test)
EMD	RDT&E (develop/build/test/qualify); selected long-lead/AP/EOQ in Procurement when authorized
PD	Procurement (e.g., OPN); limited RDT&E for fixes
OS	OMN sustainment; spares via Procurement as applicable

2.4.6 MILCON v.s. O&M sustainment v.s. OPN modernization

Rule of thumb: Real property construction ⇒ MILCON; keeping systems running (repair/overhaul, services) ⇒ OMN; new capability/end-item upgrades ⇒ Procurement (e.g., OPN).

2.4.7 Field Activity Financial Management (NWCF quick hits)

- Goal.** NWCF activities price to *break even over time*; in-year result is **NOR**, cumulative is **AOR**.
- SLR.** Recover direct labor + overhead + G&A; shocks flow to NOR/AOR and are managed over time.
- Carryover.** Unfilled orders at FY end; subject to limits/management.
- IGT via G-Invoicing.** Treasury-mandated platform for intra-gov orders/settlement; apportionment/availability rules still govern customer funds.

2.5 Cost Elements, Estimates, and Learning Curves

Refs:

2.5.1 Direct v.s. Indirect Costs

- Direct.** Traceable to a final cost objective (e.g., technician hours, end-item material).
- Indirect.** Pooled and allocated (overhead, G&A, facilities, depreciation). See the Federal Acquisition Regulation (FAR) cost principles [FAR].

2.5.2 Program Cost Terms (Know the Stack)

- Flyaway Cost.** Recurring production cost of an aircraft/weapon delivered (excludes non-recurring tooling, spares, support).
- Weapon System Cost.** Flyaway plus support equipment, training, data, and initial spares.
- Procurement Cost.** Weapon system cost plus peculiar support and MILCON as applicable.
- Life-Cycle Cost (LCC).** All costs from concept through disposal (RDT&E, procurement, O&S, disposal).
- Total Ownership Cost (TOC).** LCC plus broader infrastructure/indirect enterprise costs.

Note

Use DON/DoW cost handbook definitions; be consistent across documents. [SECNAV5000-2G, DoDI5000-85].

Figure 2.5 shows the LCC from above and how they relate to one another. Note how each cost builds to the next as different types of expenditures are added.

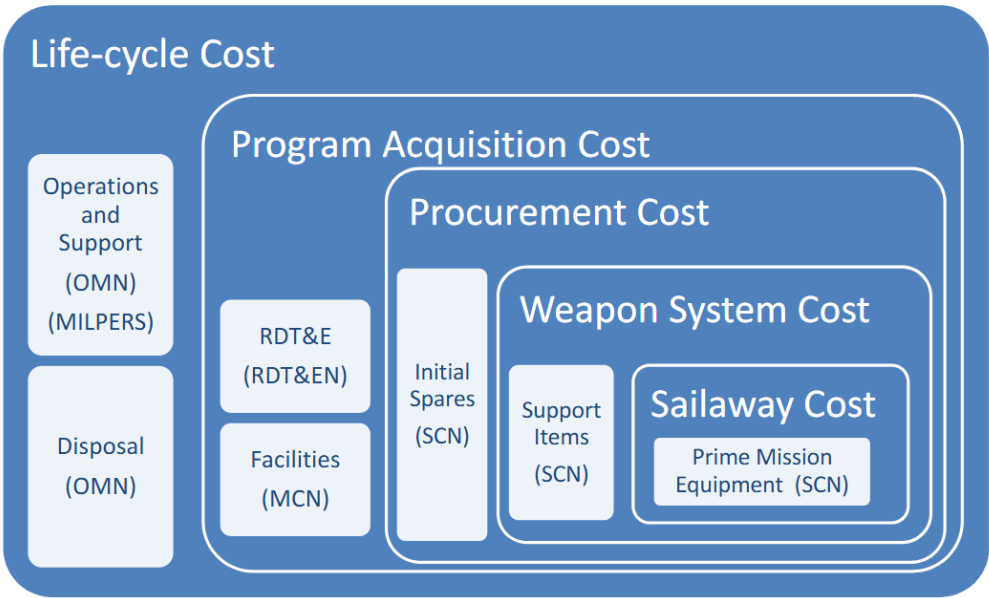


Figure 2.5. Composition of Life Cycle Costs. Source: edo-3-1-6-cost-estimating-2024, edo-3-1-6-cost-estimating-2024 [edo-3-1-6-cost-estimating-2024]

2.5.3 Why the LCCE Matters

Establishes the affordability baseline, informs Acquisition Program Baseline (APB), drives color-of-money phasing, and underpins “will-cost / should-cost” targets [DoDI5000-85]. Figure 2.6 shows the different types of funding that will be used in different phases of the Major Capability Acquisition (MCA). Most of the LCC will be from the O&S phase.

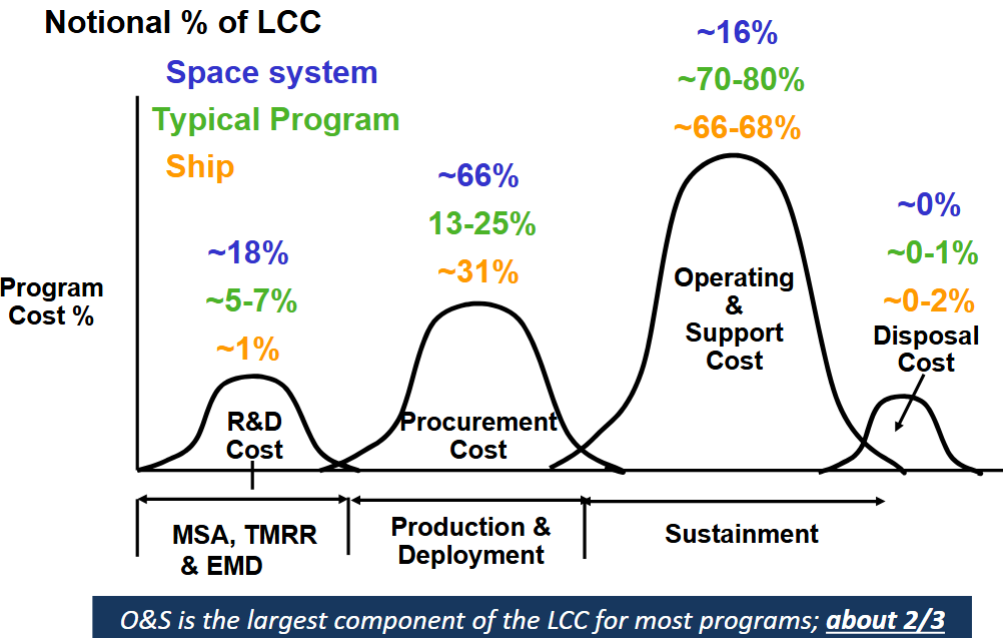


Figure 2.6. LCC over time. The colors of money used are shown for each phase including percent of total costs.
Source: edo-3-1-6-cost-estimating-2024, edo-3-1-6-cost-estimating-2024 [edo-3-1-6-cost-estimating-2024]

2.5.4 Estimating Methods (Types, When, and Why)

Analogy (top-down). *When:* Earliest stages (ICD/Materiel Development Decision (MDD), pre- Analysis of Alternatives (AoA)) when design is immature and only analogous programs or components exist. *Why:* Fast, defensible scoping by scaling from a close comparator using adjustment factors (size, weight, speed, complexity). Good for bounding affordability and informing trades before detailed data exists.

Parametric (CER-based). *When:* AoA through TMRR when historical data supports Cost Estimating Relationships (CERs) (e.g., weight, Source Lines of Codes (SLOCs), thrust, kW). *Why:* Enables rapid sensitivity analysis and trade-space exploration with statistical confidence intervals; supports independent cross-checks and early budget phasing.

Engineering (bottom-up). *When:* EMD and production planning when Bill of Materials (BoMs), routing, labor standards, and quotes are available. *Why:* Most traceable and auditable; ties to technical baseline and schedule networks; supports Integrated Baseline Reviews (IBRs) and negotiation objectives.

Actuals / Extrapolation. *When:* From late TMRR into production when pilots/Low-Rate Initial Production (LRIP) actuals exist and learning effects are visible. *Why:* Highest fidelity; captures learning curves and process improvements; anchors estimates to realized performance and Cost and Software Data (CSDR) actuals [DAU-AAF].

TABLE 2.6:

TYPE	DESCRIPTION	WHEN USED	WHY USED
Analogy	Uses cost of a similar past system, adjusted for differences	Early concept/refinement (Pre-Milestone A/B)	Quick estimate when data limited
Parametric	Uses statistical cost estimating relationships (CERs) like cost vs. weight or power	Milestone B/C; early design	Captures cost drivers using quantifiable parameters
Engineering (Bottom-Up)	Builds from detailed WBS—materials, labor, overhead	Post-CDR, Low-Rate Initial Production	High accuracy for mature designs
Actual Cost / Extrapolation	Uses historical/production actuals (learning curves)	Full-Rate Production / O&S	Most accurate; supports should-cost and sustainment budgeting

2.5.5 Products and Players

Cost Analysis Requirements Description (CARD). Technical/schedule baseline for independent estimates.

Independent Cost Estimate (ICE). Component Acquisition Executive (CAE) or OSD CAPE for Acquisition Category (ACAT) I; Program Office Estimate (POE).

CSDR. Contractor cost & software data reporting for actuals/CERs.

APB/Selected Acquisition Report (SAR)/Defense Acquisition Executive Summary (DAES). Baselines and reporting [DoDI5000-85].

2.5.6 Learning Curve (Production Efficiency)

If unit time/cost follows an $s\%$ slope, doubling quantity reduces unit cost by $s\%$. Typical aerospace slopes: 85–90% early, flattening as processes mature. Plan lots and spares buys accordingly [DAU-AAF].

2.5.7 Cost Escalation (Inflation Indices)

Escalate base-year costs to then-year using approved DoW inflation indices; separate real growth from price growth; align phasing to obligation windows [DoDFMR-Vol3].

2.5.8 Will-Cost / Should-Cost

Will-Cost. Conservative reference estimate used for budgeting and margin planning.

Should-Cost. Management targets that drive efficiencies (e.g., lean events, value engineering, rate negotiations) [DoDI5000-85].

3 Contracting and Solicitation

3.1 Intro to Contracting Fundamentals

Refs:

3.1.1 Why the Navy Uses Contracts

- Contracts create a legally enforceable relationship between the Government and industry partners, defining rights and responsibilities for each party.
- Written terms provide structure for changes via agreed conditions, protecting both the Navy and the Contractor throughout acquisition actions.
- Binding agreements ensure accountability for cost, schedule, and performance outcomes that cannot be achieved through informal arrangements.

3.1.2 Essential Elements of a Binding Contract

Mutual Assent. Requires an offer and acceptance with a meeting of the minds on all material terms such as scope, price, quantity, and delivery.

Consideration. Both sides exchange value (e.g., payment, performance, schedule relief) that courts will evaluate for adequacy in Government contracting.

Capacity. Parties must be legally competent to enter the agreement; lack of capacity (e.g., incapacity, lack of authority) undermines enforceability.

Lawful Purpose. The contract must pursue a legal objective; agreements for unlawful acts are void.

3.1.3 Government Relationship to Contractors

Transactional. Each party enters with distinct incentives (contractor profit versus government outcomes); avoid unauthorized commitments.

Professional. Both teams must understand the contract and collaborate to meet requirements.

Collaborative. Contractors bring technical expertise while programmatic decision-making remains inherently governmental.

Constrained. Interactions are bound by ethics rules, conflicts-of-interest standards, and contract clauses.

3.1.4 FAR System and NAVSEA Overlays

FAR. Government-wide acquisition regulation establishing policy, procedures, and contract clauses [FAR].

Defense Federal Acquisition Regulation Supplement (DFARS). DoW-level supplement tailoring FAR provisions for defense-unique requirements, including competition, source selection, and industrial base policy [DFARS].

Navy Marine Corps Acquisition Regulation Supplement (NMCARS). DON supplement that adds Navy-specific directives such as approval thresholds, peer reviews, and templates [NMCARS].

SUPSHIP Operation Manual (SOM) Chapter 3. NAVSEA guidance for Supervisor of Shipbuilding (SUPSHIP) on contract formation, modification, and surveillance [SOM-Ch3-2023].

NAVSEA Source Selection Guide. Standardizes competitive source selection procedures, roles, and documentation for SYSCOM procurements [NAVSEA-Source-Selection-Guide-2022].

NAVSEA Contracts Handbook. Practical desk reference covering policy interpretations, clause usage, and best practices for NAVSEA contracting professionals [NAVSEA-Contracts-Handbook-2023].

3.1.5 Types of Contracting Officers (Know All Three)

Procuring Contracting Officer (PCO). Leads acquisition planning through award; signs contracts and bilateral modifications on behalf of the Government.

Administrative Contracting Officer (ACO). Oversees post-award administration, surveillance, and contractor performance; typically assigned via Defense Contract Management Agency (DCMA) or NAVSEA field offices.

Termination Contracting Officer (TCO). Manages partial or complete contract terminations, settlement proposals, and equitable adjustments.

All contracting officers must hold a warrant that delineates dollar and authority limits; only a warranted Contracting Officer (KO) can obligate the United States [FAR].

3.1.6 PM and KO Partnership

PM. Accountable to the Milestone Decision Authority (MDA) for cost, schedule, and performance; integrates technical authority, requirements, and budget execution across the lifecycle.

KO. Provides acquisition strategy execution expertise, ensures compliance with statute/regulation, and is responsible for contract integrity and enforceability.

Board Cue. PMs lead program outcomes; KOs safeguard the contracting instrument. Neither can assume the other's authorities, so coordination before solicitations, negotiations, or modifications is mandatory.

3.1.7 Competition in Contracting Act Requirements

Full and Open Competition. Default posture: all responsible sources may compete [USC-3201-CICA, FAR].

Full and Open After Exclusion of Sources. Permits set-asides (e.g., small business, 8(a)) or alternate-source strategies when justified [FAR].

Approval for Other than Full and Open. Requires documented justification and senior approval per Subpart 6.3 [FAR].

Seven Exceptions to Full and Open Competition (Memorize)

1. Only one responsible source will satisfy agency requirements (see [FAR]).
2. Unusual and compelling urgency (see [FAR]).
3. Industrial mobilization; engineering, developmental, or research capability (see [FAR]).
4. International agreement (see [FAR]).
5. Authorized or required by statute (see [FAR]).
6. National security (see [FAR]).
7. Public interest (see [FAR]).

Hint

Be ready to cite an example scenario for each exception and the approval level required.

3.1.8 Responsiveness, Responsibility, and Key Determinations

Responsiveness (sealed bidding). Bid must conform to all material terms of the Invitation for Bids; nonconforming bids are rejected without discussion [FAR].

Responsibility. Prospective contractor must possess adequate resources, schedule compliance, performance record, integrity, and necessary systems to receive award ([FAR]).

3.1.9 J&A v.s. D&F

Justification and Approval (J&A). Documents the rationale for other-than-full-and-open competition, identifies the chosen statutory exception, and records approval by the appropriate official. Must be posted to <https://sam.gov> after award with required redactions [FAR].

Determination and Findings (D&F). Formal determination that specific conditions are satisfied before taking an action (e.g., use of special contract types, multiyear contracting); states the findings that support the determination [FAR].

Note

At the NRO, documents and rational are post on the low and high-side Acquisition Research Center (ARC). We are required to post other-full-and-Open compeition for five days on the ARC to allow opportuniy for other contractors to bid.

3.1.10 Who Signs D&Fs (and When)

General Rule. [FAR] requires the contracting officer to sign D&Fs when the action is within their delegated authority, unless a higher approval level is specified elsewhere in the regulation or delegation memo.

Head Contracting Activity (HCA). [FAR] reserve approval for actions such as issuing a letter contract or awarding a single-award task/delivery IDIQ expected to exceed \$100M; DON HCAs may redelegate no lower than a flag/Senior Executive [NMCARS].

SAE. Multiyear contracting, extraordinary contractual relief, or other actions identified in [FAR] and [DFARS] require a D&F signed by the Service SAE (ASN(RD&A) for the Navy, who is also the DON Senior Procurement Executive) or a specifically delegated official.

Document Content. Every D&F must cite the specific statutory/regulatory authority, describe supporting facts, and state the determination in clear language; expiration dates and any required follow-on reviews must also be included per [FAR] and [NMCARS] guidance.

3.2 Solicitation Preparation

Refs:

3.2.1 Summary

Uniform Contract Format (UCF) scaffolding. Tailor the UCF (Sections A through M) so Section C defines the requirement, Section L tells offerors how to respond, and Section M mirrors evaluation factors and the stated basis of award [FAR, edo-3-2-2-solicitation-prep-2025].

Release readiness. Do not release the Request for Proposal (RFP) until the acquisition plan/strategy is approved, funds are certified, legal review is complete, synopsis rules are satisfied, and the source-selection teams are chartered [FAR, NMCARS, edo-3-2-2-solicitation-prep-2025].

Communication discipline. Request for Informations (RFIs), draft RFPs, industry days, and Q&A all flow through the KO; once released, clarifications must be shared with all offerors through written amendments or controlled exchanges [FAR, edo-3-2-2-solicitation-prep-2025].

3.2.2 Practitioner Steps

1. Finalize the requirement package (spec /Statement of Work (SOW), Contract Data Requirements Lists (CDRLs), Independent Government Cost Estimate (IGCE), market research report) with IPT concurrence and Small Business coordination documentation [FAR, edo-3-2-2-solicitation-prep-2025].
2. Structure Section L instructions: volumes, page limits, submission medium, proposal due date, classification controls, and [FAR] synopsis timing.
3. Align Section M evaluation factors, subfactors, and relative importance statements with the basis of award (Lowest Price Technically Acceptable (LPTA) v.s. trade-off) and rating methodology approved by the Source Selection Authority (SSA), KO, legal, and cost/price community [FAR, NAVSEA-Source-Selection-Guide-2022].
4. Verify pre-release approvals and postings: acquisition plan or strategy, Determination of Acquisition Strategy (as applicable), certified funds, and <https://www.SAM.gov> synopsis [NMCARS, edo-3-2-2-solicitation-prep-2025].
5. Manage amendments and records after release: capture bidder Q&A, issue conformed RFPs, adjust milestones when requirements shift, and file every action in the official contract record [FAR, NAVSEA-Contracts-Handbook-2023].

3.2.3 Checklist

- Acquisition plan/strategy signed; conformed requirements package appended [NMCARS].
- Funding document (Purchase Request (PR), project order, or MIPR) signed and funds certified for the planned obligation [FAR].
- Market research report and Small Business Coordination Record approved [FAR].
- Source Selection Plan endorsed by SSA, legal, and cost/price; nondisclosure/OCI statements executed for SSA, Source Selection Advisory Council (SSAC), Source Selection Evaluation Board (SSEB), and advisors [NAVSEA-Source-Selection-Guide-2022].
- Section L instructions mirror Section M factors, include proposal structure, late proposal policy, and submission portal guidance [FAR].
- <https://www.SAM.gov> synopsis posted (15 days before closing for most supplies/services; 30 days for R&D unless justified) [FAR].
- Amendment template/change log prepared; routing matrix established for expedited approvals [NAVSEA-Contracts-Handbook-2023].

3.2.4 Navy Overlays and Tailoring

NMCARS overlays. Follow [NMCARS] for synopsis exceptions and NAVSEA contracting notices for Contract Requirement Package checklists and release approvals [NMCARS, NAVSEA-Contracts-Handbook-2023].

Technical data. Coordinate with TA on [DFARS] clauses, distribution statements, and CDRL tailoring to protect Navy equities.

Shipbuilding tailoring. For availabilities, modernization, or planning efforts, ensure Section C and the WBS matches the avail sequence and integrates warfare-center technical direction and installation responsibilities [edo-3-2-2-solicitation-prep-2025].

3.2.5 Industry Engagement & Communications

Pre-release. RFIs, sources-sought notices, draft RFPs, and industry days are vetted through the KO; responses shared with all potential offerors to avoid unequal access [FAR].

Post-release. Clarifications and Q&A must be issued as amendments for all offerors; exchanges stay within [FAR] boundaries until competitive range is established [NAVSEA-Contracts-Handbook-2023].

Small business focus. Coordinate with the Small Business Professional and Competition Advocate on set-aside decisions, subcontracting plan reviews, and mitigation of potential limitations on subcontracting [FAR].

3.2.6 Documentation & Approvals to Capture

- Signed Source Selection Plan and SSA/SSAC/SSEB appointment letters with confidentiality and OCI certifications [NAVSEA-Source-Selection-Guide-2022].
- Competition Advocate memoranda where narrowed sources or synopsis deviations are requested [FAR, NMCARS].
- Legal sufficiency memorandum for the conformed solicitation (Sections C, H, L, and M) retained in the contract file [NAVSEA-Contracts-Handbook-2023].
- KO release memorandum noting solicitation number, issue date, amendment log, and proposal due date/-time [edo-3-2-2-solicitation-prep-2025].

3.2.7 Competitive Method Selection: Sealed Bidding v.s. Negotiated Procurement

Sealed bidding (FAR Part 14). Preferred when requirements are well-defined, award will be based on price alone, discussions are not needed, and the Government expects to receive more than one responsive bid. It uses public opening, responsiveness determinations, and fixed-price awards [FAR].

Negotiated procurement (FAR Part 15). Used when the Government needs to evaluate technical approach or past performance, intends to conduct discussions, or when requirements or pricing demand flexibility. Negotiated acquisitions support best-value trade-offs and cost-reimbursement vehicles [FAR].

When to choose. If the team can describe performance in terms of precise specifications with minimal risk and expects no need for exchanges, sealed bidding streamlines award. When innovation, risk, or integration complexity requires subjective evaluation, or when schedule/budget changes are likely, negotiated procurement is mandatory [FAR, NAVSEA-Source-Selection-Guide-2022].

3.2.8 Contract Type Landscape and Risk Allocation

Fixed-price family. Contractor accepts the cost risk; Government locks price once requirements are stable. Includes:

- **Firm-Fixed-Price (FFP):** Used for mature, low-risk requirements, often in Production and Deployment [FAR, DoDI5000-85].
- **Fixed-Price Incentive (Firm Target) (FPIF):** Shares cost variance through a negotiated share ratio; encourages cost control while keeping final price bounded by a ceiling. Used during EMD or LRIP when cost risk remains but production discipline is needed [FAR, DoDI5000-85].
- **Fixed-Price with Economic Price Adjustment (FPEPA):** Adds indexed adjustments for volatile commodities or long-lead items [FAR].
- **Fixed-Price Redetermination (FPR):** Re-prices after defined milestones when initial uncertainty is expected to retire [FAR].


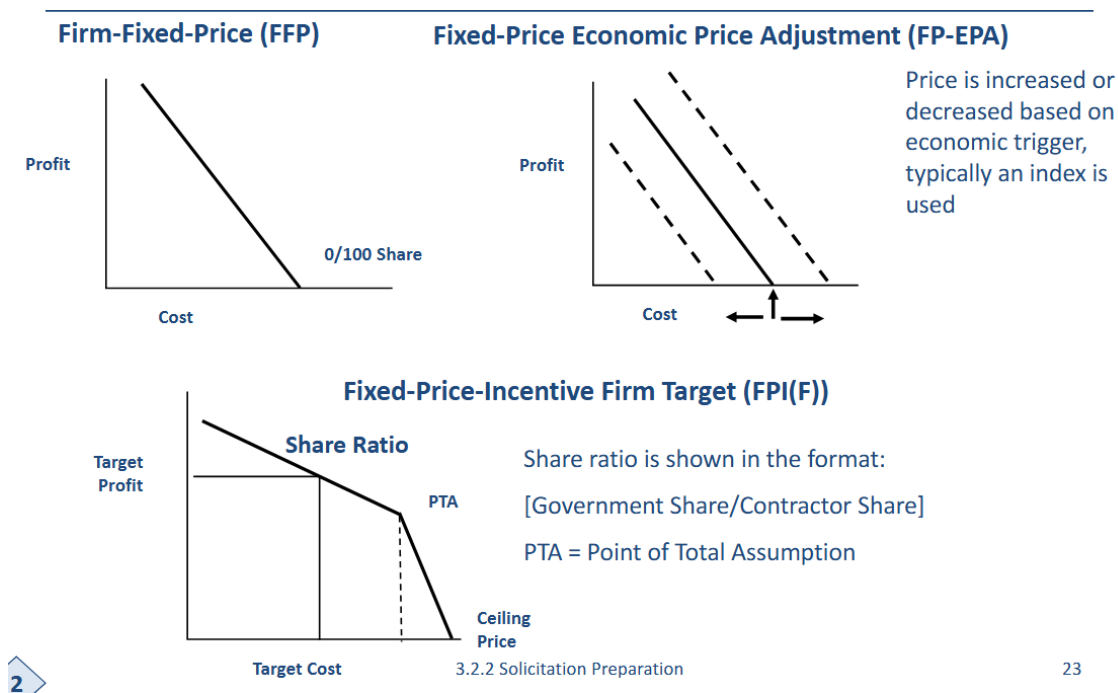


Figure 3.1. Fixed-price incentive geometry (cost, profit, PTA).

Cost-reimbursement family. Government carries more cost risk; contractor must deliver best effort. Includes:

- **Cost-Plus-Fixed-Fee (CPFF)**: Used in early R&D or prototyping (MSA/TMRR) when effort is exploratory [FAR, DoDI5000-85].
- **Cost-Plus-Incentive-Fee (CPIF)**: Shares cost variance similar to FPIF but without a price ceiling; encourages efficiency while acknowledging uncertain cost baseline [FAR].
- **Cost-Plus-Award-Fee (CPAF)**: Adds subjective award-fee evaluation for mission effectiveness or management performance that cannot be captured in objective metrics [FAR].

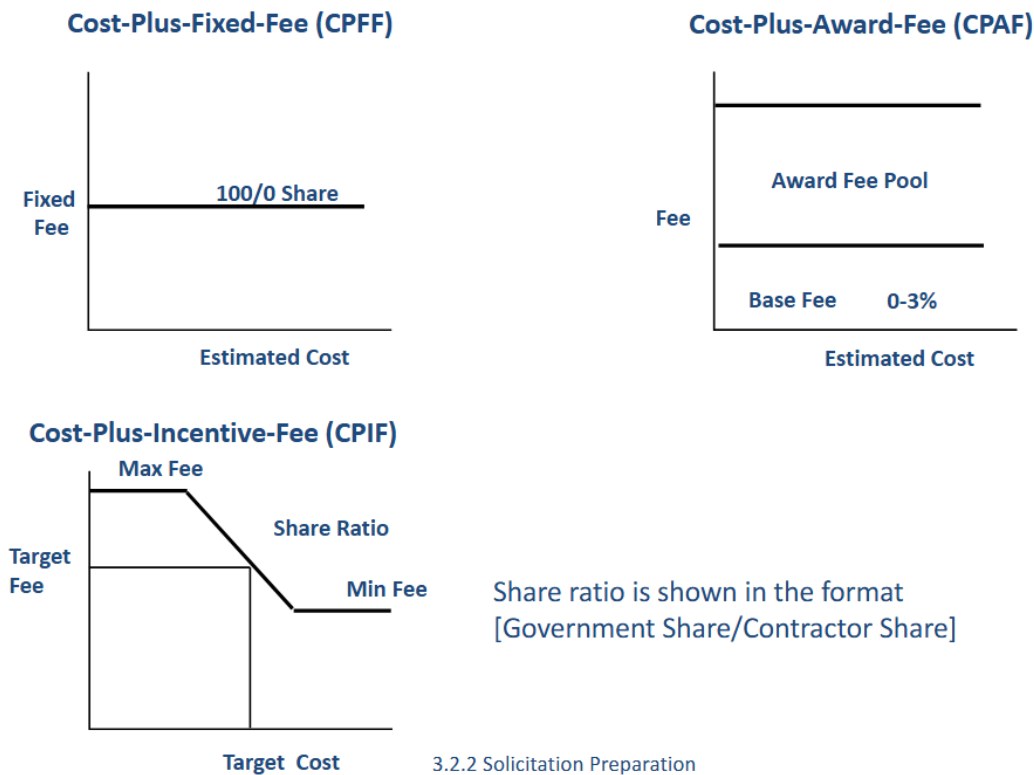

3.2.2 Solicitation Preparation

Figure 3.2. Cost-reimbursement contract risk/fee characteristics. Source: edo-3-2-2-solicitation-prep-2025, edo-3-2-2-solicitation-prep-2025 [edo-3-2-2-solicitation-prep-2025].

Award v.s. incentive fees. Incentive fees (cost or performance) are calculated from predetermined formulas tied to measurable outcomes (cost, schedule, technical). Award fees are earned through periodic board evaluations against tailored factors and may be unearned if performance is merely satisfactory [FAR, NAVSEA-Contracts-Handbook-2023].

Award-fee governance. The Award Fee Determining Official (often the PM or SSA designee) chairs an Award Fee Board, uses the approved plan, and issues a determination memo. Fees are paid after each period and must be commensurate with value delivered; scores below the threshold earn zero dollars for that segment [FAR, NAVSEA-Source-Selection-Guide-2022].

MCA phase alignment. MSA and TMRR generally use CPFF or CPAF because of design uncertainty; EMD can transition to CPIF or FPIF as risk retires; Production and Deployment favors FFP/FPIF; Operations and Support relies on FFP or FFP Level of Effort (LOE) and can incorporate sustainment IDIQs for depot work [DoDI5000-85].

MSA. Analytical trades and early prototypes benefit from CPFF flexibility as requirement scope evolves.

TMRR. CPIF/CPAF maintain incentives while the Government still absorbs major technical risk during competitive prototyping.

EMD. FPIF or CPIF balance contractor motivation and cost control once the design stabilizes, with ceilings to protect the Government.

PD. FFP/FPIF dominate because production baselines and learning curves are known; contractor should own execution risk.

OS. Sustainment leverages FFP, FFP LOE, or IDIQs task orders to manage repeatable workloads and retain competition for modernization.

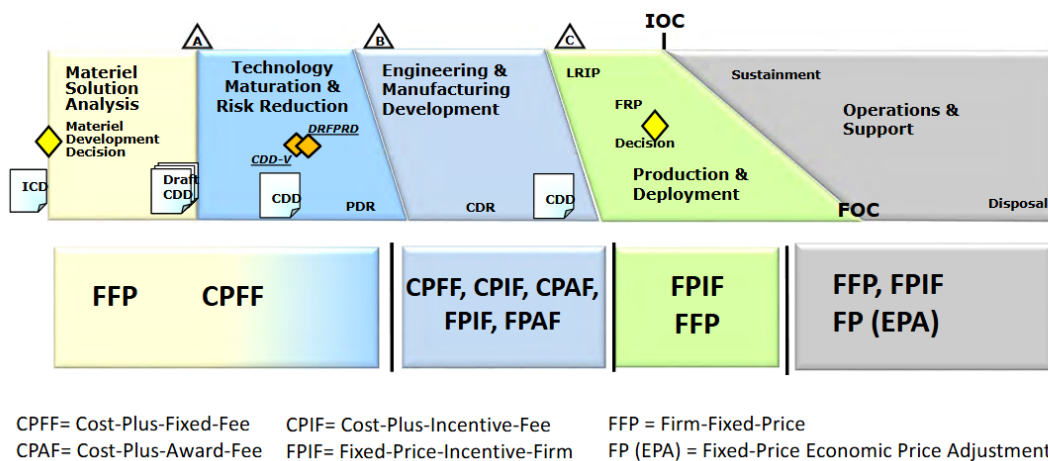


Figure 3.3. Contract-type emphasis across the Major Capability Acquisition phases.

3.2.9 Fixed-Price Incentive (Firm Target) Mechanics

Share ratio. Defines how cost overruns or underruns are split between Government and contractor (e.g., 70/30 means Government absorbs 70)

Point of Total Assumption (PTA). The cost point beyond which every additional dollar of overrun is borne entirely by the contractor:

$$PTA = \frac{\text{Ceiling Price} - \text{Target Cost}}{\text{Government Share Ratio}} + \text{Target Cost}.$$

Example. Target cost \$100M, target profit \$10M (target price \$110M), ceiling price \$120M, share ratio 70/30. If actual cost is \$112M:

$$\text{Contract price} = \$110M + 0.3 \times (\$100M - \$112M) = \$106.4M.$$

The PTA occurs at \$113.3M; beyond that, profit erodes dollar-for-dollar until exhausted [FAR, NAVSEA-Contracts-Handbook-2023].

3.2.10 Indefinite & Flexible Contract Forms

IDIQ. Indefinite-Delivery, Indefinite-Quantity contracts provide flexibility in quantity and timing with task/delivery orders; suited for recurring installations, sustainment, or services [FAR].

Time-and-Materials (T&M)/Labor-Hour (LH). Hybrid vehicles when it is not possible to estimate effort precisely; require ceiling price, surveillance, and justification because Government assumes cost risk on labor hours [FAR].

Undefinitized Contract Actions (UCAs). Letter contracts or other actions authorized before all terms are settled (e.g., urgent ship repair). Must be definitized within the regulatory timeline, with strict management for obligation limits and profit [FAR, DFARS, NMCARS].

3.2.11 Debriefings and Protests (Forums and Timelines)

Debriefings. Post-award (and certain pre-award) debriefings are conducted per [FAR]. For DoD enhanced debriefings, the question period extends the debrief conclusion for protest timeliness purposes; verify current Class Deviation guidance.

Protest forums. (i) Agency-level to the contracting activity (KO/Head of Contracting Activity) [FAR]; (ii) GAO bid protests [FAR]; (iii) U.S. Court of Federal Claims (COFC) under 28 U.S.C. § 1491(b).

Who handles them. Agency: procuring activity and counsel; GAO: GAO decides, agency produces the record and implements any stay; COFC: Department of Justice litigates, COFC judge adjudicates and may grant injunctive relief.

Timelines (common rules). Pre-award challenges to solicitation terms must be filed before the proposal due date. For post-award protests at GAO: file within 10 calendar days of when the basis is known, or within 5 business days after debriefing conclusion to obtain an automatic stay of performance under CICA. Agency-level protest timeliness follows similar 10-day knowledge rules in [FAR]. COFC has no fixed day-limit but relief is equitable; prompt filing is expected.

3.2.12 Why Cost-Plus After Low-Rate Initial Production? (PD and O&S Exceptions)

High residual technical risk. Post-LRIP, major engineering change proposals, tech refresh, or obsolescence-driven redesign can reintroduce uncertainty better handled under CPIF/CPAF than FFP.

Unstable scope or emergent defects. Corrective actions discovered during Initial Operational Test and Evaluation (IOT&E)/early fielding may require iterative investigation and rework where a best-effort *cost-reimbursable* vehicle protects schedule and access to talent.

Sustainment stand-up. Initial depot activation, organic transition, or complex Performance-Based Logistics (PBL) standing up new measurements and data flows can warrant short-duration CPFF/CPAF with incentives while processes stabilize.

Data rights/technical baseline gaps. Where the Government lacks detailed technical data to price FFP confidently, a temporary cost-plus arrangement with aggressive CDRL deliverables can bridge to FFP.

Governance. Treat as exceptions with a plan to transition to FFP/FPIF once uncertainty retires; document rationale in the Acquisition Strategy and obtain approvals consistent with [FAR, DFARS].

3.2.13 Simplified Acquisition and Small Business Programs

Simplified Acquisition Threshold (SAT). Generally \$250,000 (higher in contingency or overseas circumstances). Benefits include streamlined competition, quotation-based awards, and mandatory small-business reservations above the micro-purchase threshold [FAR].

Small Business Administration (SBA) programs. FAR Part 19 [FAR] implements 8(a), Historically Underutilized Business Zone (HUBZone), Service-Disabled Veteran-Owned Small Business (SDVOSB), and Women-Owned Small Business (WOSB) programs. The contracting officer must consider set-asides, sole-source thresholds, and subcontracting plans to meet DON goals.

3.2.14 Alternative Acquisition Authorities

Other Transaction (OT) agreements. Authorized by 10 U.S.C. § 4021 (prototype) and § 4022 (follow-on production) to rapidly engage nontraditional performers, provided cost share or significant participation criteria are met [USC-4021-OTA, USC-4022-OTF].

Small Business Innovation Research (SBIR). 15 U.S.C. § 638 establishes Phase I (feasibility), Phase II (prototype), and Phase III (commercialization/production). SBIR awards leverage R&D funds to deliver Navy-unique technology with data rights protections for five years [USC-638-SBIR].

3.2.15 Technical Data Rights Overview

Unlimited rights. Government may use, disclose, and authorize others without restriction (typically for data developed exclusively at Government expense) [DFARS].

Government purpose rights. Government may use or authorize contractors for Government purposes for five years, after which rights convert to unlimited. Applies to mixed-funding developments [DFARS].

Limited/Restricted rights. Contractor retains control; Government use is constrained to internal purposes (limited for noncommercial technical data, restricted for commercial computer software). Negotiated licenses or specifically negotiated licenses can expand access [DFARS].

3.2.16 Uniform Contract Format Essentials

Sections A through H (contract). Cover Standard Form 33, supplies/services, packaging, inspection, delivery, special contract requirements, clauses, and attachments [FAR].

Sections I through K (legal/representations). Incorporate FAR/DFARS clauses, representations, certifications, and instructions for completion [FAR, DFARS].

Sections L and M (solicitation/Evaluation). Instructions to offerors, proposal structure, page limits, and evaluation criteria that must remain synchronized to any change to factors or relative order requires an amendment [FAR, NAVSEA-Source-Selection-Guide-2022].

3.3 Cost and Price Evaluation

Refs:

3.3.1 Summary

KO accountability. The KO must determine that every negotiated price is fair and reasonable, integrating price, cost, technical, field-pricing, and risk analysis inputs before award per FAR 15.404-1(a)(1)–(5) [FAR].

Cost v.s. price lens. Use price analysis when certified cost or pricing data are not required, and escalate to cost analysis when element-by-element scrutiny is needed to support the prenegotiation objective [FAR].

Rate discipline. Forward pricing rates and structured profit analysis keep the Government prenegotiation objective current; the objective is always proposed cost plus profit or fee per FAR policy [FAR].

Financial health cue. Profitability ratios (Return on Sales (ROS), Return on Assets (ROA)) and cash-flow checks expose responsibility risk and focus Defense Contract Audit Agency (DCAA)/ DCMA field-pricing support requested by the KO [FAR] [edo-3-2-4-cost-price-evaluation-2024].

3.3.2 Practitioner Steps

1. Baseline the offeror's proposal: confirm certified cost or pricing data requirements, request data other than certified cost or pricing data when warranted, and map contractual requirement traces [FAR].
2. Execute price analysis first—compare competition results, historical buys, catalog/commercial data, and independent estimates; pivot to cost analysis when price analysis alone cannot demonstrate reasonableness [FAR].
3. Decompose direct labor, material, and Other Direct Costs (ODCs); verify indirect pools and allocation bases; and apply the five allowability tests before accepting proposed cost elements [FAR].
4. Establish the profit/fee objective using the agency's structured approach and update forward pricing rates or agreements as necessary to avoid stale factors in negotiations [FAR].
5. Pull in field-pricing support early: blend DCAA audit results, DCMA production assessments, and program team technical evaluations into the prenegotiation briefing and contract file [FAR] [FAR] [DFARS].

3.3.3 Proposed Price, Cost, Profit, and Fee

The breakdown of the proposed price is showing in Figure 3.4 and described below.

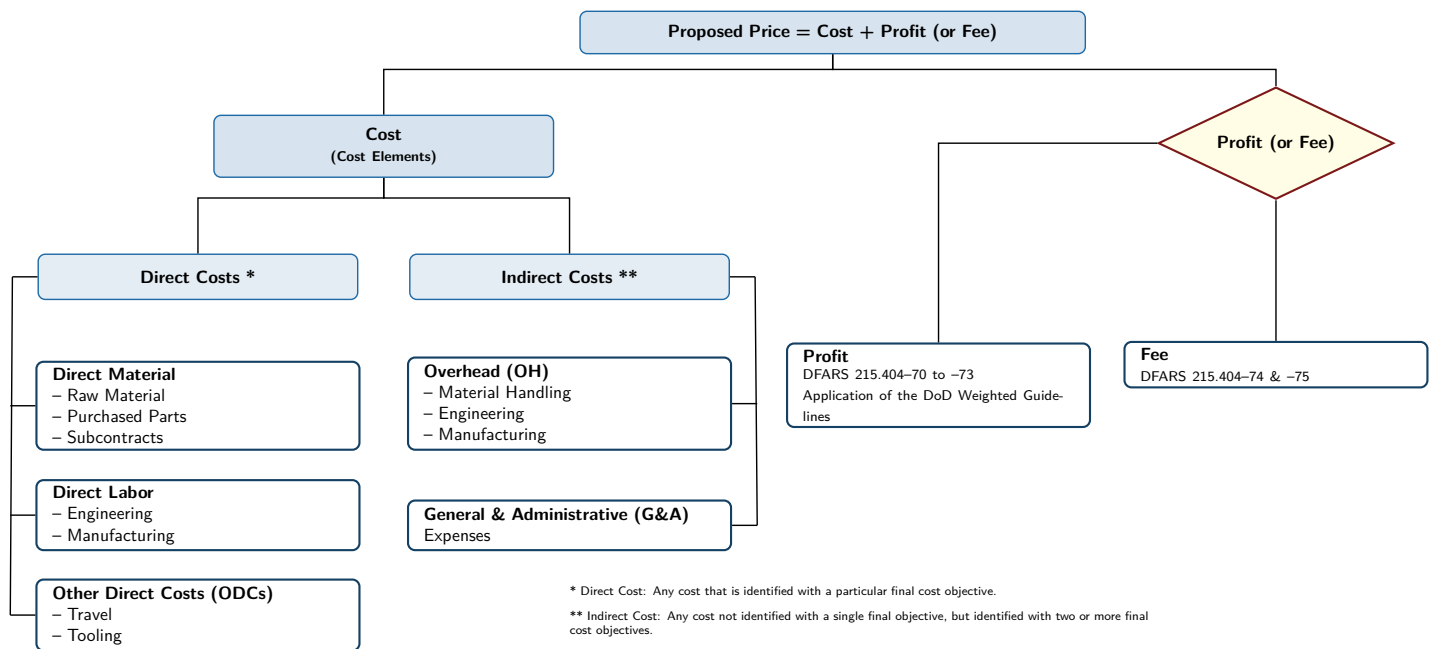


Figure 3.4. Mapping direct v.s. indirect contractor cost elements. Source: edo-3-2-4-cost-price-evaluation-2024, edo-3-2-4-cost-price-evaluation-2024 [e

Proposed price. The offeror's total price equals estimated cost plus any profit or fee applicable to the contract type [FAR].

Cost. Sum of allowable direct and indirect costs required to deliver the contract—all subject to reasonableness, allocability, and cost-principle limits [FAR].

Profit. Negotiated incentive element above allowable cost for fixed-price or incentive contracts, set through structured analysis [FAR].

Fee. Fixed remuneration on cost-reimbursement vehicles that does not vary with actual cost (e.g., CPFF fee) [FAR].

3.3.4 Direct and Indirect Cost Structure

Direct cost pools. Direct labor, materials, and ODCs traceable to a single final cost objective; charged through project-specific accounts backed by bills of material, timecards, travel authorizations, or subcontract quotes [FAR] [edo-3-2-4-cost-price-evaluation-2024].

Indirect cost pools. Overhead (manufacturing, engineering) and General and Administrative (G&A) accrued across multiple objectives, then allocated using consistent bases that reflect benefits received [FAR].

3.3.5 Other Direct Costs and Cost Allowability

ODCs. Travel, subcontract services, specialized tooling, and similar charges that can be singled out for the contract even though they are not labor or bulk material categories [FAR] [edo-3-2-4-cost-price-evaluation-2024].

Cost allowability. A cost is billable only if it is reasonable, allocable, consistent with applicable Cost Accounting Standards (CAS) / Generally Accepted Accounting Principles (GAAP), compliant with contract terms, and within any Subpart 31.2 limitations [FAR].

Note

Slides may refer to “cash allowability”; FAR terminology is *cost* allowability.

3.3.6 Cost and Price Analysis

Price analysis. Examination of the total proposed price without breaking out cost elements using competition, historical buys, or market indicators [FAR].

Cost analysis. Evaluation of individual cost elements (direct, indirect, and profit) when price analysis alone cannot demonstrate reasonableness [FAR].

Integrated view. Technical analysis, field-pricing support, and risk assessments feed both techniques to substantiate the final fair and reasonable determination [FAR].

3.3.7 Forward Pricing Rates and Fully Burdened Labor

Forward Pricing Rate Proposal (FPRP). Contractor-submitted forward pricing rate proposal that lays out projected indirect rates and factors for the pricing period [FAR].

Forward Pricing Rate Agreement (FPRA). Negotiated agreement-often executed by DCMA-that locks indirect rates for one to three years, reducing repetitive audits and speeding negotiations [FAR] [edo-3-2-4-cost-price-evaluation-2024].

Fully burdened rate. Applies direct labor, indirect burdens, and any negotiated profit/fee to a common labor-hour baseline so skill mixes can be compared on an apples-to-apples basis [edo-3-2-4-cost-price-evaluation-2024].

3.3.8 Indirect Rate Math and Profitability Checks

Apply the standard relationships from the cost principles and the coursebook when validating proposals; they are board favorites for quick-turn computations covering indirect pools, Total Cost Input (TCI), G&A, and profitability metrics such as ROS and ROA [FAR] [edo-3-2-4-cost-price-evaluation-2024].

$$\text{Indirect Cost Rate} = \frac{\text{Indirect Cost Pool}}{\text{Allocation Base}}$$

(3.1)

$$\text{TCI} = \text{Direct Cost} + \text{Overhead Cost}$$

(3.2)

$$\text{G\&A Cost} = \text{G\&A Rate} \times \text{TCI}$$

(3.3)

$$\text{Fully Burdened Labor Rate} = \frac{\text{Direct Labor Cost} + \text{Indirect Costs} + \text{Profit/Fee}}{\text{Direct Labor Hours}}$$

(3.4)

$$\text{ROS} = \frac{\text{Operating Profit}}{\text{Net Sales}}$$

(3.5)

$$\text{ROA} = \frac{\text{Net Income}}{\text{Total Assets}}$$

(3.6)

Track ROS and ROA against industry benchmarks, cash-on-hand, and debt loads to detect responsibility concerns or unsustainable buy-ins before negotiations [edo-3-2-4-cost-price-evaluation-2024].

3.3.9 Oversight and Field Pricing Support

DCMA production insight. Delegated contract administration offices deliver manufacturing surveillance, schedule risk analysis, and forward-pricing coordination; DFARS highlights that payment authority stays with the buying command even when DCMA supports rates [DFARS] [edo-3-2-4-cost-price-evaluation-2024].

DCAA audit coverage. DCAA is the responsible Government audit agency for most contractors, providing proposal adequacy reviews, incurred cost audits, and financial capability analyses [FAR].

Integrated negotiation record. Document how DCMA, DCAA, technical, and program inputs influenced the prenegotiation objective and the final price reasonableness determination [FAR] [edo-3-2-4-cost-price-evaluation-2024].

3.3.10 Checklist

- File both price and cost analysis results (including technical inputs) showing how the fair-and-reasonable price was determined [FAR].
 - Verify each significant cost element passes the five allowability tests and that allocation bases match current practice [FAR].
 - Confirm the current FPRA/FPRP is in the file or document why legacy rates remain valid [FAR].
 - Capture DCAA audit opinions, DCMA rate guidance, and profitability ratio trends in the prenegotiation briefing to evidence responsibility diligence [FAR] [edo-3-2-4-cost-price-evaluation-2024].
-

3.4 Earned Value Management (EVM)

Refs:

3.4.1 What EVM is

Earned Value Management (EVM) is a project management technique that integrates scope, schedule, and cost to assess project performance and progress. It provides a quantitative measure of project performance by comparing the planned work with the actual work completed and the associated costs. EVM is widely used in government and defense projects to ensure that projects are delivered on time and within budget.

3.4.2 Key Components of EVM

Core cost and schedule metrics establish the earned value performance baseline [edo-3-6-1-evm-intro-2025, edo-3-6-2-evm-analysis-2025].

Planned Value (PV) / Budgeted Cost of Work Scheduled (BCWS): The budgeted cost for the work scheduled to be completed by a specific date.

Earned Value (EV) / Budgeted Cost of Work Performed (BCWP): The budgeted cost for the work actually completed by a specific date.

Actual Cost (AC) / Actual Cost of Work Performed (ACWP): The actual cost incurred for the work completed by a specific date.

Budget at Completion (BAC): The total budget allocated for the project.

Estimate at Completion (EAC): The forecasted total cost of the project based on current performance.

Cost Performance Index (CPI): A measure of cost efficiency, calculated as $CPI = EV/AC$. A CPI less than 1 indicates a cost overrun.

Schedule Performance Index (SPI): A measure of schedule efficiency, calculated as $SPI = EV/PV$. An SPI less than 1 indicates a schedule delay.

Schedule Variance (SV): The difference between the earned value and the planned value, calculated as $SV = EV - PV$. A negative SV indicates a schedule delay.

Cost Variance (CV): The difference between the earned value and the actual cost, calculated as $CV = EV - AC$. A negative CV indicates a cost overrun.

Info

The first three are equivalent terms and should know both. This guide will use the first set (PV, EV, AC)

3.4.3 When to Use EVM

EVM is mandated on cost or incentive contracts (and applicable subcontracts) when the program meets the policy thresholds and the effort is discretely measurable [**edo-3-6-1-evm-intro-2025**, **DFARS**]. Key decision points for the PM include:

\$100 million and above: Implement the full ANSI/EIA-748 standard and ensure the contractor's system is formally validated by DCMA.

\$20 million to \$99.9 million: Implement ANSI/EIA-748 guidelines, with validation required when performance indicates risk.

Additional policy considerations follow [**edo-3-6-1-evm-intro-2025**, **DoDI5000-85**].

- Applicability determinations must confirm the work scope can be discretely measured before mandating EVM.
- The Milestone Decision Authority may approve EVM on FFP, time-and-materials, or LOE contracts, but such use is discouraged absent clear benefit.
- For efforts below \$20 million, the PM conducts a risk-based cost-benefit analysis to decide whether EVM adds value.
- Contracts that require EVM must also deliver Integrated Program Manager's Data Analysis Report (IPMDAR) data and complete an IBR within six months of award.

3.4.4 EVM Compliance

EVM clauses are flowed in the solicitation and award package (DFARS 252.234-7001 and 252.234-7002) alongside the Contractor Business Systems clause (DFARS 252.242-7005) to anchor validation and surveillance requirements [**DFARS**]. Compliance expectations follow [**edo-3-6-1-evm-intro-2025**, **DoDI5000-85**].

- The program office integrates EVM planning into the WBS, maintains the Performance Measurement Baseline, and ensures timely receipt and analysis of IPMDAR submissions.
- DCMA leads EVM system acceptance, validation, and ongoing surveillance against ANSI/EIA-748 and the DoW EVM Implementation Guide; DCAA supports with accounting system audits.
- Service focal points such as Acquisition Data and Analytics and the DON Center for EVM adjudicate applicability determinations and coordinate policy updates.
- SUPSHIP can execute validation and surveillance responsibilities for shipbuilding programs on behalf of DCMA.

3.4.5 EVM Compliance

EVM clauses are flowed in the solicitation and award package (DFARS 252.234-7001 and 252.234-7002) alongside the Contractor Business Systems clause (DFARS 252.242-7005) to anchor validation and surveillance requirements [**DFARS**]. Compliance expectations follow [**edo-3-6-1-evm-intro-2025**, **DoDI5000-85**].

- The program office integrates EVM planning into the WBS, maintains the Performance Measurement Baseline, and ensures timely receipt and analysis of IPMDAR submissions.
- DCMA leads EVM system acceptance, validation, and ongoing surveillance against ANSI/EIA-748 and the DoW EVM Implementation Guide; DCAA supports with accounting system audits.
- Service focal points such as Acquisition Data and Analytics and the DON Center for EVM adjudicate applicability determinations and coordinate policy updates.
- SUPSHIP can execute validation and surveillance responsibilities for shipbuilding programs on behalf of DCMA.

3.4.6 EVM Principal Players

Programmatic, contracting, and oversight roles synchronize to sustain disciplined performance management [edo-3-6-1-evm-intro-2025].

PMO: Implements EVM on the contract, ensures solicitations and awards contain the required clauses, and works with the contracting activity to tailor reporting and Integrated Master Schedule (IMS) requirements.

DCMA: Serves as the DoW EVM Executive Agent by validating, accepting, and surveilling contractor systems, maintaining the official acceptance roster, and analyzing IPMDAR and schedule submissions (including the 14-point IMS review) to focus government attention on emerging issues.

DCAA: Conducts accounting system audits, corroborates cost data, and supports DCMA during surveillance events and reviews.

Acquisition Data and Analytics (ADA): Acts as the department-wide focal point for EVM policy, guidance, and competency management; issues interpretations to maintain consistent application across programs.

DON Center for EVM: Coordinates applicability determinations with Deputy Assistant Secretary of the Navy (Acquisition Policy and Budget) (DASN (APB)) and OSD, and serves as the Navy's central point of contact for EVM matters.

SUPSHIP: Performs many DCMA/DCAA surveillance roles for shipbuilding contracts when delegated by the cognizant program office.

3.4.7 PMB

Figure 3.5 shows the characteristic S-curve depicting cumulative PV/BCWS, while Figure 3.6 summarizes the progression from defining the SOW to final Performance Measurement Baseline (PMB) adjustments. PMBs are:

- Scoped, scheduled, and budgeted plans for the authorized work
- Time-phased budgets that align to the master schedule
- The basis for cost and schedule performance management

- Effectively the PV for the entire project

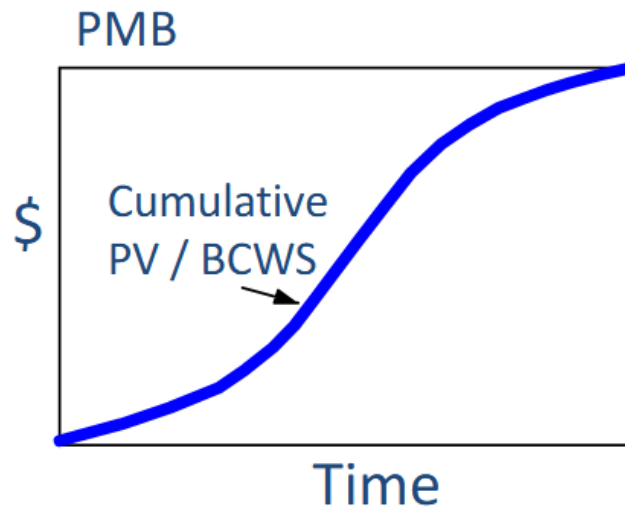


Figure 3.5. PMB Cost v.s. Time chart showing the “S”-curve. Source: edo-3-6-1-evm-intro-2025, edo-3-6-1-evm-intro-2025 [edo-3-6-1-evm-intro-2025].



Figure 3.6. The development flow for PMB. Source: edo-3-6-1-evm-intro-2025, edo-3-6-1-evm-intro-2025 [edo-3-6-1-evm-intro-2025].

PMB Development

STEP 1: *Define all work.* Decompose the effort using the WBS and align it with the organizational structure. Control accounts are the natural management points where Control Account Managers (CAMs) are assigned, and each control account contains work packages and (if needed) planning packages.

STEP 2: *Schedule the work.* Develop the integrated schedule (often visualized with Gantt charts) that sequences the WBS elements, includes key milestones, and forms the backbone of the time-phased budget.

STEP 3: *Budget the work.* Assign time-phased budgets to each work package, establish management reserve for in-scope known unknowns, and confirm that the sum of the control accounts equals the contract budget base.

Changes to the PMB must be formally controlled and documented. Reasons for changes include:

- Contract changes
- Internal replanning

- Formal reprogramming

3.4.8 EVM Reviews and Reports

Formal reviews validate the integrity of EVM data products before and after system acceptance [edo-3-6-1-evm-intro-2025].

Post-Acceptance Review

- Objective: ensure performance data remain accurate after system acceptance and identify any corrective actions required to reaffirm compliance.
- Timing: conducted as needed following system acceptance and prior to the next IBR.
- Led by the Review Director (typically DCMA) with membership tailored to the purpose of the review.
- Culminates in a formal report prepared by the Review Director.

Initial Compliance Evaluation

- Objective: validate that the Contractor's EVM system description matches actual practice and satisfies the EVMS criteria.
- Timing: executed prior to the initial IBR (and subsequently only if needed).
- Led by the DCMA Review Director with cross-functional support as required.
- Results documented in a report signed by the Review Director.

Integrated Baseline Review

- Participants: the contractor, PM and deputy, DCMA/DCAA/SUPSHIP personnel, and relevant technical staff.
- Purpose: joint assessment to verify the realism and accuracy of the PMB, confirm the entire technical scope is captured, and ensure resources and schedules are achievable.
- Timing: conducted within six months of contract award (or major replanning event) in accordance with the DoW EVM Implementation Guide and service policy [edo-3-6-1-evm-intro-2025].

Integrated Program Management Data Analysis Report

This contractually required report delivers cost, schedule, and technical status derived from the Contractor's EVM system, enabling the PMO to identify performance problem areas and emerging risks. It is required on every contract that mandates EVM and must be delivered at least monthly. The data set is tailored for each contract based on risk, size, and integration considerations, but the canonical formats are:

1. WBS (most common)
2. Organizational categories

3. Program Management Baseline
4. Staffing
5. Explanation and Problem Analysis
6. IMS

A Contract Funds Status Report (CSFR) complements the IPMDAR by providing funding (price) information that reconciles to the cost-focused earned value data [edo-3-6-1-evm-intro-2025].

Problems

When using EVM, the following are indications that a problem exists [edo-3-6-2-evm-analysis-2025].

- Use of management reserves
- Significant revisions to the PMB
- Zero variance
- Sudden change in trends
- Unreasonable Total Cost Performance Index (TCPI)

3.4.9 EVM Data Analysis

Figure 3.7 shows the S-curve representation of the EVM variables; the gaps between the curves are the cost and schedule variances that drive performance assessments [edo-3-6-2-evm-analysis-2025].

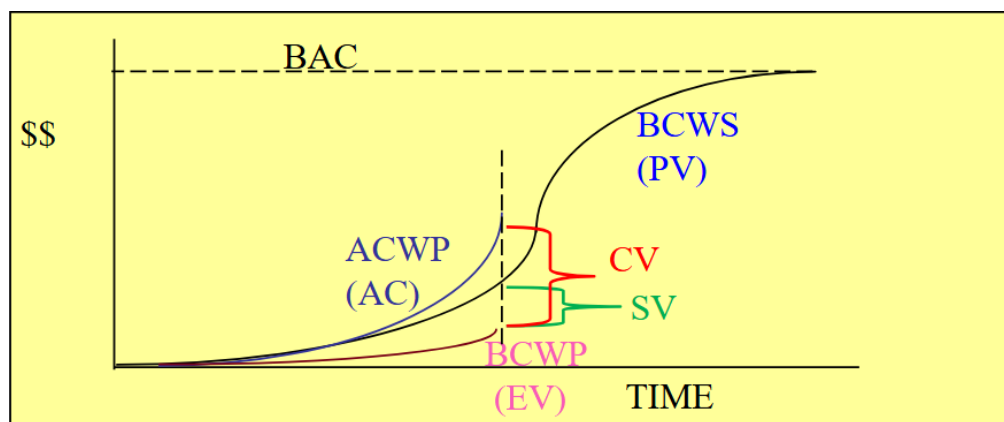


Figure 3.7. EVM chart showing the independent variables and variances. Source: edo-3-6-2-evm-analysis-2025, edo-3-6-2-evm-analysis-2025 [edo-3-6-2-evm-analysis-2025].

Data Analysis Steps

1. **Get current status:** capture the latest cost and schedule performance using CPI, SPI, and narrative explanations.

2. **Identify trends:** analyze indices and variance trajectories over time to highlight emerging risks and opportunities.
3. **Predict completion:** develop independent EAC and Variance at Complete (VAC) assessments to forecast final outcomes.
4. **Determine management actions:** decide where to apply resources, contract changes, or risk mitigations to recover performance [edo-3-6-2-evm-analysis-2025].

Performance Measurement Techniques

Percent Complete: Applies to long-duration tasks lacking interim milestones; progress is reported as the earned value fraction of total budget.

Weighted Milestones: Uses milestone weights for long-duration tasks with clear waypoints, crediting earned value as milestones are completed.

Percent Start/Percent Finish: Suitable for short-duration tasks (less than two reporting periods) with credit apportioned at start and finish.

0/100 Method: Provides earned value only when the task is complete, offering a conservative measure for discrete, short tasks [edo-3-6-2-evm-analysis-2025].

Equations

Standard cost and schedule performance calculations include [edo-3-6-2-evm-analysis-2025].

$$CV = EV - AC$$

$$SV = EV - PV$$

$$CPI = \frac{EV}{AC}$$

$$SPI = \frac{EV}{PV}$$

$$CV\% = \left(\frac{CV}{EV} \right) \times 100$$

$$SV\% = \left(\frac{SV}{PV} \right) \times 100$$

$$\% \text{ Complete} = \left(\frac{EV}{BAC} \right) \times 100$$

$$\% \text{ Spent} = \left(\frac{AC}{BAC} \right) \times 100$$

$$EAC = \frac{BAC}{CPI}$$

$$EAC = AC + \frac{BAC - EV}{\left(\frac{EV}{AC} \right)_{3 \text{ months}}}$$

$$EAC = AC + \frac{BAC - EV}{CPI \times SPI}$$

$$EAC = AC + \frac{BAC - EV}{0.8 \text{ CPI} + 0.2 \text{ SPI}}$$

$$VAC = BAC - EAC$$

$$TCPI = \frac{\text{Work remaining}}{\text{Budget remaining}}$$

$$TCPI_{EAC} = \frac{BAC - EV}{EAC - AC}$$

$$TCPI_{BAC} = \frac{BAC - EV}{BAC - AC}$$

4 Defense Acquisitions

4.1 Acquisition Policy

Refs:

4.1.1 Summary

Statute drives authority. Title 10 charges the Military Departments to equip the force, while each annual NDAA refreshes acquisition authorities and reporting duties—know the latest delegation trail before advising a board [edo-3-3-1-acq-policy-players-2025].

Policy = DoW 5000 series. DoDD 5000.01 establishes acquisition principles and senior roles; DoDI 5000.02 operationalizes the Adaptive Acquisition Framework (AAF) pathways; DoDI 5000.85 prescribes MCA execution details [DoDD5000-01, DoDI5000-02, DoDI5000-85].


Regulation stack. FAR > DFARS > NMCARS translates statute and policy into enforceable contracting rules; SEC-NAVINST 5000.2G tailors the AAF for DON programs and makes ASN(RD&A) the SAE [FAR, DFARS, SECNAV5000-2G].

The main drivers that a PM must balance is cost, schedule, and performance as shown in Figure 4.1. The trade space for performance versus cost is shown in Figure 4.2, which shows the relation of performance and cost with the threshold and objective requirements.



Figure 4.1. The cost, schedule, and performance triangle that must be balanced and traded.

Source: edo-3-3-1-acq-policy-players-2025, edo-3-3-1-acq-policy-players-2025 [edo-3-3-1-acq-policy-players-2025].

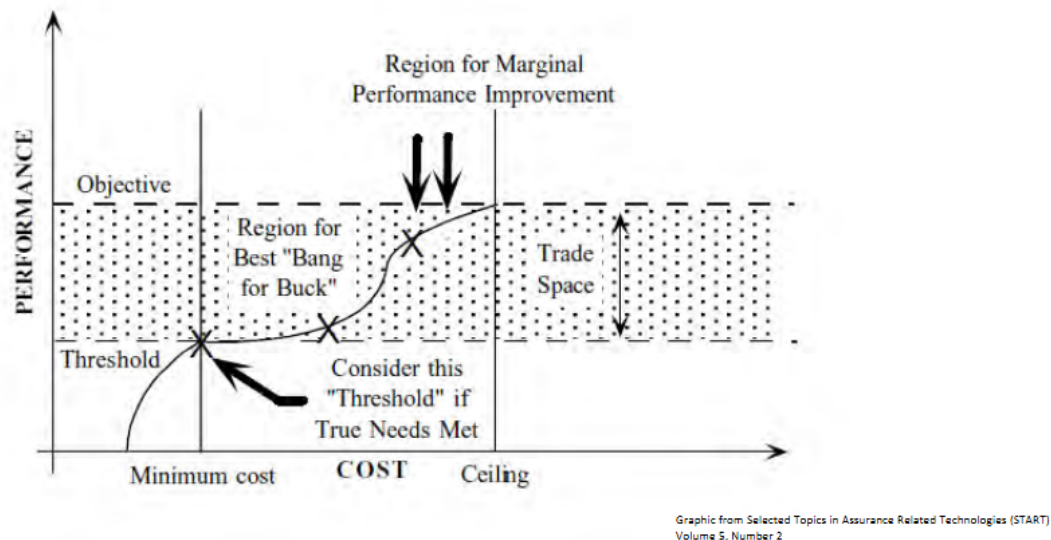

*The “knee of the curve” helps answer this question:
“Is the additional performance worth the additional investment?”*

3.3.1 Acquisition Policy and Players

Figure 4.2. Trade space of performance v.s. cost showing the range of viable options with the region of best “value.”

Source: edo-3-3-1-acq-policy-players-2025, edo-3-3-1-acq-policy-players-2025 [edo-3-3-1-acq-policy-players-2025].

4.1.2 Practitioner Steps (Board Prep Focus)

1. Confirm statutory authority and delegation: identify the Defense Acquisition Executive (DAE) (Under Secretary of War for Acquisition and Sustainment (USW(A&S))) or delegated MDA, the SAE, ASN(RD&A), and the resource sponsor accountable for the requirement [DoDD5000-01, edo-3-3-1-acq-policy-players-2025, SECNAV5000-2G].
2. Select the correct AAF pathway (or hybrid) and align entry/exit criteria, statutory reports, and decision forums (MS A/B/C, MDD, Business Case Analyses (BCAs), Congressional notices) [DoDI5000-02, DoDI5000-85].
3. Map contracting rules to the pathway: FAR/DFARS clauses, competition requirements, and Tailored Acquisition Strategy approvals [FAR, DFARS, edo-3-3-1-acq-policy-players-2025].
4. Crosswalk Navy overlays: SECNAVINST 5000.2G, SECNAVINST 5400.15D organization responsibilities, and PEO/DRPM charters for technical authority touchpoints [SECNAV5000-2G, SECNAV5400-15D].
5. Prepare decision documentation: update the Acquisition Strategy /Systems Engineering Plan (SEP) /Test and Evaluation Master Plan (TEMP), ensure statutory certifications (Clinger-Cohen, PPBE affordability caps) are current, and pre-brief the chain (Program Office → PEO → ASN(RD&A)) [DoDI5000-85, edo-3-3-1-acq-policy-players-2025].

4.1.3 Policy Stack and Authorities

Title 10, U.S.C. Establishes Service responsibilities (Subtitle C for DON organization, Subtitle A Part V for acquisition management) and empowers annual NDAA's to adjust acquisition thresholds or pilot authorities [edo-3-3-1-acq-policy-players-2025].

DoW Directives/Instructions. DoDD 5000.01 sets acquisition principles, governance forums, and senior leader responsibilities; DoDI 5000.02 implements the AAF with six scalable pathways; DoDI 5000.85 gives MCA-specific statutory requirements (Joint Requirements Oversight Council (JROC), cost reporting, baseline control) [DoDD5000-01, DoDI5000-02, DoDI5000-85].

Regulations. FAR and DFARS governs all federal contracting; DFARS adds DoW-specific clauses (e.g., earned value, data rights, cybersecurity); NMCARS adds DON policy and ASN(RD&A) approval levels [FAR, DFARS, NMCARS].

Service overlays. SECNAVINST 5000.2G tailors milestone documentation, Naval SYSCOM oversight, and Naval Accelerated Acquisition; SECNAVINST 5400.15D assigns PEO and SYSCOM responsibilities for acquisition program execution [SECNAV5000-2G, SECNAV5400-15D].

Advisory guidance. The Defense Acquisition Guidebook (DAG) captures best practices—it is not directive authority, but boards expect you to know how it informs planning reviews and tailoring memoranda [DoDAcqGuidebook].

Info

Boards expect you to quote the controlling document *and* state who owns the decision. Memorize the policy ladder:
Statute → Directive → Instruction → Regulation → Service overlay.

4.1.4 Acquisition Players and Decision Forums

DAE. USW(A&S) chairs the Defense Acquisition Board (DAB), is MDA for ACAT ID/IAM programs unless delegated, and approves key acquisition policies [DoDD5000-01, edo-3-3-1-acq-policy-players-2025].

SAE. ASN(RD&A) serves as the DON SAE; appoints PEOs, assigns MDA for ACAT II and below, and ensures Navy acquisition compliance with DoW policy [SECNAV5000-2G, SECNAV5400-15D].

Chief of Naval Operations/Resource Sponsor. Validates requirements and PPBE resourcing, provides integrated warfare/community priorities to ASN(RD&A) and the PEOs [edo-3-3-1-acq-policy-players-2025].

PEO/DRPM. Executes programs within delegated authorities; maintains acquisition baseline control, briefs ASN(RD&A) and DAB-level forums, and ensures SYSCOM technical authority integration [SECNAV5400-15D, DoDI5000-85].

PM. Accountable for cost, schedule, performance; leads the IPT, maintains statutory certifications, and readies milestone documentation [DoDI5000-85, edo-3-3-1-acq-policy-players-2025].

Governance forums. Milestone Decision Reviews, the DAB, Configuration Steering Boards, Overarching IPTs, and Navy Program Executive Council reviews provide structured oversight and risk adjudication [DoDD5000-01, DoDI5000-85, edo-3-3-1-acq-policy-players-2025].

Note

Edge case: Rapid acquisition authorities (e.g., UCA) compress governance. Ensure delegation letters document any waived statutory certifications before you recommend skipping a DAB or ASN(RD&A) review [DoDI5000-02].

4.1.5 Adaptive Acquisition Framework Pathways

The AAF can be visualized in Figure 4.3. The figure shows all six pathways with their purposes and general flow of the acquisition for each.

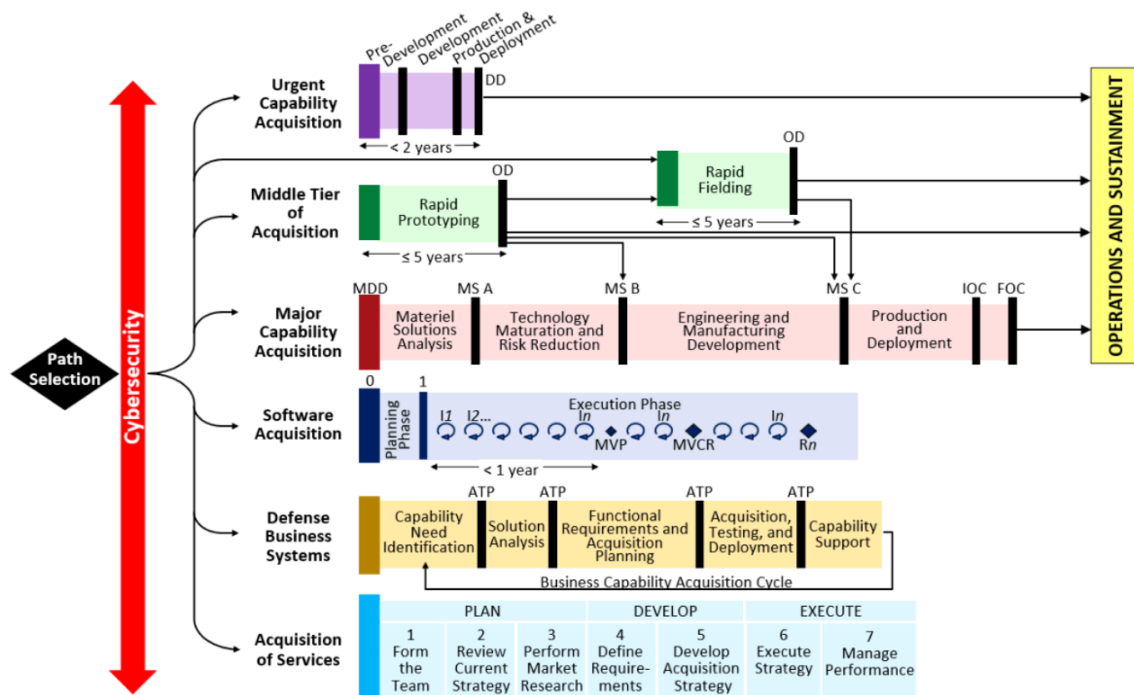


Figure 4.3. Adaptive Acquisition Pathways. Source: DAU-AAF, DAU-AAF [DAU-AAF].

The MCA is the main acquisition pathway that EDOs will operate in. As shown in Figure 4.4, it can be broken down into five phases, four major decision points and three milestones.




Figure 4.4. Major Capability Acquisition with phases, milestones, and decisions points. Source: edo-3-3-1-acq-policy-players-2025, edo-3-3-1-acq-policy-

Pathway Playbooks

Major Capability Acquisition.

Entry. Default when a validated ICD, PPBE affordability certification, and Title 10 Major Defense Acquisition Program (MDAP) thresholds are triggered; the DAE (USW(A&S)) or delegated MDA authorizes the Materiel Development Decision [DoDI5000-02, DoDI5000-85, USC-10-4201]. **Major events.** Materiel Solution Analysis, TMRR, EMD, Production & Deployment, and Operations & Support framed by MS A/B/C, Production Readiness Reviews, Configuration Steering Boards, and Full-Rate Production Decisions [DoDI5000-85]. **Outputs.** Acquisition Strategy, SEP, Life-Cycle Sustainment Plan (LCSP), TEMP, SAR/DAES, and when applicable Live Fire and survivability certifications [DoDI5000-85, DoDI5000-89, USC-10-2366]. **What happens.** The Program Manager leads integrated product teams, controls the Acquisition Program Baseline, and coordinates statutory certifications before each milestone package is staffed through the Navy Program Executive Council and the DAB [DoDI5000-85]. **Pros.** Maximum statutory confidence, predictable decision forums, and the ability to tailor documentation while retaining congressional transparency [DoDI5000-85]. **Cons.** Heavier documentation, longer lead times, and concurrency risks if requirements or funding discipline erodes between milestones [DoDI5000-85].

Middle Tier of Acquisition.

Entry. Warfighter sponsor certifies the capability can be prototyped or fielded within 5 years, and the MDA approves a rapid prototyping or rapid fielding strategy in lieu of JCIDS milestone paperwork [DoDI5000-80]. **Major events.** Competitive prototyping sprints, operational demonstrations, and limited fielding increments documented in the MTA Strategy and semiannual execution reports to Under Secretary of War for Research and Engineering (USW(R&E))/USW(A&S) [DoDI5000-80]. **Outputs.** MTA Acquisition Strategy, Test Strategy (tailored TEMP), transition plan to either MCA or sustainment funding, and congressional notifications when cost or schedule deviates [DoDI5000-80]. **What happens.** Programs lean on OTAs, digital engineering, and combined DT/OT events; logistics and cybersecurity artifacts are right-sized but must be ready before transition to production [DoDI5000-80]. **Pros.** Compresses documentation, accelerates learning, and protects prototyping budgets from the full milestone stack. **Cons.** Sustainment planning and PPBE wedges still have to be established before transition; poor exit planning strands prototypes without a production home [DoDI5000-80].

Software Acquisition Pathway.

Entry. Capability owner commits to iterative Development, Security, and Operations (DevSecOps) delivery, establishes a software factory or enterprise pipeline, and designates a product manager vice a traditional milestone PM [DoDI5000-87]. **Major events.** Plan, Execute, and Deliver phases with quarterly (or faster) capability drops, authority-to-operate reciprocity reviews, and portfolio synchronization reviews in lieu of MS A/B/C [DoDI5000-87]. **Outputs.** Software Acquisition Strategy, Product Roadmap, backlog burn-down metrics, continuous test/accreditation evidence, and sustainment metrics for cloud hosting costs [DoDI5000-87]. **What happens.** The government product owner jointly manages the pipeline with

contractors, employs automated testing, and updates requirements via configuration-controlled roadmaps instead of static CDDs [DoDI5000-87]. *Pros.* Continuous user feedback, cyber resiliency baked into each sprint, and the ability to budget in capability releases instead of monolithic blocks [DoDI5000-87]. *Cons.* Requires mature pipelines, disciplined product management, and close PPBE coordination to realign color-of-money profiles from hardware-centric norms [DoDI5000-87].

Urgent Capability Acquisition.

Entry. A validated Joint Urgent Operational Need (JUON)/Joint Emergent Operational Need (JEON)/Urgent Operational Need (UON) identifies a combatant-commander risk that cannot wait two years; ASN(RD&A) or USW(A&S) approves entry with an affordability determination and sustainment exit criteria [CJCSI3470-01H, DoDI5000-81]. *Major events.* Rapid assessment within days, solution selection inside 30 days, fielding no later than 24 months, and close-out/transition reviews that assign residual sustainment ownership [DoDI5000-81]. *Outputs.* Urgent Capability Acquisition Strategy, tailored test/safety releases, congressional notification packages, and a signed disposition plan for residual hardware [DoDI5000-81]. *What happens.* The Rapid Acquisition Cell coordinates funding reprogramming, waivers, and senior integration group decisions while the program office executes minimal-but-sufficient contracting and test [DoDI5000-81]. *Pros.* Weeks-to-months fielding, ability to leverage existing production lines or COTS solutions. *Cons.* Limited longevity (normally five years or less), intense oversight on waivers, and explicit requirement to transition to another pathway or divest [DoDI5000-81].

Defense Business Systems.

Entry. A portfolio exceeds the statutory DBS cost thresholds or is designated critical; requires Business Process Reengineering certification, a Functional Sponsor, and alignment to the Business Enterprise Architecture before funds may be released [DoDI5000-75]. *Major events.* Capability Needs Statement approval, Functional Requirements Board adjudication, incremental capability releases, and annual Investment Review Board certification to Congress [DoDI5000-75]. *Outputs.* Business Case, Functional Strategies, Capability Support Plan, data standards, and interoperability determinations to satisfy Net-Ready KPP expectations [DoDI5000-75]. *What happens.* Functional leads co-chair the IPT with the Program Manager, enforcing process improvements before automating legacy workflows [DoDI5000-75]. *Pros.* Forces portfolio-level prioritization, ties funding to measurable process change. *Cons.* Extra governance (IRB, Defense Business Council) and Clinger-Cohen certifications can slow schedules if stakeholders are not aligned early [DoDI5000-75].

Defense Acquisition of Services.

Entry. Non-IT services exceeding simplified acquisition thresholds, or any effort designated special interest, must use DoDI 5000.74 governance and appoint a Services Category Manager before solicitation [DoDI5000-74]. *Major events.* Service Requirement Review Board, Acquisition Strategy Panel, independent cost estimate for Category I/II services, and annual review of contractor performance metrics [DoDI5000-74]. *Outputs.* Services Acquisition Plan, Quality Assurance Surveillance Plan, Performance Work Statement, and documented affordability/cost realism analyses [DoDI5000-74]. *What happens.* Multifunctional teams (requirements owner, contracting, legal, comptroller) collaborate early, determine best-fit contract type, and tailor competitive ranges for recurring availabilities or modernization services [DoDI5000-74]. *Pros.* Aligns recurring services with category management, encourages outcome-based metrics. *Cons.* Additional reviews for Category I/II services can add lead time if the requirement was scoped as a product effort originally [DoDI5000-74].

Info

Pathways can be combined (e.g., prototype under Middle-Tier, transition to MCA, then adopt the Software Pathway for continuous upgrades). Boards expect you to articulate which statutory obligations remain even when tailoring [DoDI5000-02].

4.1.6 Warfighting Acquisition System Imperatives (2025)

Purpose.

Secretary of War (SECWAR) redesignated the Defense Acquisition System (DAS) as the Warfighting Acquisition System (WAS) on 7 Nov 2025 to treat acquisition as a warfighting function, make speed-to-field the primary metric, and push decisions to the accountable portfolio leaders [secwar-was-memo-2025].

Portfolio accountability.

Portfolio Acquisition Executives (PAEs) chair Capability Trade Councils, own integrated portfolio scorecards, and are tasked to deliver minimum viable combat capability in months—not years—while continuously iterating increments; they are expected to waive non-statutory documents, reallocate within portfolio controls, and document trades in decision memoranda [secwar-acq-transformation-2025, secwar-was-memo-2025].

Mission engineering and experimentation.

The Mission Engineering and Integration Activity (MEIA) replaces lengthy requirements staffing with rapid kill-chain analysis, cross-Service experiments, and industry demos so requirement adjustments are anchored in real data before the DAE or PAE commits resources [secwar-was-memo-2025, secwar-jcids-reform-2025].

Requirements–budget coupling.

Key Operational Problems (KOPs) and the Requirements and Resourcing Alignment Board (RRAB) ensure every joint problem statement is paired with funding guidance (including Joint Acceleration Reserve (JAR) taps) inside the same PPBE cycle, eliminating the historical gap between validated requirements and appropriated dollars [secwar-jcids-reform-2025].

Implications for EDOs.

Expect Capability Trade Council taskers in lieu of Configuration Steering Boards, portfolio scorecards that track cycle time from need to Initial Operational Capability, and requests for mission-thread data packages to feed MEIA campaigns—ships, systems, and industrial-base briefs must now quantify time-based performance alongside cost/schedule [secwar-was-memo-2025, secwar-acq-transformation-2025].

Info

Board cue: explain how you would tailor milestone documentation under the WAS memo while preserving statutory certifications (e.g., Clinger-Cohen, cybersecurity) and how you will capture trade rationales now that Capability Trade Councils replace legacy Configuration Steering Boards [secwar-was-memo-2025].

4.1.7 Urgent Operational Needs Governance

JUON.

Combatant commanders submit JUONs to the Joint Rapid Acquisition Cell when an unforeseen operational gap threatens lives or mission success within the current fight; the Joint Staff validates within days, assigns a lead Service, and requires fielding in ≤24 months with a plan to transition or terminate after the contingency [CJCSI3470-01H].

JEON.

A JEON covers emerging threats with a slightly longer horizon (2–5 years) but still demands joint prioritization, Functional Capabilities Board staffing, and explicit affordability bounds before the Joint Requirements Oversight Council renders a decision [CJCSI5123-01H].

UON.

Fleet, Type, and numbered Force Commanders elevate UONs per OPNAVINST 5000.42E; requests must include the operational vignette, DOTMLPF-P analysis, recommended sponsor, and incremental funding estimate before Gate 1 of the two-pass/seven-gate process [OPNAVINST5000-42E].

Request content.

Every urgent package documents the risk of not acting, desired operational effect, timeframe to theater, sustainment/retrograde plans, cybersecurity implications, and classification handling; incomplete data delays Joint Staff or OPNAV acceptance [CJCSI3470-01H, OPNAVINST5000-42E].

Acquisition handoff.

Validated packages flow to the UON Management Board and then to ASN(RD&A) for alignment with the Urgent Capability Acquisition (UCA) pathway, rapid contracting, and source selection; the MDA records any tailored documentation and must still close on lifecycle ownership before the temporary solution sunsets [DoDI5000-81].

4.1.8 Security Cooperation and Capital Alignment (2025 Reforms)

Arms-transfer realignment.

SECWAR shifted the Defense Security Cooperation Agency (DSCA) and the Defense Technology Security Administration (DTSA) under USW(A&S) to unify Foreign Military Sales, Direct Commercial Sales, technology protection, and industrial-base production decisions under one accountable enterprise that can plan exportability features early and keep allied demand synced with U.S. production lines [secwar-arms-transfer-2025].

National Security Capital Forum.

Section 1092 of the FY 2025 NDAA and subsequent SECWAR direction established the National Security Capital Forum (NSCF), chaired by the Office of Strategic Capital, to convene federal and non-federal financiers, monitor capital flows that affect defense production, and flag transactions that threaten supply-chain resilience [secwar-nscf-2025].

EDO relevance.

Program briefs now need to show how exportability, co-production, and investment incentives are built into acquisition strategies because DSCA/DTSA decisions and NSCF findings will increasingly shape schedule risk (supplier solvency, capital availability) and board questions on allied burden-sharing [**secwar-arms-transfer-2025**, **secwar-nscf-2025**].

4.1.9 Acquisition Categories and Delegated Decision Authority

USW(A&S) serves as the DAE; SECNAV designates ASN(RD&A) as both the Navy SAE and CAE, while SECNAVINST 5000.2G and the Warfighting Acquisition Strategy empower PAEs to manage portfolios and request tailored delegation [**DoDD5000-01**, **SECNAV5000-2G**, **secwar-acq-transformation-2025**].

ACAT I (MDAP).

Programs that meet the MDAP thresholds ($\geq$ \$525M RDT&E or $\geq$ \$3.6B procurement in FY 2020 constant dollars) default to DAE oversight; ACAT ID programs (e.g., *Columbia*-class SSBN) keep USW(A&S) as MDA, whereas ACAT IC efforts (e.g., DDG(X) combat systems refresh) are normally delegated to ASN(RD&A) with reporting to Congress via SAR/DAES [**USC-10-4201**, **DoDI5000-85**, **edo-3-3-1-acq-policy-players-2025**].

ACAT IA.

Major Automated Information Systems exceeding \$360 M life-cycle cost or designated by Under Secretary of War (Comptroller) (USW(C))/CAE; the Navy SAE is the default MDA and may assign PEO Digital or the relevant PAE to execute under the Software or Business Systems pathways (examples: Navy ERP, Maritime Maintenance IT portfolio) [**DoDI5000-02**, **DoDI5000-75**].

ACAT II.

Programs below MDAP thresholds but above \$200 M RDT&E or \$920 M procurement (FY 2020 constant dollars) are typically delegated from ASN(RD&A) to the cognizant PAE/PEO; examples include shipboard radars, launch-and-recovery systems, or complex weapon upgrades where the PEO retains the MDA [**DoDI5000-85**, **edo-3-3-1-acq-policy-players-2025**].

ACAT III.

Efforts below ACAT II thresholds (but still acquisition programs) normally have the PAE, SYSCOM commander, or PM acting as MDA; documentation is tailored, yet APBs, TEMPs, and configuration control still apply [**DoDI5000-85**, **SECNAV5000-2G**].

ACAT IV (DON unique).

SECNAVINST 5000.2G divides ACAT IV into IVT (test) and IVM (monitor) for sustainment, modernization, and In-Service Engineering efforts; NAVSEA/NAVAIR/NAVWAR commanders often serve as MDA, delegating narrowly scoped efforts to PMs while ensuring technical authority concurrence [**SECNAV5000-2G**].

Delegation chain. The DAE retains ACAT ID decisions unless a signed memo delegates to ASN(RD&A); the Navy SAE typically keeps ACAT IC/IA programs and can further delegate ACAT II/III/IV to PAEs. SECNAVINST 5000.2G requires each delegation letter to specify statutory certifications retained by ASN(RD&A), while the Warfighting Acquisition Strategy directs PAEs to chair Capability Trade Councils and reassign funds across their portfolios when trades stay within cost/schedule thresholds [**SECNAV5000-2G**, **secwar-acq-transformation-2025**].

4.1.10 Project Overmatch Status

Project Overmatch is the Navy’s operational architecture initiative to link platforms, weapons, sensors, and data fabrics so that Fleet Commanders can execute Combined Joint All-Domain Command and Control (CJADC2) and Joint Fires at decision speed [DVIDS-Overmatch-OpenDAGIR-2025, DVIDS-Overmatch-FVEY-2025]. VADM Seiko Okano serves as the direct reporting program manager (DRPM) for Project Overmatch and Commander, NAVWAR; she continues to sponsor Five Eyes data-sharing arrangements, Maven Smart Systems overlays, and Open DAGIR integrations that move capability from concept to fielded software in weeks [DVIDS-Okano-2024, DVIDS-Overmatch-OpenDAGIR-2025].

The DRPM title matters: a DRPM reports directly to ASN(RD&A), can tailor milestone documentation, and retains signature authority for integration decisions that cut across multiple PEOs. As PMILDEP, VADM Okano now chairs Program Decision Meetings when delegated, synchronizes PAEs across portfolios, and uses tools such as Open DAGIR and Maven to inform both requirements trades and PPBE issue papers [SECNAV5000-2G, DVIDS-Overmatch-OpenDAGIR-2025]. Her priorities for FY26–27 include: (1) expanding the Joint Fires Network interface validated during the 2025 FVEY Project Arrangement; (2) institutionalizing Open DAGIR so commercial AI/ML tools can be onboarded at “commercial speed”; and (3) ensuring Overmatch digital threads remain visible in milestone packages so that new ship, submarine, and aircraft programs inherit the data standards by default [DVIDS-Overmatch-FVEY-2025, DVIDS-Overmatch-OpenDAGIR-2025].

4.1.11 Navy Overlays and Touchpoints

- SECNAVINST 5000.2G.** Implements ASN(RD&A) Program Decision Meetings, requires risk-based tailoring plans, and codifies DON-level documentation (Acquisition Plan, LCSP, POA&M) [SECNAV5000-2G].
- SECNAVINST 5400.15D.** Aligns PEOs and SYSCOMs, clarifies technical authority (NAVSEA 05, NAVWAR 5.0) integration, and designates Deputy ASN(RD&A) portfolio responsibilities [SECNAV5400-15D].
- Resource Sponsor coordination.** OPNAV N9, N4, or equivalent sponsor must endorse requirements and PPBE positions before ASN(RD&A) decisions [edo-3-3-1-acq-policy-players-2025].

Note

When SECNAV policy conflicts with older DoW memoranda, defer to the most current directive from the higher authority unless ASN(RD&A) grants written tailoring. Document the rationale in the Acquisition Strategy.

4.2 Milestones and Phases

Refs:

4.2.1 Defense Acquisition System Overview

The DAS is the governance framework that aligns requirements, resourcing, and acquisition execution to deliver warfighter capability. It is policy-driven by DoDD 5000.01 and process-enabled through DoDI 5000.02, using the AAF to tailor pathways while preserving statutory oversight and Navy-unique controls [DoDD5000-01, DoDI5000-02].

4.2.2 Adaptive Acquisition Framework Pathways (Board Snapshot)

MCA. Default for complex weapon systems; uses phased milestones with mandatory statutory certifications; emphasizes affordability trades, test rigor, and Navy two-pass / seven-gate touchpoints [DoDI5000-85].

Middle Tier of Acquisition (MTA). Rapid prototyping or rapid fielding to deliver an operational capability within five years; minimizes documentation, but demands robust transition planning to MCA or sustainment funding [DoDI5000-80].

UCA. Accelerated path to field urgent capability within 2 years or provide an interim solution in less than 5; leverages tailored test, streamlined acquisition decision memoranda, and dedicated senior oversight [DoDI5000-81].

Software Acquisition Pathway. Iterative, DevSecOps-focused delivery of software increments with continuous integration, enterprise cloud alignment, and recurring user feedback cadences [DoDI5000-87].

Acquisition of Services Pathway. Structures service requirements, performance metrics, and contracting strategies to assure mission outcomes and oversight thresholds (e.g., Multi-Functional IPT requirements review) [DoDI5000-74].

Defense Business Systems Pathway. Rationalizes business processes, data standards, and Business Capability Acquisition Cycle (BCAC) to unlock enterprise interoperability before investing in solutions [DoDI5000-75].

Note

Pathways are not exclusive—an EDO may begin in MTA for prototyping, then transition to MCA for production once requirements and sustainment plans stabilize. Programs can also leverage UCA for an initial bridge while planning a transition to MCA.

4.2.3 Baseline Discipline: Acquisition Program Baselines, Deviations, and Nunn–McCurdy

APB. The cost-schedule-performance contract between the MDA, resource sponsor, and PEO; defines objective and threshold values that bound trade space [DoDI5000-85].

Program Deviations. Triggered when performance, schedule, or cost thresholds breach; the Program Manager must notify the MDA within 30 days and submit a corrective action plan within 60 [DoDI5000-85].

Nunn–McCurdy Act. Statutory reporting when Program Acquisition Unit Cost (PAUC) or Average Procurement Unit Cost (APUC) breaches significant ($\geq 15\%$ current / 30% original) or critical ($\geq 25\%$ current / 50% original) thresholds; critical breaches require certification to Congress within 60 days or program termination [USC-4371-NunnMcCurdy].

4.2.4 JCIDS Flow into the Defense Acquisition System

ICD. Supports the MDD with validated capability needs and initial attributes [CJCSI5123-01H].

CDD. Provides Key Performance Parameters (KPPs) and Key System Attributes (KSAs) to anchor Milestone B and the Technical Requirements Baseline [CJCSI5123-01H].

Capability Production Document (CPD). Updates KPP/KSA values for production decisions and sustainment planning at Milestone C [CJCSI5123-01H].

Note

Maintain requirements traceability matrices linking KPP thresholds to test plans and APB values for board discussions.

4.2.5 KPPs v.s. KSAs (Know the Difference)

KPP (Key Performance Parameter). A performance attribute of a system critical to mission success. Each KPP has a threshold (minimally acceptable) and objective (desired) value. Failure to meet a *threshold* normally triggers program reassessment or revalidation of the requirement. *Why it matters:* Drives design trades, tempers requirement creep, and is reportable in baselines and decision reviews [CJCSI5123-01H].

KSA (Key System Attribute). Important performance attribute not critical enough to be a KPP. KSAs are managed and traded to balance cost/schedule/performance without jeopardizing mission effectiveness. *Why it matters:* Provides disciplined trade-space for the Program Manager and requirements sponsor [CJCSI5123-01H].

Difference. KPPs are mission-critical and tightly controlled; KSAs are important but offer more flexibility. Both appear in the CDD/CPD with threshold/objective values, but KPPs carry higher visibility and risk if breached.

4.2.6 Acquisition Strategy Essentials

Purpose. Documents tailored acquisition approach, contract strategy, intellectual property posture, and affordability constraints for MDA approval [DoDI5000-85].

Key Contents. Pathway selection, phasing plan, incentive structure, test and evaluation strategy, risk burn-down, sustainment concept, cybersecurity, international cooperation, and business case for software/data management [DoDI5000-85, DoDD5000-01].

Approval Event. MDA concurrence at Milestone A (initial) with updates prior to Milestone B and significant re-baselines; Navy 2-pass/7-gate integrates resource validation before signature [OPNAVINST5000-42E].

4.2.7 International Acquisition Objectives

Foreign Military Sales (FMS). Strengthen partner capability while leveraging U.S. economies of scale; requires disclosure review and Letter of Offer and Acceptance alignment [DoDI5000-85].

- Direct Commercial Sales (DCS).** Contractor-led exports; Program Office ensures configuration control and technology-security compliance [DoDI5000-85].
- Cooperative Development.** Shared investment with allies (e.g., Memoranda of Understanding) to reduce life-cycle cost and enhance interoperability [DoDI5000-85].
- Armaments Cooperation / International Programs Security.** Integrates disclosure, export licensing, and technology protection plans into the Acquisition Strategy [DoDI5000-85].

4.2.8 Navy Two-Pass / Seven-Gate Review

- Pass 1 – Capability.** Led by OPNAV N9 to mature the requirement: Gate 1 validates the capability gap, Gate 2 refines solutions and mission analysis, Gate 3 assesses affordability and alignment with Navy enterprises, and Gate 4 authorizes program initiation (supports MDD) [OPNAVINST5000-42E].
- Pass 2 – Resourcing.** Led by OPNAV N8 to align budgeting: Gate 5 verifies contracting/test readiness before Milestone B (often synchronized with the Development RFP Release Decision), Gate 6 confirms production and sustainment resources prior to Milestone C, and Gate 7 evaluates sustainment performance and modernization plans [OPNAVINST5000-42E].

Note

For board prep, highlight where SECNAV Gate Reviews or Defense Acquisition Board touchpoints overlay Navy gates to demonstrate cross-tier synchronization.

4.2.9 Technology Readiness Levels

Table 4.1 summarizes Technology Readiness Level (TRL) definitions with representative naval examples.

TABLE 4.1: TECHNOLOGY READINESS LEVELS WITH REPRESENTATIVE NAVAL EXAMPLES.

TRL	DEFINITION	EXAMPLE (EDO CONTEXT)
TRL 1	Basic principles observed	Novel corrosion-resistant alloy proven in laboratory
TRL 2	Technology concept formulated	Hypothesis for integrating alloy into hull structures
TRL 3	Analytical and experimental proof-of-concept	Coupon tests validating stress performance in relevant environment
TRL 4	Component validation in laboratory	Scale panel fabrication and testing under controlled loads
TRL 5	Component validation in relevant environment	Module integrated into land-based test site with salt-fog exposure
TRL 6	System/subsystem prototype in relevant environment	Full-scale hull section installed on test article or surrogate vessel
TRL 7	System prototype in operational environment	Prototype hull segment installed on operational ship during limited sea trials
TRL 8	Actual system completed and qualified	Final production drawings released, inspections passed for lead ship

Continued on next page

TABLE 4.1: TECHNOLOGY READINESS LEVELS WITH REPRESENTATIVE NAVAL EXAMPLES. (Continued)

TRL	DEFINITION	EXAMPLE (EDO CONTEXT)
TRL 9	Actual system proven in mission operations	Sustained operational deployment meeting performance metrics

Source: USDRE-TRA-2020, USDRE-TRA-2020 [USDRE-TRA-2020]

Hint: Match TRLs to TMRR exit criteria: critical technologies should be $\geq$ TRL 6 before Milestone B.

Note

Operational environment testing typically begins at **TRL 7** (system prototype in an operational environment). **TRL 8** means the actual system is completed and qualified (e.g., qualification/acceptance testing, certifications). **TRL 9** means the actual system is *proven in mission operations* (e.g., successful fleet employment meeting mission metrics).

4.2.10 T&E Organizations and Roles

OSD Director, Operational Test and Evaluation (DOT&E). Independent oversight of operational test adequacy, approves/concurs in TEMP for covered programs, and reports to Congress on operational suitability and effectiveness.

Service Operational Test Agencies. Navy Commander, Operational Test and Evaluation Force (COMOPTEVFOR) (COTF), Air Force Operational Test and Evaluation Center (AFOTEC), U.S. Army Test and Evaluation Command (ATEC), Marine Corps Operational Test and Evaluation Activity (MCOTEA). Plan/execute IOT&E and report independent findings to the Service and DOT&E.

Developmental Test (DT). Program Offices with SYSCOM Warfare Centers (e.g., Naval Air Warfare Center Aircraft Division (NAWCAD), Naval Air Warfare Center Weapons Division (NAWCWD), NSWC, NUWC) plan and run DT to verify requirements, qualify designs, and feed Operational Test Readiness Review (OTRR).

Interoperability/Joint. Joint Interoperability Test Command (JITC) assesses joint interoperability/Net-Ready KPP compliance where applicable.

Ranges/Land-based sites. Service ranges and land-based engineering/test sites provide representative and operational environments to support DT/Operational Test (OT).

Artifacts. TEMP aligns DT/OT scope and phases; OTRR certifies readiness for IOT&E; SAR / DAES capture results for governance [DoDI5000-85].

4.2.11 Major Capability Acquisition Lifecycle Overview

MSA. Shape the trade space and select a preferred materiel solution; conclude with an AoA recommendation and technology maturation plan [DoDI5000-85].

TMRR. Mature technologies, refine requirements, and reduce integration risk to enter EMD; manage competitive prototyping where feasible [DoDI5000-85].

EMD. Complete detailed design, verify system performance, and prepare for production and deployment decisions [DoDI5000-85].

P&D. Produce capability, conduct IOT&E, field initial units, and decide on Full-Rate Production (FRP) [DoDI5000-85].

O&S. Sustain readiness, execute modernization, and plan for disposal while feeding affordability back into PPBE cycles [DoDI5000-85].

Figure 4.5 Shows the major phases, review and decision points within MCAs. The following are the reviews that occur during the phases:

Alternative Systems Review (ASR). Validates the preferred materiel solution and technology maturation approach emerging from the AoA; inputs include threat assessments, cost-schedule trades, draft system concepts, and updated Technology Development Strategy / SEP outlines, and the primary output is an ASR report that authorizes drafting authoritative system-level requirements for the upcoming System Requirements Review (SRR) [DoDI5000-85, DoDAcqGuidebook].

SRR. Confirms that system-level performance, interface, cyber, and logistics requirements trace to the validated ICD / CDD and are testable; requires a draft System Specification, mission threads, interface control documentation, and technical performance measures, and produces a baselined system requirements set and updated verification strategy feeding System Functional Review (SFR) planning [DoDI5000-85, DoDAcqGuidebook].

SFR. Demonstrates that the functional architecture and allocated requirements can satisfy the mission needs within cost/schedule constraints; leverages functional allocation matrices, preliminary hazard analyses, and draft reliability growth plans, and yields an approved functional baseline plus a risk/opportunity burn-down plan ahead of Preliminary Design Review (PDR) [DoDI5000-85, DoDAcqGuidebook].

PDR. Assesses whether the allocated baseline and preliminary design (drawings, models, manufacturability assessments, support concepts) are mature enough to enter detailed design; the review outputs include an approved allocated baseline, configuration-controlled action list, and direction for completing qualification hardware prior to Critical Design Review (CDR) [DoDI5000-85, DoDAcqGuidebook].


CDR. Confirms the detailed design meets all requirements with acceptable technical risk; inputs include product baseline technical data packages, qualification/analysis results, producibility assessments, and cybersecurity artifacts, and the decision produces an approved product baseline plus direction to release build-to packages and procure long-lead items [DoDI5000-85, DoDAcqGuidebook].

Test Readiness Review (TRR). Evaluates readiness to execute a specific test event by reviewing test articles, instrumentation, facilities, procedures, safety releases, and deficiency dispositions; a successful TRR outputs an authorization to start test with documented entrance/exit criteria and risk mitigations [DoDI5000-85, DoDAcqGuidebook].

System Verification Review (SVR). Verifies the integrated system meets the product baseline and is ready for production decision reviews; it uses completed verification cross-reference matrices, configuration audits, and qualification / DT results to produce a verified system baseline, deficiency adjudication list, and recommendation for Full-Rate Production Decision Review (FRPDR) preparation [DoDI5000-85, DoDAcqGuidebook].

OTRR. Certifies that production-representative assets, training, logistics products, safety artifacts, and test ranges are ready to support initial operational test; the review outputs the operational test readiness certification and any restrictions or corrective actions before DOT&E concurrence [DoDI5000-85, DoDAcqGuidebook].

Production Readiness Review (PRR). Determines whether manufacturing processes, supply chain, quality systems, and sustainment enablers can support LRIP / FRP quantities; requires control plans, process capability data, staffing/budget burn rates, and yields a decision to proceed into production along with corrective actions for any shortfalls [DoDI5000-85, DoDAcqGuidebook].

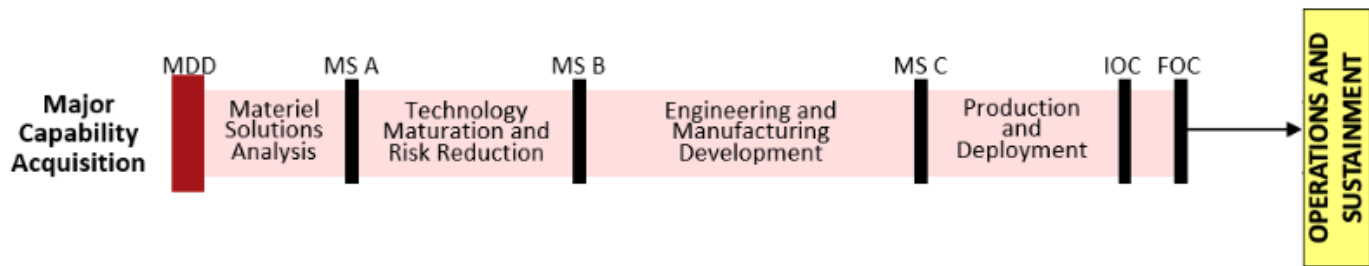

Lifecycle View of Major Capability Acquisition

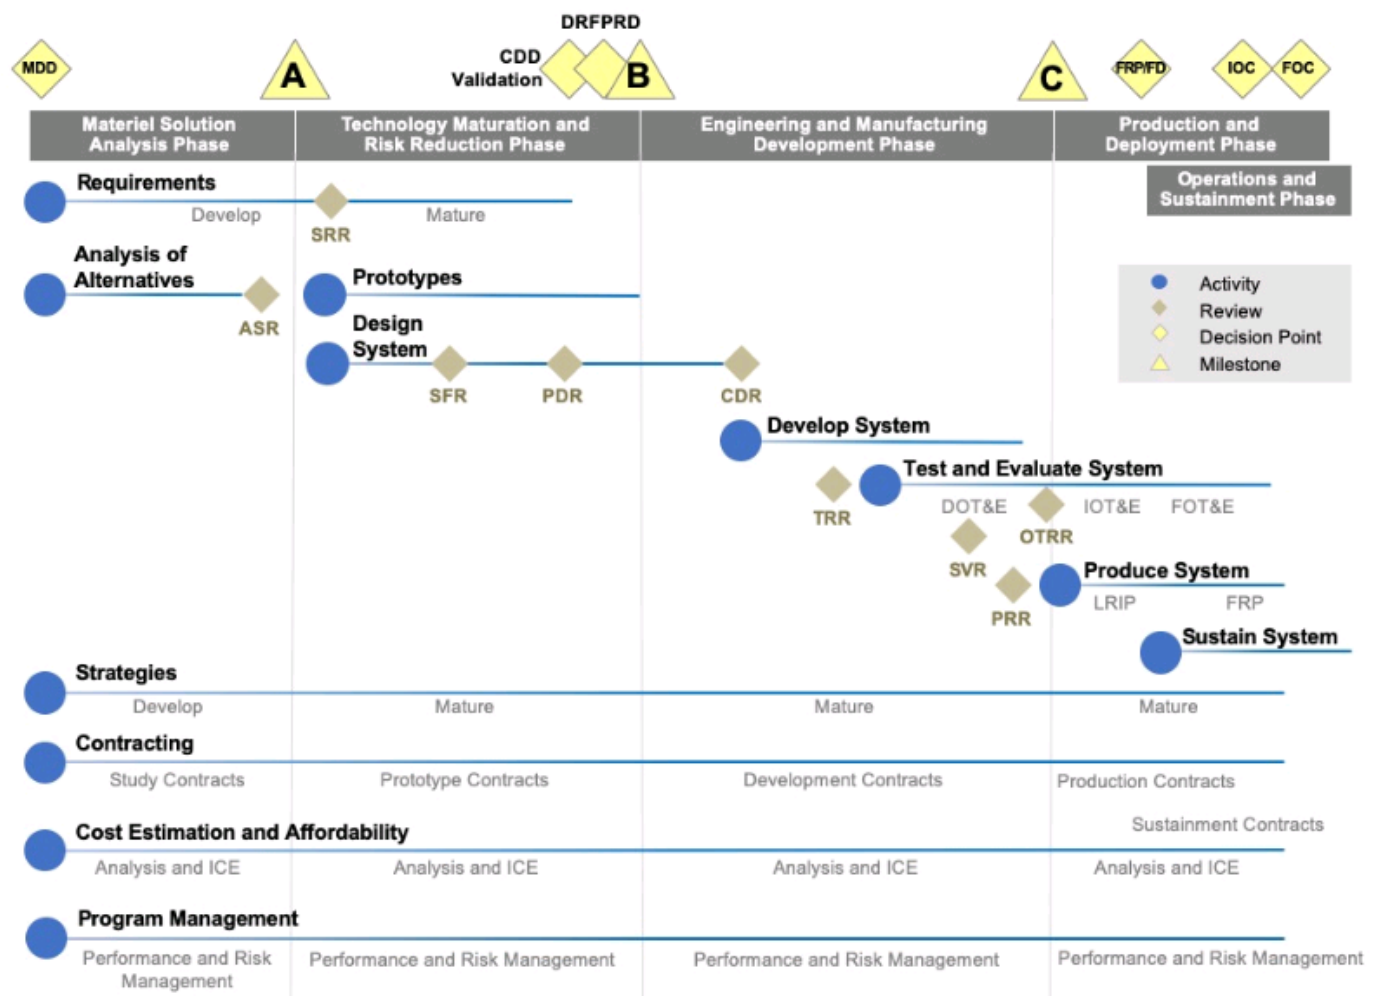


Figure 4.5. Lifecycle view for a MCA showing all functions and activities for each phase. Source: DoDI5000-85, DoDI5000-85 [DoDI5000-85]

4.2.12 Materiel Development Decision

Inputs. Validated ICD, initial affordability analysis, preliminary acquisition strategy, and resource sponsor endorsement [DoDI5000-02].

Decision. MDA authorizes entry into MSA (or an alternate pathway) and designates the lead PEO/PM [DoDI5000-85].

Outputs. Acquisition Decision Memorandum (ADM), competitive AoA guidance, and direction to form the IPT structure [DoDI5000-85].

4.2.13 Materiel Solution Analysis Phase Essentials

Purpose. Analyze alternatives, define the preferred materiel solution, and scope technology maturity and risk reduction tasks [DoDI5000-85].

Key Activities. Conduct AoA, establish initial system performance metrics, develop early test strategies, and plan technology maturation for critical subsystems [DoDI5000-85].

Entrance Criteria. Approved MDD, resourced AoA study guidance, and draft acquisition strategy [DoDI5000-02].

Exit Criteria. Approved TMRR acquisition strategy update, technology risk assessments (i.e., $TRL \geq 3-4$), and draft CDD inputs for Joint staffing [DoDI5000-85].

4.2.14 Milestone A Focus Areas

Purpose. Authorize entry into TMRR and approve the initial Acquisition Strategy and APB [DoDI5000-85].

Board Topics. AoA results, technology maturation plans, affordability caps, cost estimates, and early test strategies [DoDI5000-85].

Outputs. ADM, approved initial APB, direction for competitive prototyping, and signed Technology Development Strategy if required [DoDI5000-85].

4.2.15 Technology Maturation and Risk Reduction Phase Essentials

Purpose. Reduce integration risk, mature the Technical Baseline, and prepare for Engineering & Manufacturing Development source selection [DoDI5000-85].

Key Activities. Competitive prototyping (if directed), systems engineering trade studies, reliability growth, cyber-resilience planning, and Capabilities Development Document Validation (CDD-V) [DoDI5000-85].

Entrance Criteria. Approved Milestone A ADM, funded risk-reduction plan, and established IMS aligned to Navy Gate 5 timeline [DoDI5000-85, OPNAVINST5000-42E].

Exit Criteria. Technology Readiness Assessments showing $TRL \geq 6$, draft Milestone B documentation (e.g., SEP, TEMP), and configured product baseline ready for the Development Request for Proposal Release Decision (DRFPRD) [DoDI5000-85].

4.2.16 Milestone B Focus Areas

Purpose. Authorize entry into EMD and establish the program as a major defense acquisition program with formal reporting [DoDI5000-85].

Board Topics. Affordability caps, independent cost estimates, TEMP approval, LRIP planning, and production-representative prototype evidence [DoDI5000-85].

Outputs. Updated APB, approved Acquisition Strategy revision, and contractual authority to release EMD RFPs [DoDI5000-85].

4.2.17 Engineering and Manufacturing Development Phase Essentials

Purpose. Complete detailed design, build and test engineering development models, and validate manufacturing processes [DoDI5000-85].

Key Activities. CDR, system verification, developmental test events, cybersecurity accreditations, and sustainment baseline development [DoDI5000-85].

Entrance Criteria. Approved Milestone B ADM with resourced contracts, finalized technical baseline, and product-support planning aligned to Navy Gate 6 [DoDI5000-85].

Exit Criteria. Successful IOT&E readiness, manufacturing readiness $\geq$ TRL 8, and validated sustainment strategies supporting Milestone C [DoDI5000-85].

4.2.18 Milestone C Focus Areas

Purpose. Authorize production and deployment following demonstration of operational effectiveness and suitability [DoDI5000-85].

Board Topics. IOT&E results, sustainment and supply-chain readiness, affordability assessments, and updated manpower/-training plans [DoDI5000-85].

Outputs. FRPDR plan, updated APB, and authority to obligate procurement funding for production lots [DoDI5000-85].

4.2.19 Production and Deployment Phase Essentials

Purpose. Produce and deliver the system while validating operational performance and support concepts [DoDI5000-85].

Key Activities. LRIP execution, IOT&E, Configuration Steering Board (CSB) governance, and ramp to Full-Rate Production [DoDI5000-85].

Exit Criteria. FRP approval, attainment of Initial Operational Capability (IOC), and sustainment plans ready for fleet release [DoDI5000-85].

4.2.20 Operations and Support Phase Essentials

Purpose. Sustain mission effectiveness, execute modernization, and manage total ownership cost until disposal [DoDI5000-85].

Key Activities. Performance-Based Logistics execution, Depot maintenance planning, Post-Deployment reviews, and CSBs for major updates [DoDI5000-85].

Milestones. Full Operational Capability (FOC), disposal decision documentation, and updates to capability requirements feeding future planning cycles [DoDI5000-85].

5 Requirements

5.1 Joint Capabilities Integration & Development System

Refs:

5.1.1 Requirements Demand Versus Acquisition Supply

Joint Capabilities Integration and Development System (JCIDS). Establishes the joint demand signal by translating strategic guidance into validated capability requirements, risk statements, and Doctrine, Organization, Training, Materiel, Leadership and Education, Personnel, Facilities, and Policy (DOTMLPF-P) change recommendations that scope non-materiel and materiel options [jcids-manual-2021, edo-3-3-3-jcids-2025].

DAS. Converts validated requirements into executable acquisition strategies, cost/schedule baselines, and lifecycle sustainment plans under DoDD 5000.01 and DoDI 5000.85 [DoDD5000-01, DoDI5000-85].

Note

Board cue: be ready to explain where a program sits in both systems; Gate 2 packages are dead on arrival if the JCIDS paperwork is stale even when the DAS strategy is current [edo-3-3-3-jcids-2025].

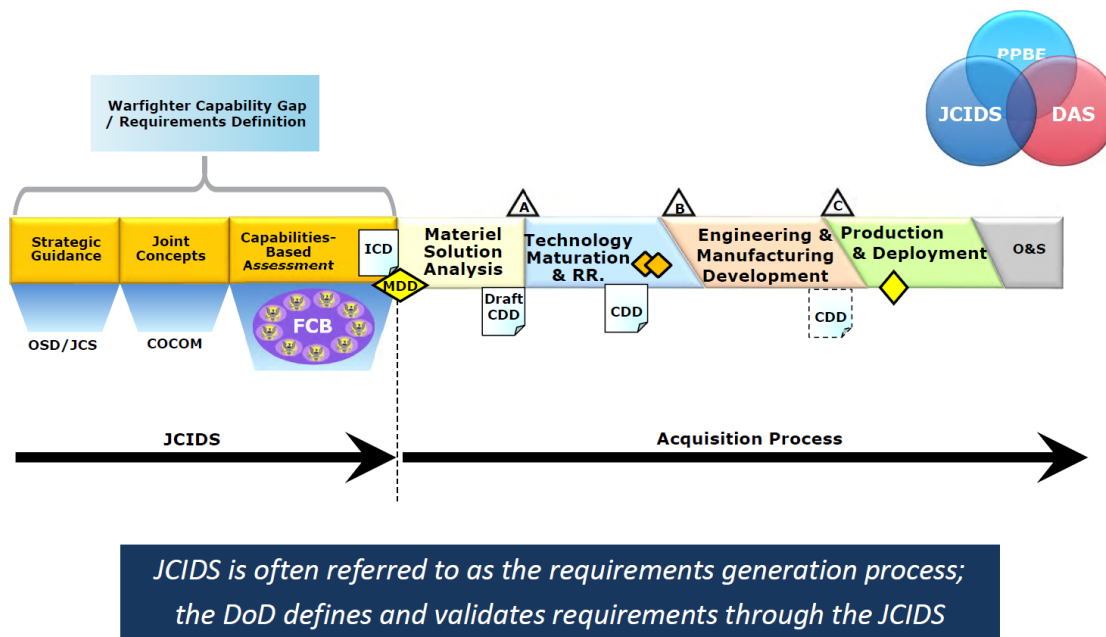


Figure 5.1. Relationship between the Joint Capabilities Integration and Development System and the Defense Acquisition System.

Source: edo-3-3-3-jcids-2025, edo-3-3-3-jcids-2025 [edo-3-3-3-jcids-2025]

5.1.2 Capability Requirements and the Capability-Based Assessment Cadence

Capability requirements are mission-task statements (task, condition, standard) that are solution-agnostic yet measurable enough to drive trades, and Capability-Based Assessments (CBAs) provide the disciplined analysis to justify them [jcids-manual-2021]. Each CBA follows repeatable phases:

Study initiation. The sponsoring component issues the study notice, nominates a lead Functional Capabilities Board (FCB), scopes timelines, and aligns analytical support and governance expectations [jcids-manual-2021].

Operational context & mission threads. Analysts decompose national / Combatant Command (CCMD) guidance into joint concepts, mission threads, and integrated architectures to keep the study “concept-based and threat-informed” [jcids-manual-2021].

Gap and risk assessment. Existing and programmed capabilities are mapped against required mission effects to quantify gaps, assess risk, and prioritize by warfighting impact and threat timelines [jcids-manual-2021].

Solution analysis. DOTMLPF-P are explored first; only when risk remains unacceptable are materiel approaches carried forward, together with preliminary affordability bounds and schedule realism [jcids-manual-2021].

Documentation & validation path. The resulting evidence package (mission context, gaps, DOTMLPF-P recommendations, risk, and proposed documents) feeds the Gatekeeper, FCB, and validation authority decision on which JCIDS artifact (ICD, DOTMLPF-P Change Recommendation (DCR), update) to staff [jcids-manual-2021].



Figure 5.2. Concept-to-requirement flow that must stay synchronized with acquisition execution.

Source: edo-3-3-3-jcids-2025, edo-3-3-3-jcids-2025 [edo-3-3-3-jcids-2025].

5.1.3 Strategy-to-Requirement Synchronization

Joint demand starts with strategic direction (National Defense Strategy, Joint Warfighting Concept, campaign orders) and is progressively tailored until a validated requirement enters the DAS [jcids-manual-2021, edo-3-3-3-jcids-2025]. Key touchpoints:

Strategic guidance. SECDEF and CJCS translate national objectives into force design problems and assign lead sponsors; the Joint Staff J-7 houses concept development and readiness assessments that set the analytical agenda [jcids-manual-2021].

Joint concepts & mission threads. Mission engineers decompose guidance into mission areas, integrated kill chains, and threat-informed architectures so that requirements stay “concept-based and threat-informed” before solutioneering [jcids-manual-2021].

CBAs. Sponsors conduct the structured CBA described above to document measurable capability requirements, prioritize risks, and recommend DOTMLPF-P levers with quantitative evidence [jcids-manual-2021].

Gatekeeping & staffing. The Joint Staff Gatekeeper assigns a Joint Staffing Designator (JSD), routes packages through Knowledge Management and Decision Support (KM/DS), and tasks the appropriate FCB for certification prep; timelines and suspense assignments live inside KM/DS so Navy leads can monitor in real time [jcids-manual-2021].

Validation. Depending on the JSD, the JROC, Joint Capabilities Board (JCB), or delegated Service/CCMD authority validates requirements, issues memoranda Joint Requirements Oversight Council Memorandums (JROCMs), and records mandatory actions (e.g., certifications, follow-on DCRs) that acquisition teams must honor [jcids-manual-2021, USC-10-181].

Acquisition handoff. Validated artifacts, with their JROCM direction and Capability Trade Council (CTC) or CSB trade expectations, become entry criteria for Gate 2, the MDD, and milestone reviews, ensuring the PAE and PEO communities inherit coherent demand signals [edo-3-3-3-jcids-2025].

5.1.4 Major Capability Acquisition Requirement Set

ICD. Captures the operational context, quantified gaps, and risk that justify materiel and non-materiel approaches; it is required to support the Materiel Development Decision and is deliberately solution-agnostic [jcids-manual-2021].

CDD. Establishes system-level performance attributes (KPPs, KSAs, Additional Performance Attributes (APAs)) that anchor TMRR planning and must be validated before the Development RFP release and Milestone B; it becomes the authoritative source for the Technical Requirements Baseline [jcids-manual-2021, DoDI5000-85].

CDD updates. Refine thresholds/objectives when an EMD phase spans multiple lots or when KPPs trades are needed before Milestone C; updates keep production-representative values authoritative without re-opening earlier portions of the document [jcids-manual-2021].

CPD. Translates the validated CDD into production-ready parameters, sustainment metrics, and deployment considerations for Milestone C and Full-Rate Production/Fielding decisions [jcids-manual-2021, DoDI5000-85].

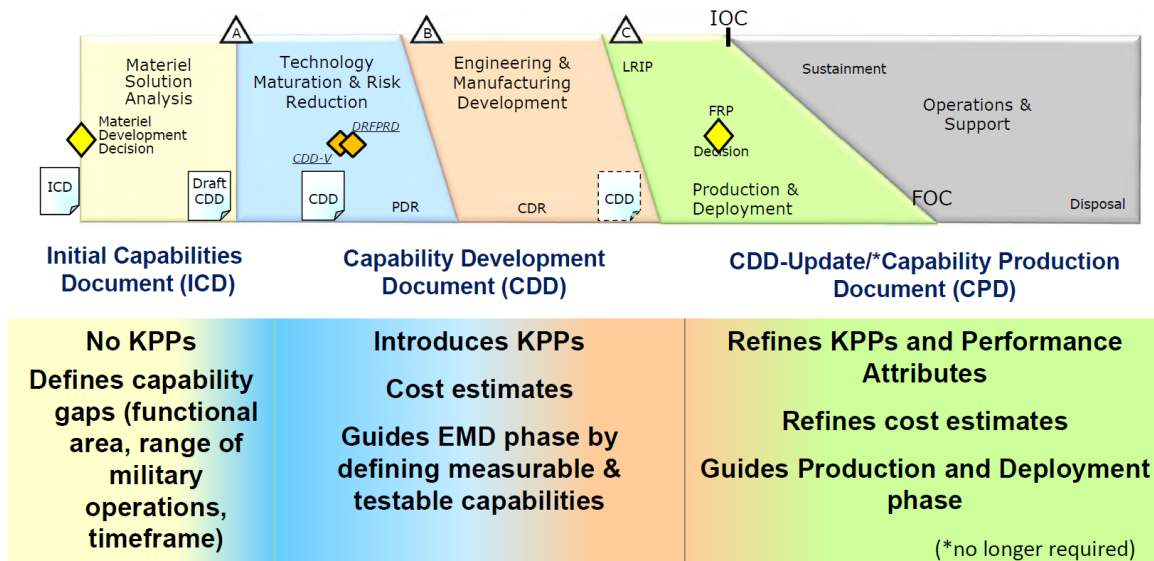


Figure 5.3. Placement of Joint Capabilities Integration and Development System artifacts inside the phased Major Capability Acquisition pathway.
Source: edo-3-3-3-jcids-2025, edo-3-3-3-jcids-2025 [edo-3-3-3-jcids-2025].

5.1.5 How KPPs Stay Integrated with DAS

Validated KPPs define the trade space that Milestone Decision Authorities use to approve baselines, certifications, and contracts. DoDI 5000.85 requires KPP ownership to be traceable from the CDD into the System Requirements Review, Developmental Test plans, and Acquisition Program Baseline; breaches trigger Gatekeeper tripwire reviews and Configuration Steering Boards [DoDI5000-85, jcids-manual-2021]. Navy PMs must therefore align CDD/CPD updates with SEA 05 warrant packages and ASN(RD&A) Gate 6 readiness to keep statutory certifications (Net-Ready (NR)-KPP, cybersecurity, safety) synchronized [OPNAVINST5000-42E, edo-3-3-3-jcids-2025].

5.1.6 Prioritizing Materiel and Non-Materiel Solutions

JCIDS policy directs sponsors to work through every DOTMLPF-P lever before defaulting to expensive materiel approaches, both to reduce risk and to speed delivery [jcids-manual-2021]. Practical applications include:

Doctrine. Update joint/combined warfighting concepts or tactics to mitigate gaps quickly (e.g., change Anti-Submarine Warfare (ASW) Concept of Operations (CONOPS) before buying sensors).

Organization. Re-align Fleet/NAVWAR command relationships or mission tailoring to close gaps without new hardware.

- Training.** Modify Fleet Readiness Training Plan events or simulator syllabi so crews can exploit existing systems better.
- Material.** Only after non-material levers fail should new material increments be scoped, with clear linkage to DAS milestones.
- Leadership.** Insert leadership development or acquisition workforce upskilling when governance bottlenecks (e.g., JROC literacy) create the gap.
- Personnel.** Adjust billets, Navy Enlisted Classifications, or civilian skill codes to align manpower with capability employment.
- Facilities.** Invest in pier-side infrastructure, cyber ranges, or test venues necessary to realize capability performance.
- Policy.** Seek changes to SECNAV/OPNAV directives or coalition agreements when authorities constrain capability delivery.

5.1.7 Governance Roles and Validation Chain

- JROC.** Executes Title 10 § 181 duties—prioritizing capability gaps, validating KPPs, delegating authority, and issuing JROCM guidance that binds both requirements and acquisition communities [jcids-manual-2021, USC-10-181].
- Joint Staff Gatekeeper & JCB.** The J-8 Gatekeeper screens every submission, assigns Joint Staff suspense, and recommends whether the JROC or JCB (chaired by the VCJCS) is the right validation venue; the JCB focuses on issues that are joint but lower risk, accelerating queue time for most Navy programs [jcids-manual-2021].
- FCBs.** Functional Capabilities Boards (e.g., C4/Cyber, Protection, Logistics) chair working groups, broker certifications (Net-Ready, Force Protection, System Survivability), monitor implementation of DCRs tasks, and elevate tripwires to the JCB/JROC [jcids-manual-2021].
- Service validation authorities.** OPNAV N9/N9I act as the Navy Gatekeeper, ensuring Gate 0/1 packages satisfy OPNAVINST 5000.42E expectations before forwarding to the Joint Staff, and they remain responsible for Service-specific “Joint Integration” decisions even when joint validation is delegated [OPNAVINST5000-42E].

Requirements are therefore validated either by the JROC, the JCB (if delegated), or by the cognizant Service/CCMD authority when the Joint Staff assigns a Joint Staffing Designator of “Joint Integration/Information” [jcids-manual-2021].

5.1.8 IT, C4I, and Coalition Interoperability Implications

- Net-Ready.** Every Information System (IS) ICD, IS CDD, and Capability Drop version of the CDD must secure Net-Ready certification from the C4/Cyber FCB chair, demonstrating compliance with enterprise architecture, data standards, and mission thread-level interoperability [jcids-manual-2021].
- Architecture and reuse.** Sponsors must deliver Department of War Architecture Framework (DoDAF) views (All Viewpoint (AV), Operational Viewpoint (OV), Systems Viewpoint (SV), Capability Viewpoint (CV)) that trace requirements to reusable services, Application Programming Interfaces (APIs), and data models, enabling software pathways and rapid iteration [jcids-manual-2021, DoDI5000-02].

C4I interoperability. DoDD 5000.01 compels all acquisition programs to plan for cross-Service and allied interoperability; JCIDS enforces this by requiring coalition releasability considerations and Combined/Joint Mission Threads inside every requirement [DoDD5000-01].

Allied impacts. Capability sponsors must document how U.S. and allied systems exchange data, share bandwidth, and remain cyber survivable before validation; failure to do so can halt Gate 2 or Net-Ready KPPs endorsements [jcids-manual-2021, edo-3-3-3-jcids-2025].

5.1.9 Warfighting Acquisition System (JCIDS Replacement)

SECWAR's 7–10 Nov 2025 memoranda and Acquisition Transformation Strategy direct the Department to replace legacy JCIDS paperwork with the Warfighting Acquisition System (WAS), an enterprise approach built on Capability Portfolio Management (Capability Portfolio Management (CPM)) and Capability Trade Councils that keep requirements, resourcing, and acquisition synchronized [secwar-was-memo-2025, secwar-acq-transformation-2025].

Key Operational Problems.

The JROC now publishes a short list of KOPs—problem statements tied to the National Defense Strategy—and stops validating Service-level CDDs except where statute forces it, returning day-to-day authority to the Services [secwar-jcids-reform-2025].

Mission Engineering & Integration Activity.

USW(R&E) and USW(A&S) created the MEIA to run rapid experiments, collect live data, and produce mission-thread analyses that replace lengthy JCIDS studies before resource decisions are made [secwar-jcids-reform-2025, secwar-was-memo-2025].

Requirements & Resourcing Alignment Board.

The new RRAB, co-chaired by the DepSecWar and VCJCS, aligns each prioritized KOP with PPBE guidance, reallocations, and Joint Acceleration Reserve decisions inside the same budget cycle so validated needs show up in the FYDP immediately [secwar-jcids-reform-2025].

Joint Acceleration Reserve.

The JAR is a centrally managed pool that bridges the “valley of death” by funding promising prototypes or industrial-base surges between POM builds; RRAB recommendations trigger its use when a KOP solution proves viable [secwar-jcids-reform-2025].

Inputs.

Mission-thread data, kill-chain metrics, threat assessments, PPBE affordability guidance, experimentation results, and digital engineering artifacts flow into each CPM cell so that operational problems are quantified before trades begin [secwar-acq-transformation-2025].

Core events.

The DepSecWar and Vice Chairman convene quarterly CPM reviews; PAEs call Capability Trade Councils whenever trades exceed delegated cost/schedule/performance thresholds; unresolved items elevate to the Deputies Management Action Group [secwar-acq-transformation-2025].

Outputs.

Portfolio scorecards, capability roadmaps, trade memoranda, and data packages that substitute for the ICD/CD-D/CPD sequence while still feeding Program Decision Memoranda, issue papers, and Acquisition Program Baselines [secwar-acq-transformation-2025].

Key players.

DepSecWar, VCJCS, USW(A&S), USW(R&E), USW(C), PAEs, and functional analytics teams replace the traditional Gatekeeper/FCB/JROC staffing chain; Capability Trade Councils provide the audit trail for requirement changes [secwar-acq-transformation-2025].

Integration with PPBE and the DAS.

The strategy instructs USW(C) and USW(A&S) to budget and execute at the portfolio level, letting PAEs move resources inside those controls while simultaneously updating APBs and milestone documentation when trades occur [secwar-acq-transformation-2025].

Differences from JCIDS.

WAS relies on live data and executive accountability instead of protracted document staffing, collapses requirements/re-sourcing/acquisition touchpoints, and uses Capability Trade Councils in lieu of formal Configuration Steering Boards [secwar-acq-transformation-2025].

Legislative status.

The strategy is policy guidance pending FY 2026 NDAA language; during FY 2025 the Department is executing pilot portfolios (munitions industrial base, Project Overmatch) under DepSecWar memoranda while still producing any JCIDS artifacts explicitly mandated by statute [secwar-acq-transformation-2025].

5.1.10 What EDOs Must Master Under WAS

Time-based metrics.

Portfolio scorecards now track median days from KOP identification to MDD/IOC; EDOs must baseline their programs against those targets and be ready to discuss what trades are required to shrink the timeline [secwar-was-memo-2025].

Capability Trade Councils.

Expect recurring requests to convene or support these councils with mission-thread data, digital models, and industrial-base options so that requirement, schedule, and cost trades are justified without defaulting to a JROC package [secwar-acq-transformation-2025].

Experiment-to-budget pipeline.

Because MEIA experimentation outputs feed the RRAB, EDOs must deliver credible prototype results (with cost/sustainment implications) fast enough to influence the same PPBE build; missing the window means losing JAR opportunities [secwar-jcids-reform-2025].

Security cooperation touchpoints.

DSCA/DTSA realignment under USW(A&S) means exportability, tech-release, and allied production plans are now discussed alongside Capability Trade Councils—EDO briefs should cover how security cooperation choices affect industrial-base capacity and delivery risk [secwar-arms-transfer-2025].

5.1.11 Current Events: SECWAR Acquisition Transformation Strategy

SECWAR's 10 Nov 2025 Acquisition Transformation Strategy directs the Warfighting Acquisition System to eliminate legacy JCIDS bureaucracy, convert Configuration Steering Boards into CTCs, and empower PAEs to make requirements trades inside cost/schedule thresholds [secwar-acq-transformation-2025]. The memo explicitly calls for JCIDS elimination and streamlining of DAS reviews, meaning Navy teams must plan for near-term transition periods where PAEs convene CTCs to validate trades in lieu of traditional Joint Staff staffing, while DAS documentation is simultaneously pushed to lower approval levels [secwar-acq-transformation-2025]. Expect joint governance updates (Gatekeeper rules, FCB charters) and plan to capture trade rationales in Decision Memoranda so that future auditors can trace how requirements changes affected APBs.

5.2 Test & Evaluation

Refs:

5.2.1 Board Prep Summary

Test and Evaluation (T&E) provides the objective evidence that a system can achieve the warfighter outcomes promised in requirements documents before obligating the fleet to fielding, sustainment, and congressional reporting commitments [edo-3-5-5-test-eval-part-i-2025, DoDI5000-85]. A test is the controlled activity (lab, range, digital thread, fleet event) that produces data, while an evaluation is the analytic judgment that compares that data to thresholds, suitability expectations, and risk acceptance criteria [edo-3-5-5-test-eval-part-i-2025]. Effective T&E integrates developmental, operational, and live-fire evidence so that each MCA milestone is backed by verified design data and validated mission performance insights rather than optimistic modeling alone [DoDI5000-89]. Programs that synchronize T&E with systems engineering and program control expose performance gaps early, recycle fixes through the technical baselines, and enter OTRR with a defensible TEMP, resource plan, and deficiency scrub.

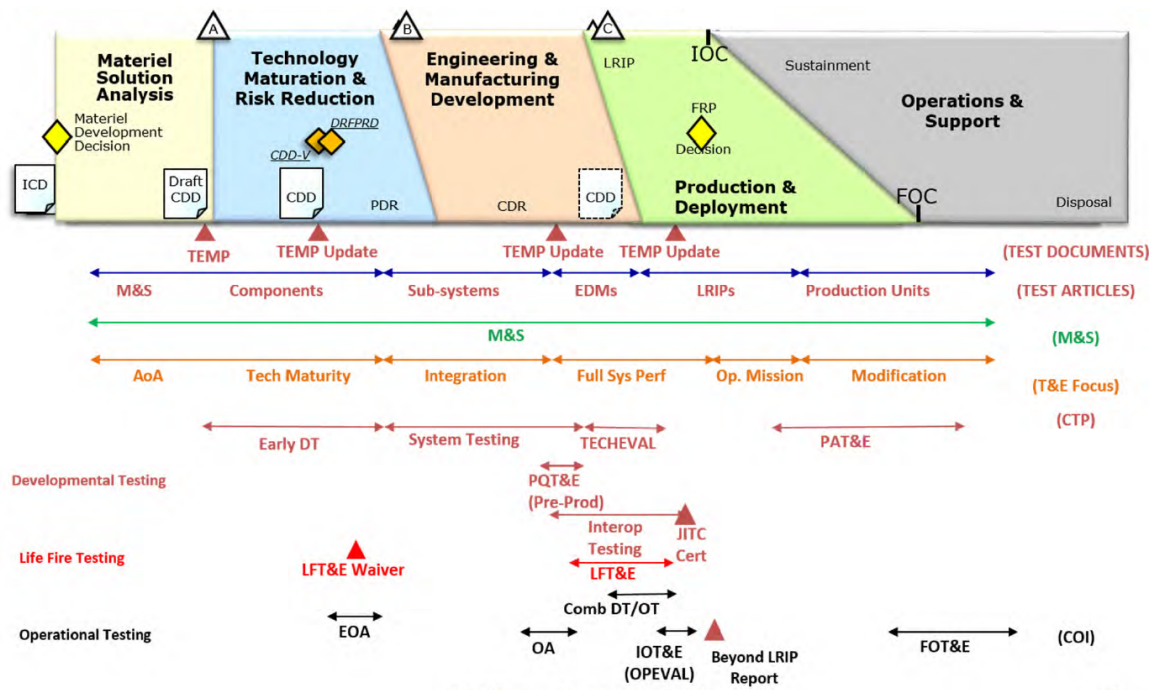


Figure 5.4. Key MCA test and evaluation touchpoints that frame DT, OT, and certification decisions.

Source: edo-3-5-5-test-eval-part-i-2025, edo-3-5-5-test-eval-part-i-2025 [edo-3-5-5-test-eval-part-i-2025].

5.2.2 Definition and Relationship to Verification and Validation

Developmental Test and Evaluation (DT&E) verifies “did we build the system right” by showing the technical baseline meets allocated requirements, standards, and interface controls, while Operational Test and Evaluation (OT&E) validates “did we build the right capability” by proving Sailors and Marines can accomplish missions under representative threat, environment, and sustainment conditions [DoDI5000-02]. Verification relies on repeatable measurements (e.g., propulsion plant efficiency in a land-based engineering site) and feeds configuration control; validation uses operational scenarios, tactics, and logistics supportability to demonstrate mission effectiveness and suitability. DoDI 5000.88 further directs programs to execute frequent, iterative end-user validation of features and usability so mission thread owners can accept the delivered capability before major decisions [DoDI5000-88]. Verification and Validation (V&V) and Verification, Validation, and Accreditation (VV&A) activities must be planned in the TEMP and SEP so that models, simulations, hardware-in-the-loop facilities, and live events share common data assumptions and confidence levels before milestone reviews [DoDI5000-89]. *Verification* therefore proves compliance with the documented specification (analysis, inspection, test, demonstration), whereas *validation* proves the warfighter accepts the delivered capability and can close the mission threads; both sides of the V&V matrix must be satisfied before the MDA can certify readiness for production or fleet release [DoDI5000-89].

5.2.3 Statutory Requirements and Key Roles

10 U.S.C. § 139. Establishes the DOT&E as an independent advisor to SECWAR and Congress; DOT&E approves operational test plans, monitors execution, and must issue a public report for covered programs [USC-10-139].

10 U.S.C. § 2399. Prohibits a program from proceeding beyond LRIP or requesting Full-Rate Production approval until DOT&E and the lead Operational Test Agency submit their independent reports to Congress [USC-10-2399].

10 U.S.C. § 2366. Requires Live Fire Test and Evaluation (LFT&E) or an approved waiver for covered systems (personnel, platform, and munitions lethality/survivability) before beyond-LRIP decisions; it also directs reporting of vulnerability/lethality findings to defense committees [USC-10-2366].

Deputy Assistant Secretary of War for Test and Evaluation (DASW(T&E)). Serves as the OSD focal point for test resources, designates Chief Developmental Testers (CDTs) for ACAT I programs, charts Lead Developmental Test and Evaluation Organizations (LDTOs), and co-chairs Defense-level T&E Working Integrated Product Teams [DoDI5000-89].

CDT and LDTO. The CDT orchestrates the integrated test schedule, data requirements, and deficiency resolution cadence, while the LDTO (often a warfare center or system command test directorate) furnishes instrumentation, modeling, and range execution authority for DT&E [DoDI5000-89].

Operational Test Agencies. COMOPTEVFOR, AFOTEC, ATEC, and MCOTEA plan and execute OT&E Missile Defense Agency (MDA) record [edo-3-5-6-test-eval-part-ii-2025].

TODO: Insert DoW-wide test and evaluation organization graphic (OSD DOT&E, DASD(T&E), Service OTAs, warfare centers).

Figure 5.5. Notional DoW test and evaluation governance chain.

5.2.4 Developmental Test Activities

Component and qualification testing. Bench, lab, and land-based engineering site events that verify materials, software builds, cyber hardening, interoperability, and safety factors before integration; data feeds configuration audits and reliability growth curves [edo-3-5-5-test-eval-part-i-2025].

Subsystem and integration testing. Hardware-in-the-loop, systems integration labs, and shore-based platform integration tests that expose interface defects and mission thread timing issues before at-sea trials [edo-3-5-5-test-eval-part-i-2025].

System-level DT&E. Full-up prototypes or first-of-class hulls execute combined developmental/operational scenarios, cybersecurity assessments, and logistics demonstrations to validate readiness for TRR and Technical Evaluation (TECHEVAL) [DoDI5000-85].

Reliability growth and maintainability demonstrations. Planned stress events and failure-mode tracking prove that Mean Time Between Operational Mission Failure (MTBOMF) and corrective maintenance timelines align with sustainment strategies before Operational Test Readiness [DoDI5000-89].

Certification testing. Airworthiness, safety, information assurance, weapon certification, and electromagnetic environmental effects tests that deliver statutory certifications needed for fielding [edo-3-5-5-test-eval-part-i-2025].

Note

Edge case: Software pathway efforts may collapse TECHEVAL/Operational Evaluation (OPEVAL) into continuous DevSecOps assessments, but the program must still show how combined testing and user evaluations satisfy Title 10 adequacy requirements before fielding [DoDI5000-02].

5.2.5 Live Fire Test and Evaluation

When required.

Title 10 demands LFT&E for every new or significantly upgraded crew-occupied platform, combat vehicle, major munitions program, or missile defense component that will face threat lethality; full-up system-level shots must be realistically stressed prior to requesting Full-Rate Production approval [USC-10-2366, DoDI5000-89].

When waived.

Only the SECWAR can waive full-up LFT&E when the system is unmanned, when destructive testing would be unreasonably expensive or impractical, or when alternative testing (component shots, validated modeling, allied data) provides equivalent insights; Congress must be notified of the rationale and the alternative plan [USC-10-2366, DoDI5000-89].

Execution and use.

Programs plan vulnerability and lethality events in the TEMP, employ full-up articles plus critical subsystems and surrogates, and collect battle damage, crew survivability, and cascading-effect data to inform design hardening, tactics, and survivability equipment upgrades; the results become an annex to the DOT&E report before the FRPDR [DoDI5000-89, DoDI5000-85].

5.2.6 Operational Test Phases

Early Operational Assessment (EOA). A qualitative review, often using simulations or limited field events, that informs CDD refinement and acquisition strategy decisions before Milestone B [edo-3-5-6-test-eval-part-ii-2025].

Operational Assessment (OA). Focused operational events (sometimes embedded in Fleet Battle Problems or Fleet Exercises) that characterize mission effectiveness, training load, and logistics demands prior to LRIP or dedicated IOT&E [edo-3-5-6-test-eval-part-ii-2025].

Initial Operational Test and Readiness Evaluation (IOT&RE). Navy programs often combine IOT&E and Readiness Evaluation to prove both mission performance and Fleet introduction readiness; Title 10 requires that the IOT&E portion be adequate, realistic, and reported to Congress before FRP [USC-10-2399].

Follow-on Operational Test and Evaluation (FOT&E). Conducted after FRP or major configuration changes to verify corrective actions, CPD thresholds, cybersecurity resilience, and software drops prior to wide deployment [DoDI5000-89].

5.2.7 Fundamental Test and Evaluation Terms

Critical Operational Issue (COI). The mission-outcome questions (“Can the ship defend itself against a raid?”) that structure OT&E plans and reports [edo-3-5-6-test-eval-part-ii-2025].

Measure of Effectiveness (MOE) & Measure of Suitability (MOS). Measures of Effectiveness and Suitability quantify warfighting value (probability of raid annihilation) and fleet readiness attributes (reliability, maintainability, training burden) tied to COIs [edo-3-5-6-test-eval-part-ii-2025].

Measure of Performance (MOP). Measures of Performance (e.g., radar detection range) show lower-level technical behaviors that roll up to MOEs/MOS [edo-3-5-5-test-eval-part-i-2025].

Deficiency categories. Category I deficiencies are mission-critical failures that could cause death, severe injury, or major mission loss; Category II items are significant but less critical issues requiring tracking and correction [edo-3-5-6-test-eval-part-ii-2025].

Combined testing. Planned events that collect developmental and operational data simultaneously to save schedule and align datasets for evaluation teams [DoDI5000-02].

5.2.8 Critical Technical Parameters and Technical Performance Measures

Critical Technical Parameters (CTPs) are the small subset of design attributes that must be controlled to assure a KKPP or KSA remains achievable; they are derived from the ICD/CDD and baselined inside the APB [DoDI5000-85]. Each CTP maps to one or more Technical Performance Measures (TPMs) that engineers track continuously using lab data, digital models, or DT&E results; TPMs trends highlight when technical debt threatens TEMP and SEP assumptions so leadership can adjust scope, schedule, or funding. Programs are expected to show a clean trace from COI → KPP/KSA → CTP → TPM → planned test points in the TEMP, ensuring every test objective underwrites an operational outcome and every requirement has an observable verification method [DoDI5000-89, edo-3-5-5-test-eval-part-i-2025].

5.2.9 Test and Evaluation Master Plan

The TEMP captures the integrated T&E strategy, schedule, resources, and data management approach across the lifecycle; it harmonizes the SEP, LCSP, and APB so that every milestone package shows how risk will be retired [DoDAcqGuidebook]. Part I summarizes program context and key performance requirements, Part II defines the integrated test program (DT, OT, certification, modeling, and analysis), Part III outlines resource needs (ranges, threat surrogates, workforce, instrumentation), and annexes address data rights, stats, and cyber accreditation [DoDI5000-89]. ACAT ID TEMPs require DOT&E approval; other TEMPs are approved by the Component Acquisition Executive. Updates are mandatory when requirements change, critical deficiencies emerge, or significant schedule/funding revisions alter test sequencing [DoDI5000-85].

5.2.10 Modeling and Simulation

Modeling and simulation provide the only practical way to explore the mission design space before hardware exists, rehearse high-risk scenarios (e.g., hypersonic raid defense), and extend sparse live-test data across the operational envelope [edo-3-5-5-test-eval-part-i-2025]. Programs must document model purpose, pedigree, uncertainty, and VV&A status in the TEMP; accredited models can bound live-test needs, size instrumentation, and support decision-quality evaluations when safety, cost, or treaties limit destructive testing [DoDI5000-89]. Mission engineering digital threads (system-of-systems simulations, campaign models) allow combined DT/OT teams to choreograph events, align data management plans, and feed statistical confidence calculations before and after live events.

5.2.11 Navy Overlays and Integration

OPNAVINST 3960-series policy (captured in the coursebook) requires Navy programs to plan TECHEVAL (led by the engineering agent) before OPEVAL, to obtain OPNAV N94/N9 concurrence on test objectives that bear on Fleet introduction risk, and to route OTRR packages through COMOPTEVFOR for certification that logistics, training, and safety enablers are in place [edo-3-5-6-test-eval-part-ii-2025]. First-of-class ships also execute Builder's and Acceptance Trials, INSURV events, and dedicated combat system Ship Qualification Trials that integrate with TECHEVAL/OPEVAL data packages. Navy Commander, Operational Test Force (COTF) retains authority to recommend restricted Fleet release if Cat I deficiencies remain; those actions feed the Key Roles appendix update for DASW(T&E), CDT, and COTF responsibilities.

5.2.12 Fiscal and PPBE Touchpoints

RDT&E appropriations fund most DT&E events, test articles, range time, and contractor support, while procurement colors such as SCN or Weapons Procurement, Navy buy dedicated OT assets when production-representative hardware is required for statutory adequacy [DoDFMR-Vol3, edo-3-5-5-test-eval-part-i-2025]. Operations and Maintenance funds cover Fleet participation, temporary duty, and sustainment of government test ranges. Because OT adequacy is a precondition for FRP and sustainment decisions, Program Objective Memorandum issue papers must protect test range modernization, threat-representative targets, and Modeling & Simulation accreditation costs or risk a PPBE disconnect when COMOPTEVFOR identifies unfunded test objectives.

5.2.13 Assumptions and Uncertainties

- Coursebook Modules 3.5.5 and 3.5.6 (March 2025 editions) remain the latest DON-specific T&E references.
 - COMOPTEVFOR manual updates post-2024 were not available offline; Navy-specific terminology (e.g., OPEVAL taxonomy) is based on coursebook guidance.
 - Upcoming NDAA changes to Title 10 T&E statutes have not been incorporated pending official publication.
-

6 Maintenance

6.1 Fleet Maintenance Assets

Refs:

6.1.1 Echeloned Maintenance Levels

Organizational-level. Ship’s force keeps the hull, mechanical, and electrical plants safe and combat-ready by executing preventative checks, battle damage control, and light repairs with organic tools, allowing the platform to remain as self-sufficient as possible while deployed [OPNAVINST4700-7M, edo-4-1-1-fleet-maint-assets-2025].

Intermediate-level. Intermediate Maintenance Activitys (IMAs) and tenders augment the crew with certified artisans (e.g., welders, riggers, calibration labs) who can disassemble components, correct corrosion, and return equipment to specification without docking the ship; Navy Afloat Maintenance Training Strategy (NAMTS) builds those Navy Enlisted Classifications (NECs), and so strike groups can recover faster when forward [OPNAVINST4700-7M, edo-4-1-1-fleet-maint-assets-2025].

Depot-level. Naval Shipyards (NSYs), private yards, and SUPSHIPs conduct heavy industrial work such as reactor refueling, shaft and underwater body repairs, and major modernizations that exceed shipboard capability; every task is tied to the Class Maintenance Plan (CMP) and engineered work instructions [NAVSEAINST5450-14D, NAVSEAINST5450-145A, edo-4-1-1-fleet-maint-assets-2025].

Note

Board cue: reference at least one example task in each echelon (e.g., IMA balancing pump rotors vs. depot replacement of a main reduction gear) to show command of maintenance depth.

6.1.2 Shore Maintenance Organizations and Roles

NSYs. Public yards (e.g., Norfolk, Pearl Harbor, Puget, Portsmouth) report to NAVSEA 04 and integrate nuclear workforces, planning codes, and lifting/handling departments that mirror the NAVSEAINST 5450.14D standard organization [NAVSEAINST5450-14D].

Regional Maintenance Centers (RMCs). Regional Maintenance Centers deliver voyage repairs, execute CMP work, and act as the local TA for availabilities; they synchronize contracting, production shops, and total ship readiness assessments (TSRA) under CNRMC [NAVSEAINST5450-145A, edo-4-1-1-fleet-maint-assets-2025].

SUPSHIP. Supervisors of Shipbuilding administer new construction and conversion/modernization contracts as ACOs, coordinate budget execution, and provide technical oversight for nuclear refueling overhauls (e.g., CVN RCOH) [NAVSEAINST5450-145A, edo-4-1-1-fleet-maint-assets-2025].

Private shipyards. Huntington Ingalls, Bath Iron Works, General Dynamics NASSCO/Electric Boat, Fincantieri Marinette Marine, and Austal execute modernization packages, submarine maintenance, and surge depot work as part of the industrial base portfolio directed by OPNAV and PEO contracts [edo-4-1-1-fleet-maint-assets-2025].

6.1.3 Command, Funding, and Technical Authority Chains

Operational chain. CNO delegates readiness to U.S. Fleet Forces (USFF) and U.S. Pacific Fleet (PACFLT), who assign Type Commanders to own production schedules and risk acceptance for their forces [OPNAVINST4700-7M].

Technical chain. NAVSEA 21/04 issue modernization and maintenance standards, while warfare centers and TAs publish CMP-derived work packages; disputes escalate through the Technical Authority chain independent of the operational chain [OPNAVINST4700-7M, NAVSEAINST5450-145A].

Funding chain. Fleet maintenance (OC&MF) flows from OPNAV N82 to BSOs and on to execution activities, while modernization is forecast via FUNDS D/ALT/FUNDS K and, in limited pilots, OPN funds for selected private-yard availabilities to accelerate contract awards [edo-4-1-1-fleet-maint-assets-2025, DoDFMR-Vol3].

Maintaining clarity between supported/supporting chains prevents the common failure mode where operational priorities outpace technical warrant approvals or funding authority, triggering rework and availability churn.

6.1.4 Workforce Readiness and Assessments

Readiness assessments. TSRA events and Condition Found Reports feed the current ship's maintenance project (CSMP) so planners can refresh the CMP and future availability work packages [edo-4-1-1-fleet-maint-assets-2025].

Training pipelines. Programs such as NAMTS, SurgeMain reservists, and civilian apprentice pipelines grow targeted skills (e.g., non-skid application, inside machinist) to close gaps identified in Fleet readiness reviews [edo-4-1-1-fleet-maint-assets-2025].

Digital enablers. Class maintenance databases, Navy Data Environment (NDE) instances, and tool control systems give RMCs and NSYs shared configuration visibility that underpins quality assurance and auditability [NAVSEAINST5450-145A].

Timely feedback from these mechanisms is what allows SURFMEPP/SUBMEPP to rebalance work between the O-, I-, and depot echelons before a ship misses a CNO availability window.

6.2 Navy Modernization Program

Refs:

6.2.1 Modernization vs. Maintenance

Modernization. Improves capability or readiness above the baseline by installing approved Ship Alterations (SHIPALT), Modernization Work Orders, and Fleet modernization program items that change the ship's configuration, safety posture, or mission systems [edo-4-1-2-navy-modernization-2025, OPNAVINST4700-7M].

Maintenance. Restores the system to its original performance and reliability; it cannot change capability without an approved modernization directive [edo-4-1-2-navy-modernization-2025, COMFLTFORCOMINST4790-3].

Repair. Corrects degradations to return the item to the current baseline; repairs that change form, fit, or function require an approved modernization document to avoid unauthorized configuration changes [OPNAVINST4700-7M].

EDOs must articulate which work package element they are defending, because it dictates the funding source (e.g., FUNDS-D/ALT for modernization versus OC&MF for maintenance) and who holds approval authority.

6.2.2 Governance, Roles, and Documentation

Modernization governance. The Navy Modernization Program (NMP) integrates OPNAV resource sponsors, PEOs, Participating Acquisition Resource Managers (PARMs), Warfare Centers, and Fleet forces through the NMP Executive Steering Group and Sub-Class Modernization Coordinating Groups; the process is codified in SL720-AA-MAN-030, TS9090.310, and the JFMM [SL720-AA-MAN-030, TS9090-310, COMFLTFORCOMINST4790-3].

Key documents. Modernization Change Documents capture the requirement, Justification and Cost Forms allocate funding, SHIPALT Records (Record of Change) provide lifecycle traceability, installation drawings direct work, and the Alteration Equivalent to Repair (AER) process keeps urgent fixes legal [TS9090-310, edo-4-1-2-navy-modernization-2025].

Execution agents. Alteration Installation Teams (AITs), Regional Maintenance and Modernization Coordination Offices (RMMCOs), and SUPSHIPS integrate modernization tasks into availabilities while Naval Supervising Activities verify that work followed the approved package [SL720-AA-MAN-030, TS9090-310].

6.2.3 Process Flow and Funding Integration

1. **Identify need.** Fleet feedback, reliability data, or new threats drive a Change Initiation Notice, which is screened for technical feasibility and logistics impacts [edo-4-1-2-navy-modernization-2025].
2. **Engineer and budget.** The Alteration Engineering Agent develops Ship Check data, installation drawings, and metrics while the PARM aligns FUNDS-D (lifecycle engineering) and FUNDS-K (procurement) appropriations; pilot efforts now allow limited OPN use for private-yard execution when approved by OPNAV N9/N83 [edo-4-1-2-navy-modernization-2025, SL720-AA-MAN-030].

3. **Select availability.** Modernization Work Package Integration (WPI) events match each change to a specific CNO availability, Continuous Maintenance availability, or pier-side AIT window based on lead time material and platform readiness [TS9090-310].
4. **Install and certify.** AITs execute under a Memorandum of Agreement (MOA) that spells out safety, quality, and turnover requirements; completion data is entered into the NDE to update the authoritative configuration record [SL720-AA-MAN-030, TS9090-310].

Failure to follow this sequence is why unauthorized equipment has been discovered during Board of Inspection and Survey (INSURV) events—a career ender for the responsible EDO.

6.2.4 Execution Enablers and Lessons Learned

Configuration management. Every modernization line item in the Availability Work Package must trace back to an approved change document, logistics support analysis, and allowance parts list to avoid sparing gaps [COMFLTFORCOMINST4790-3].

MOA discipline. The MOA between the AIT, RMMCO, the Naval Supervising Activity (NSA), and Ship's Force defines boundary isolations, tag-out responsibilities, testing, and habitability; lessons learned from CANES and AWS installs show that unsigned MOAs invite production and safety conflicts [TS9090-310, edo-4-1-2-navy-modernization-2025].

AIT employment. Use AITs when the task requires repeat installations across multiple hulls, unique OEM skills, or when it is more cost-effective to mobilize the capability than to train an entire shipyard trade [SL720-AA-MAN-030].

6.3 Fleet Maintenance Policy and Implementation

Refs:

6.3.1 Policy Baseline

OPNAVINST 4700.7M. Establishes the maintenance policy for United States Navy ships: maintain the fleet at the highest practical readiness, perform work at the lowest capable level, and apply Reliability-Centered Maintenance (RCM)/Condition-Based Maintenance (CBM) methods to manage Total Ownership Cost [OPNAVINST4700-7M].

OPNAVNOTE 4700. Publishes CNO availability intervals, durations, man-day targets, and Repair Days for each platform, providing the authoritative baseline for the Long-Range Maintenance Schedule (LRMS) [OPNAVNOTE4700-24].

JFMM and CBM+. COMUSFLTFORCOM/COMPACFLTINST 4790.3 (JFMM) assigns responsibilities to Type Commander (TYCOM)s, RMMCOs, and NSAs, while OPNAVINST 4790.16 issues CBM+ policy so sensors and analytics can replace purely time-based maintenance when justified [COMFLTFORCOMINST4790-3, OPNAVINST4790-16G].

The entire maintenance enterprise hinges on tying ship assessments to these references; citing a different standard during a board (e.g., OEM manual) without reconciling it to the JFMM and policy hierarchy is a red flag.

6.3.2 Strategy Frameworks

Optimized Fleet Response Plan (OFRP). OPNAVINST 3000.15 drives Fleet Response Plans that align readiness, training, and maintenance phases; maintenance windows in the OFRP billet plan are how TYCOMs defend availability lengths and sequencing [OPNAVINST3000-15K].

Surface Force Readiness Manual (SFRM). SURFLANT/SURFPAC 3502-series guidance aligns training milestones (Basic, Advanced, Integrated) with maintenance health metrics so a ship cannot progress if critical maintenance or material conditions remain open [CNSP-CNSLINST3502-7C].

Naval Sustainment System—Shipyards (NSS-SY). NSS-SY injects commercial best practices (Theory of Constraints, value-stream management, digital dashboards) into the four public yards with the goal of 80% on-time SSN deliveries and no idle submarine backlog by FY26 [edo-4-1-3-fleet-maint-policy-2025].

6.3.3 Availability Approval and Execution Discipline

1. **Baseline work.** SURFMEPP/SUBMEPP compile CMP work, TYCOM repairs, and modernization candidates into the Baseline Availability Work Package (BAWP) at A-36 months; work then flows through the CNO scheduling conference for final approval [OPNAVNOTE4700-24, edo-4-1-3-fleet-maint-policy-2025].
2. **Directed vs. condition-based maintenance.** Directed Maintenance Tasks (DMT) must be executed regardless of condition (e.g., structural checks mandated by SUBSAFE), while CBM tasks rely on evidence such as oil analysis, smart sensors, or TSRA discoveries to justify deferral [OPNAVINST4700-7M, OPNAVINST4790-16G].
3. **Approval boards.** TYCOM Availability Work Package Reviews validate that all Departure from Specifications (DFSs) and Temporary Standing Orders (TSOs) have closure plans before endorsing the package for CNO approval [COMFLTFORCOMINST4790-3].
4. **Metrics.** Schedule adherence, manday performance, and quality escape metrics (e.g., repeat maintenance, Objective Quality Evidence (OQE) rejects) appear in USFF/COMPACFLT readiness briefs and feed the next LRMS update [edo-4-1-3-fleet-maint-policy-2025].

6.3.4 Trends, Risks, and Talking Points

- **Industrial base mix.** Navy policy seeks roughly a 50/50 public-private mix for surface depot work, with CVNs and SSNs/SSBNs remaining predominantly public-yard to retain nuclear competencies [OPNAVINST4700-7M].
- **Manpower constraints.** NSS-SY reviews highlight persistent shortages in key trades (nuclear welders, radiological controls, rigging) that drive docking delays; referencing NSS-SY corrective actions shows awareness of current risk mitigations [edo-4-1-3-fleet-maint-policy-2025].

- **Digital thread.** The NDE modernization module is now the authoritative source for installed configuration, allowing planners to reconcile modernization with maintenance data without resorting to ad-hoc spreadsheets [TS9090-310].
- **Fiscal discipline.** Maintenance execution must honor color-of-money boundaries (OC&MF vs. OPN/SCN); unauthorized obligation adjustments are Anti-Deficiency Act (ADA) violations [DoDFMR-Vol3, FAR].

6.4 AIT Fundamentals and Lessons Learned

Refs:

6.4.1 Purpose and Advantages

- **Concentrated expertise.** An AIT is a trained unit (government, contractor, or hybrid) directed by an AIT Manager to install specific modernization changes that require unique skills, tooling, or repetitive production-line execution [TS9090-310, edo-4-1-4-ait-fundamentals-2025].
- **Speed and repeatability.** Using the same team across hulls captures lessons learned, reduces quality escapes, and accelerates delivery of high-priority combat system upgrades (e.g., CANES, AWS, GPNTS) without overloading the shipyard workforce [SL720-AA-MAN-030].
- **Safety and configuration control.** Dedicated teams enforce technical work documents, boundary isolations, and logistics support for each alteration, reducing the risk of unauthorized changes that could violate SUBSAFE or Level I controls [TS9090-310].

6.4.2 Roles and Responsibilities

Sponsor / PARM. Assigns and funds the AIT, prioritizes hulls, and ensures logistics (allowance updates, training, tech manuals) are resourced before work begins [SL720-AA-MAN-030].

AIT Manager. Leads planning, safety, schedule integration, and quality execution; serves as the single point of contact for the Naval Supervising Activity and Ship's Force [TS9090-310].

On-Site Installation Coordinator (OSIC). Coordinates day-to-day shipboard actions, manages tag-outs and system turnovers, and resolves emergent issues between the AIT, NSA, and Ship's Force [edo-4-1-4-ait-fundamentals-2025].

RMMCO. Screens alteration packages, aligns them with availability windows, and enforces waterfront integration and reporting requirements [TS9090-310].

NSA/Lead Maintenance Activity (LMA). Controls work authorization, boundary isolations, tests, and Objective Quality Evidence for work accomplished under the availability contract [COMFLTFORCOMINST4790-3].

6.4.3 Planning Controls and MOA Discipline

1. **MOA.** The MOA outlines scope, funding, schedule, safety, habitability, quality, testing, and turnover; it must be signed by the AIT sponsor, RMMCO, Ship's Commanding Officer, and NSA before work starts [TS9090-310].
2. **Installation planning.** Each alteration requires a ship check, logistics certification, and completion of prerequisite changes; the NMP databases confirm that planned work matches the approved Change Document [SL720-AA-MAN-030].
3. **WAF/tag-out alignment.** Integration with the Work Authorization Form process and Tag-out Users Manual (TUM) prevents conflicting isolations between the AIT and shipyard trades [S0400-AD-URM-010].
4. **Testing.** Entry/exit criteria, including pre-installation checkout, operational tests, and system certifications (e.g., Combat System Ship Qualification Test), are tailored per alteration and witnessed by NSA [TS9090-310].

6.4.4 Lessons Learned for Board Prep

- **Late drawing changes drive rework.** Lock engineers early—AITs report that late drawing revisions, missing Interface Control Documents, or mismatched configuration data cause most delays [edo-4-1-4-ait-fundamentals-2025].
- **Habitability and safety must be priced.** Many AITs arrive without berthing or industrial hygiene plans; ensuring the MOA captures services, hot work permits, and fall protection prevents emergent cost growth [SL720-AA-MAN-030].
- **Document close-out.** Uploading OQE, system configuration updates, and post-install logistics changes to the NDE is mandatory—omitting them erodes Fleet supply support [TS9090-310].

6.5 Waterfront Organizations, Work Controls, and Safety

Refs:

6.5.1 Naval Propulsion Program Oversight

Naval Nuclear Propulsion Program (Naval Reactors). Established by executive order and statute, Naval Reactors owns cradle-to-grave authority for nuclear propulsion design, maintenance, training, and operations; they enforce uncompromising safety rules regardless of warfighting urgency [edo-4-1-5-waterfront-work-control-2025].

Naval Reactors Representative Office (NRRO). Resident Naval Reactors Representative Offices monitor each nuclear-capable waterfront, enforce program standards, and can halt work if safeguards are threatened; they are independent of yard leadership to prevent production pressure from eroding safety [edo-4-1-5-waterfront-work-control-2025].

Reactor Plant Contractor's Office (RPCO). Reactor Plant Contractor Offices represent the prime contractors (e.g., Newport News Shipbuilding) and ensure contract compliance and technical rigor during construction, refueling, and depot maintenance [edo-4-1-5-waterfront-work-control-2025].

Joint Test Groups. DOE and Navy personnel lead integrated test teams that certify plant reconstitution before turnover; they align with NRRO, SUPSHIP, and Ship's Force to execute rigorous testing sequences [edo-4-1-5-waterfront-work-control-2025].

Board insight: referencing the Thresher, Guitarro, and Miami investigations underscores why NRRO authority and independent QA cannot be waived, even under combat timelines.

6.5.2 SUBSAFE and Submergence Systems Controls

- **SUBSAFE.** NAVSEA 0924-062-0010 mandates design, material, process, and test controls for the seawater boundary and critical systems on submarines; any work that touches a SUBSAFE boundary requires certified Level I material, approved procedures, and documented Objective Quality Evidence [NAVSEA-0924-062-0010].
- **Submergence Systems Certification.** SS800 manuals reinforce submarine rescue and diver support equipment requirements; the Submergence Systems Certification Board mirrors SUBSAFE rigor for non-platform systems [SS800-AG-MAN-010].
- **Level I / critical material.** NAVSUP/NAVSEAINST 4440.16 controls procurement, receipt, and storage of Level I and SUBSAFE material to prevent counterfeit or degraded items from entering the supply chain [NAVSEA-4440-16].
- **Industrial safety.** S0570-AB-SAF-010 (fire protection) and S9002-AB-MAN-010 (submarine industrial safety) govern hot work, confined space, and damage control readiness during availabilities [S0570-AB-SAF-010, S9002-AB-MAN-010].

6.5.3 Work Authorization and Tag-out Discipline

1. **Work Authorization Forms (WAF).** The NSA/LMA generates WAFs to define scope, isolations, and boundary conditions; all trades and AITs must align their work with the active WAF or request revisions through the Project Manager [COMFLTFORCOMINST4790-3].
2. **Tag-out Users Manual.** S0400-AD-URM-010 prescribes red/amber tags, double barrier requirements, and control authority; the Ship's Force owns the tag-out log even when a contractor executes the work [S0400-AD-URM-010].
3. **Special evolutions.** Diving, radiological work, and ordnance moves require additional approvals (e.g., Naval Sea Systems Command Supervisor of Salvage and Diving Supervisor of Salvage and Diving (SUPSALV), Naval Ordnance Safety); EDOs must ensure these are embedded in the availability plan [NAVSEA-4740-2H, edo-4-1-5-waterfront-work-control-2025].

6.5.4 Waterfront Organization Insights

- **Unified waterfront teams.** Naval Shipyards, Regional Maintenance Centers, RMMCOs, and Ship's Force form integrated production and test teams; weekly Project Management Reviews should cover safety, quality, schedule, and funding status [edo-4-1-5-waterfront-work-control-2025].

- **Culture of questioning attitude.** The Naval Propulsion Program teaches that any worker can stop a job; referencing MIAMI's fire (shipyard worker's vacuum) shows how minor lapses escalate without that culture [edo-4-1-5-waterfront-work-control-2025].
- **Documentation.** Work packages, technical work documents, and checklists must be updated in the NDE to preserve traceability for Submarine Safety Program (SUBSAFE) and other certifications [NAVSEA-0924-062-0010].

6.6 Battle Damage Assessment and Repair

Refs:

6.6.1 Strategic Context

- **Global competition.** Renewed great-power competition with the PRC and Russia (plus persistent DPRK provocations) means distributed maritime operations must survive massed fires and cyber/electromagnetic attacks [NAVPLAN2024, edo-4-1-6-bdar-2025].
- **Wartime Acquisition Response Plan (WARP).** SECNAV's WARP memo directs every SYSCOM/PEO to maintain plans, contracts, and trained people to pivot from peacetime acquisition to wartime recovery of ships and systems [SECNAV-WARP-2021].
- **GAO findings.** GAO-21-246 warns that current BDAR capabilities are insufficient for contested logistics, highlighting gaps in expeditionary repair, pre-positioned materiel, and command-and-control [GAO-21-246].

6.6.2 BDAR Continuum

Damage Control. Ship's Force fights fires, floods, and casualties to stabilize the platform, preserve combat power, or keep it afloat until assistance arrives [edo-4-1-6-bdar-2025].

Rescue and Assistance (R&A). Military Sealift Command (Military Sealift Command (MSC)) tugs, Mobile Diving and Salvage Units (Mobile Diving and Salvage Unit (MDSU)), and SUPSALV assets conduct emergency towing, underwater repairs, object retrieval, and environmental mitigation [NAVSEA-4740-2H].

Damage Assessment. Ship's Force, salvage teams, and ashore Damage Assessment Teams from RMCs, NSYs, or SEA 21 analyze hull integrity, stability, and mission systems to recommend disposition [edo-4-1-6-bdar-2025].

Expeditionary Repair. Forward Deployed Ship Repair Team (FDSRT) and Expeditionary Maintenance and Repair Facility (EMRF) deploy with Shop-in-a-Box (SIB) sets to restore mobility or key mission systems without returning to a depot [CPF-MSP-PLANORD-2023, edo-4-1-6-bdar-2025].

Depot Repair / Disposition. NSYs, RMCs, and private yards perform major repairs, partial restorations, or decide to scrap; choices depend on threat, capability needs, cost, and industrial capacity [edo-4-1-6-bdar-2025].

6.6.3 Command, Control, and Technical Authority

- **Operational control.** Fleet commanders designate BDAR task forces; Task Force logistics commanders orchestrate salvage, FDSRT, and EMRF employment while coordinating with theater Joint Logistics Enterprise nodes [NWP3-32, NWP4-12].
- **Technical authority.** Wartime does not suspend Technical Authority—NAVSEA, Naval Reactors, and Warfare Centers still adjudicate waivers; however, WARP allows pre-planned delegated authorities and acceptance of graded risk when documented [SECNAV-WARP-2021].
- **Reporting.** CASREP 4.0 timelines and Battle Damage Assessment reports flow through OPNAVINST 3040.2B to inform reconstitution priorities and Congressional notifications [OPNAVINST3040-2B].

6.6.4 Logistics, Contracting, and Fiscal Readiness

Prepositioned materiel. Maritime Support Plan (MSP) force packages require pre-kitted SIBs, hull patches, and mobile power kits staged throughout the Indo-Pacific, EUCOM, and CENTCOM theaters [CPF-MSP-PLANORD-2023].

Contracting. FAR Part 18 and DFARS Part 218 emergency authorities (e.g., oral solicitations, undefinitized contract actions, Defense Priorities and Allocations System ratings) enable rapid award, but commands must still document justification and maintain traceability for later definitization [FAR, DFARS].

Funding. BDAR relies on OMN for emergent repairs, SCN for major restorations, and Weapons Procurement, Navy (WPN) when combat system replacement constitutes procurement; DoD FMR Volume 3 prescribes reprogramming thresholds [DoDFMR-Vol3].

Supply chain resilience. The Resilient Maritime Logistics initiative (Project 33) aligns OPNAV N4, Fleet Logistics Centers, and Defense Logistics Agency to keep people, parts, and processes flowing under contested logistics [NAVPLAN2024, edo-4-1-6-bdar-2025].

6.6.5 Maritime Support Plan Force Packages

1. **Afloat Augmentation.** 25–50 artisans augment the shipboard IMA to enable 24/7 casualty response within a strike group [CPF-MSP-PLANORD-2023].
2. **Afloat Independent Maintenance Activity.** Tender-like capability distributed across vessels of opportunity that integrates EMRF, FDSRT, and logistics cells under Task Force OPCON [CPF-MSP-PLANORD-2023].
3. **Ashore Lean / Robust / Austere.** Scalable shore nodes that combine contractor oversight teams, NAVSEA contracting cells, and host-nation support to execute depot-equivalent work forward [CPF-MSP-PLANORD-2023].

EDOs should be ready to explain which force package they would recommend for a given scenario, how long it takes to activate, and how technical authority, contracts, and funding are synchronized.

6.7 CNO Availability Planning

Refs:

6.7.1 Balancing Requirements, Resources, and Readiness

Customers. Fleet commanders and TYCOMs drive capability requirements and availability length based on the Optimized Fleet Response Plan and readiness gaps [OPNAVINST3000-15K, edo-4-2-1-cno-availability-planning-2025].

Planners. Shipyards, RMCs, and planning activities must sequence work, tooling, infrastructure, and LLTM so the schedule is executable [edo-4-2-1-cno-availability-planning-2025].

Resources. Budgets (OC&MF, OPN, FUNDS-D/K), workforce, and pier/dock capacity must align with CNO-directed Repair Days [OPNAVNOTE4700-24].

EDOs should articulate how they reconcile conflicting demands—for example, deferring a lower-criticality modernization so mandatory SUBSAFE work fits within the allotted man-days.

6.7.2 Availability Work Package Development

1. **Baseline (A-36 to A-24).** SURFMEPP/SUBMEPP derive the BAWP from the CMP, TYCOM repairs, and modernization candidates; Ship Checks, Condition Found Reports, and TSRA results refine the package [edo-4-2-1-cno-availability-planning-2025, COMFLTFORCOMINST4790-3].
2. **Initial Planning (A-21).** Planning Activities (Carrier Planning Activity, Submarine Planning Activity, RMCs) reconcile the BAWP with Class Plan priorities and issue the Initial Availability Work Package (Availability Work Package (AWP)) [edo-4-2-1-cno-availability-planning-2025].
3. **Final Planning (A-12 to A-3).** Results of pre-availability tests (PATs/POTS), DFSs, TSOs, and new modernization approvals are adjudicated; the final AWP is issued no later than three months before A-0 [edo-4-2-1-cno-availability-planning-2025, OPNAVNOTE4700-24].
4. **Contracting.** For surface private-yard availabilities, Multiple Award Contract, Multi-Order (MAC-MO) constructs increase competition and flexibility; public yards rely on Advanced Industrial Management (AIM) processes [edo-4-2-1-cno-availability-planning-2025].

6.7.3 Planning Teams and Integration Forums

- **Carrier Team One.** Aligns NAVSEA 08/04/21, NAVAIR, Newport News Shipbuilding, and Fleet stakeholders to drive aircraft carrier availability excellence [edo-4-2-1-cno-availability-planning-2025].
- **Surface Team One.** Unites SEA 21, SEA 05, SURFMEPP, TYCOMs, and PEOs to tackle systemic issues (e.g., late drawings, material delays) across destroyer/cruiser/amphibious availabilities [edo-4-2-1-cno-availability-planning-2025].

- **Submarine Team One.** Led by PMS 392/SUBMEPP, integrates CNRMC, NAVSEA 08/21, and public yards to sustain SSN/SSBN availabilities and implement NSS-SY initiatives [edo-4-2-1-cno-availability-planning-2025].
- **Planning summits.** Readiness Summits, Availability Work Integration (AWI) events, and Integrated Production Planning (IPP) meetings synchronize modernization, maintenance, logistics, and testing products [edo-4-2-1-cno-availability-planning-2025].

6.7.4 Risk Controls and Board-Ready Talking Points

Critical path management. Identify the top three critical path evolutions (e.g., tank blasting/coating, propulsion plant maintenance, combat system rip-outs) and ensure early start requirements—barge services, LLTM, training—are executable before A-0 [edo-4-2-1-cno-availability-planning-2025].

Material readiness. Demand 100% receipt of LLTM and government-furnished material before award; highlight mitigation plans for supply-chain risk (dual sources, cannibalization, additive manufacturing) [edo-4-2-1-cno-availability-planning-2025].

Growth vs. new work. Explain how your team budgets anticipated growth work (historical allowances) versus truly new work (unique casualty), as well as the screening process for adding either to the contract [COMFLTFORCOMINST4790-3].

Metrics. Use NSS-SY dashboards (Earned Value, manday burn, schedule adherence) and weekly risk reviews to show how you keep leadership informed and trigger help early [edo-4-2-1-cno-availability-planning-2025].

6.8 CNO Availability Execution

Refs:

6.8.1 Project Teams and Responsibilities

Shipyard team. The Project Superintendent (overall cost/schedule/safety owner), Project Manager (budget, earned value, planning integration), Assistant Project Superintendents (zone leads), Engineering & Planning (technical work documents, boundaries), and Business & Planning (funding, schedule coordination) form the core team [edo-4-2-2-cno-availability-execution-2025].

RMC/private-yard team. The Port Engineer, Ship's Maintenance Manager (SMMO), Ship's Force Maintenance Officer, TYCOM representative, Contracting Officer, and contractor Project Manager manage planning yard availabilities [edo-4-2-2-cno-availability-execution-2025].

Ship's Force. CO/XO/CHENG maintain safety, tag-out, and configuration control; Combat Systems and Supply Officers coordinate tests, SOVTs, and material receipt [COMFLTFORCOMINST4790-3].

Specialists. Integrated Test Engineers, Project Support Engineers, Quality Assurance Specialists, Alteration Coordinators, and Administrative Contract Specialists provide focused oversight on testing, configuration, QA, and change management [edo-4-2-2-cno-availability-execution-2025].

6.8.2 Execution Phases

1. **Nesting / Arrival.** Establish temporary services, fire watches, habitability, industrial hygiene controls, and turnover from Ship's Force to the Maintenance Activity; complete mandatory briefings (JFMM Chapter 2, Tag-out Users Manual) [edo-4-2-2-cno-availability-execution-2025].
2. **Rip-out & Access.** Remove interferences, open systems, and conduct initial Work Authorization Form (WAF) reviews; late identification of hazardous material and access conflicts is a top schedule killer [COMFLTFORCOMINST4790-3].
3. **Open & Inspect.** Execute inspections (tank, structural, piping) and document growth work; per NAVSEA Standard Item 009-01, inspections should be 100% complete by A+20% to preserve schedule margin [edo-4-2-2-cno-availability-execution-2025].
4. **Repair & Production.** Complete component tasks, manage new vs. growth work approvals, and track critical path milestones using Task Group Instruction (TGI) [edo-4-2-2-cno-availability-execution-2025].
5. **Testing, Trials, Certification.** Execute compartment turnover, Light-Off Assessment (LOA), Shipboard Operational Verification Test (SOVT), Combat System Ship Qualification Trial (CSSQT), Builder's/Acceptance Trials, and Sea Trials before Production Completion Date (PCD) [COMFLTFORCOMINST4790-3].

6.8.3 Governance, Quality, and Work Control

- **NSA / LMA.** Certifies that work is authorized, technically compliant, and properly tested before acceptance; reviews Objective Quality Evidence (OQE) prior to signing completion certificates [COMFLTFORCOMINST4790-3].
- **Work control.** WAFs, TGI sequencing, and boundary tags must remain synchronized; growth work requires screening panels (Ship's Force, TYCOM, KO) to verify funding, schedule, and technical impacts [edo-4-2-2-cno-availability-execution-2025].
- **New vs. growth work.** New work is undiscovered scope added post-award; growth work expands existing items. Both demand TYCOM approval, funding source identification, and contract mods (or JSN adjustments for public yards) [COMFLTFORCOMINST4790-3].
- **Testing governance.** Chief Test Conductors manage test agendas; engineering agents and Ship's Force witness tests, and discrepancies must be adjudicated before certification events (e.g., LOA, CSSQT) [edo-4-2-2-cno-availability-execution-2025].

6.8.4 Lessons Learned

- **Momentum matters.** Availability performance often collapses after undocking; maintain daily production meetings, emphasize housekeeping/safety, and enforce material staging to avoid second-half slumps [edo-4-2-2-cno-availability-execution-2025].
 - **Communication is a weapon system.** Cross-functional representatives (yard, Ship's Force, TYCOM, QA, Supply) must keep each other informed about configuration, testing, and material risks; unresolved disconnects manifest as trial failures [edo-4-2-2-cno-availability-execution-2025].
 - **Document everything.** Capture change incorporation, OQE, and lessons in the NDE immediately—waiting until the end invites errors and delays closeout [COMFLTFORCOMINST4790-3].
-

Appendices

A Platinum Card

The *Platinum Card* is a primary study tool that will have most of the information required for your boards. Sources: EDO Coursebook Modules 3.1.1, 3.1.3, 3.1.4, and 3.1.6. Be able to draw and talk through Figures A.1–A.9.

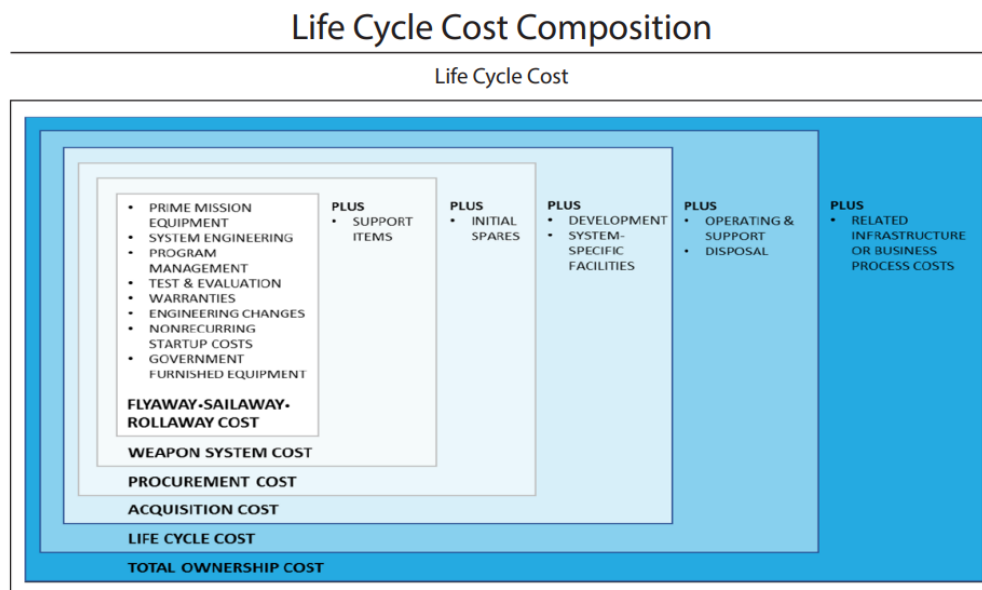


Figure A.1. Platinum Card: Life Cycle Cost Composition

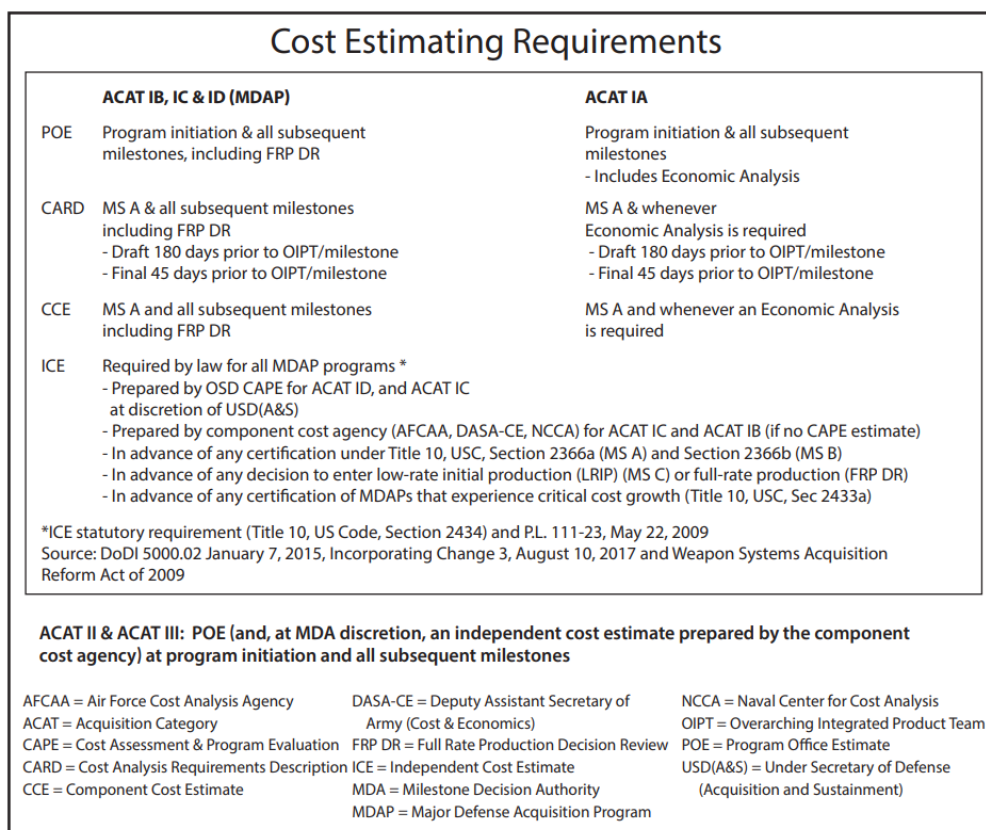


Figure A.2. Platinum Card: Cost Estimating Requirements

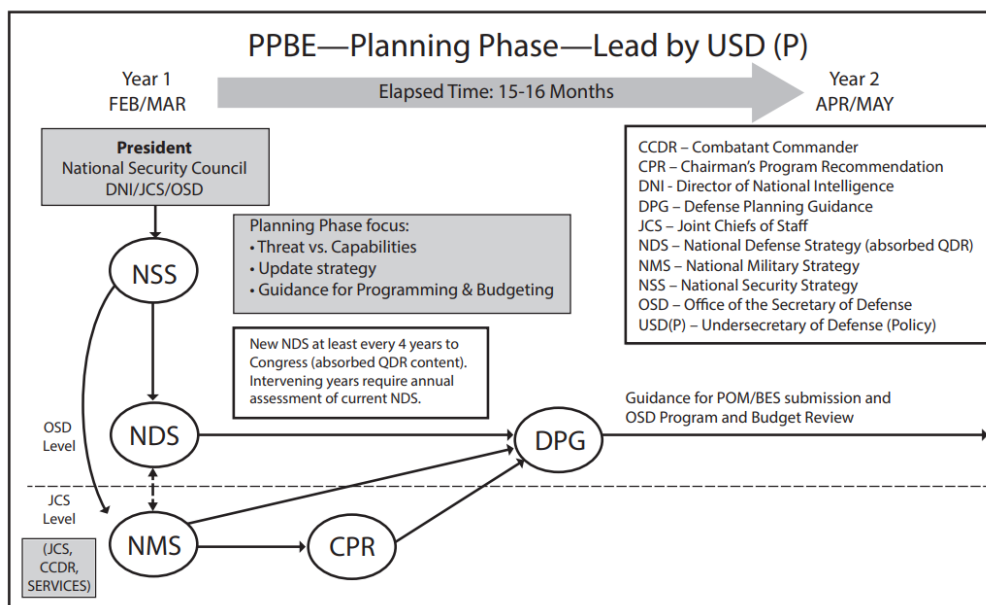


Figure A.3. Platinum Card: PPBE Planning Phase (Lead by USD (P))

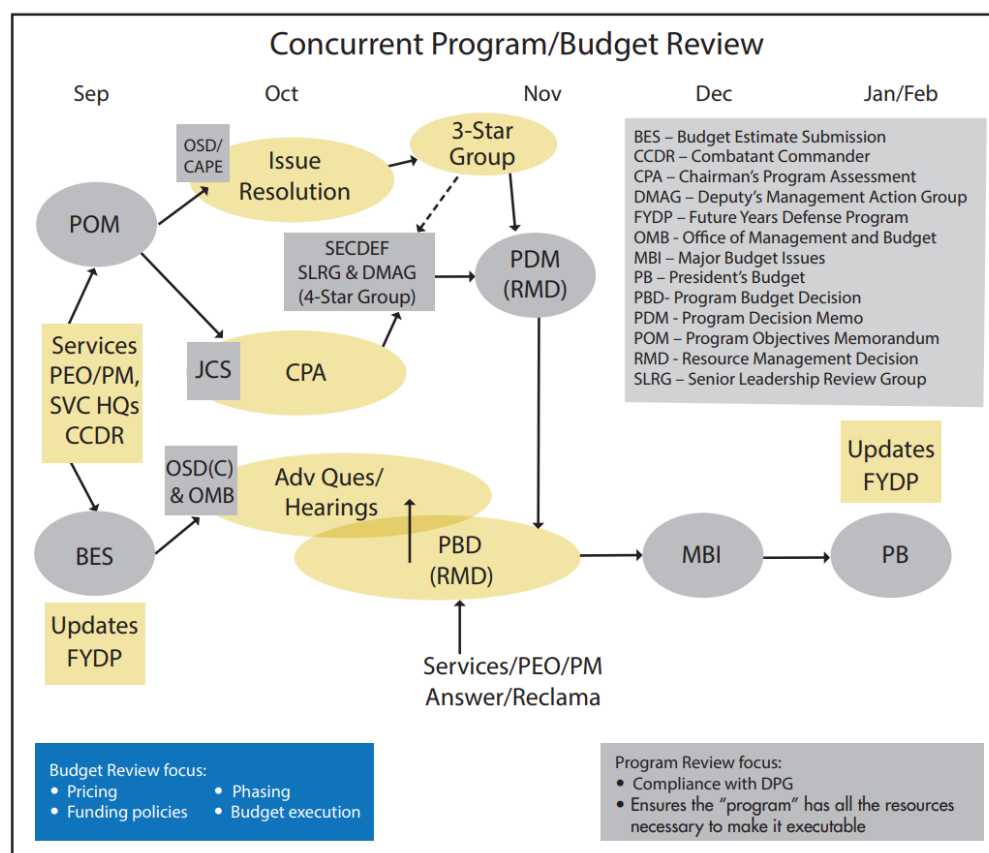


Figure A.4. Platinum Card: Concurrent Program/Budget Review

Below Threshold Reprogramming

Amounts are cumulative over Entire Period of Obligation Availability

APPRN	MAX INTO	MAX OUT	LEVEL OF CONTROL	OBL AVAIL
RDT&E	Lesser of +\$15M or + 20%	Lesser of - \$15M or - 20%	Program Element	2 Years
PROC	Lesser of + 15 M or + 20%	Lesser of - \$15M or - 20%	Line Item	3 years SCN: 5 Years
O&M	+ \$15M	- \$15M	Budget Activity (or Defense Agency) Some Sub-Activity Limitations on Decreases (see reference below)	1 Year
MILPERS	+ \$15M	- \$15M	Budget Activity	1 Year
MILCON	Lesser of +\$2M or + 25%	No Specific Congressional Restriction	Project	5 Years

Reference Sources: DoDFMR 7000.14-R, Volume 3, Chapter 6 (Sept 2015) and Chapter 7 (Mar 2011) Joint Explanatory Statement of Congress Making Appropriations for the Department of Defense for Fiscal Year 2024

Figure A.5. Platinum Card: Below Threshold Reprogramming

Resource Allocation Process

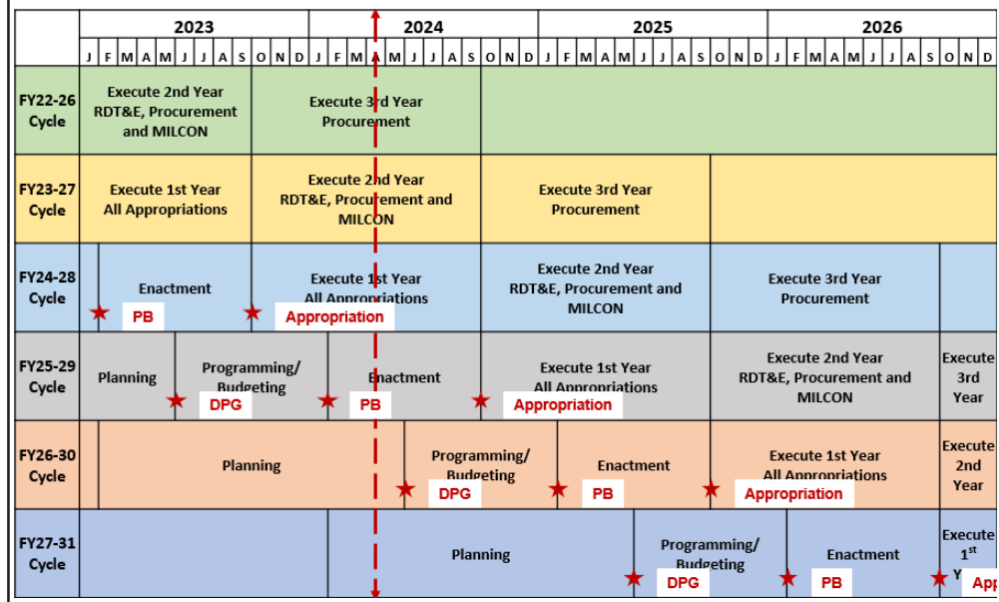


Figure A.6. Platinum Card: Resource Allocation Process

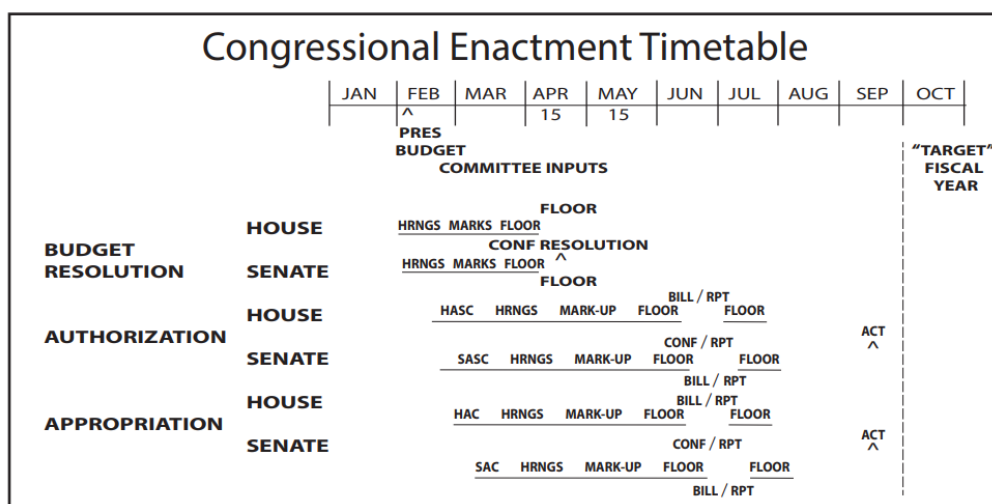


Figure A.7. Platinum Card: Congressional Enactment Timeline

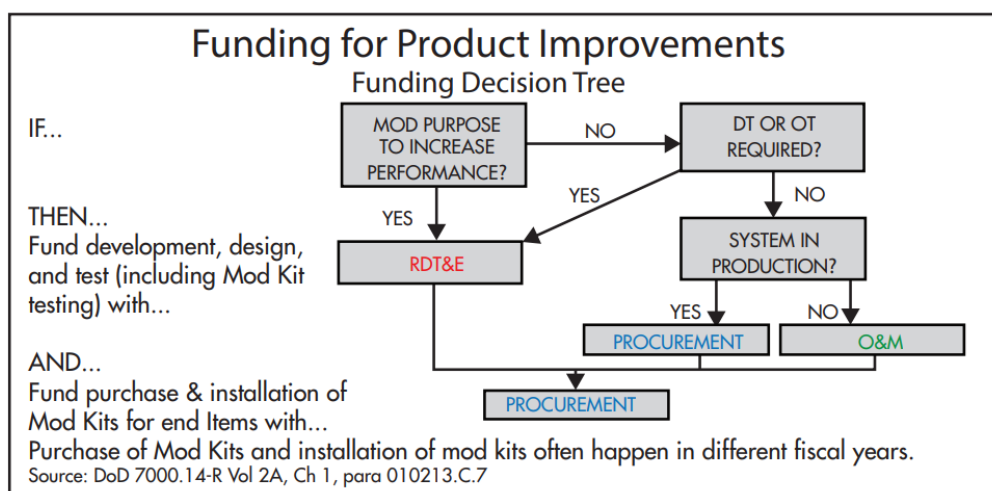


Figure A.8. Platinum Card: Funding for Product Improvements

RDT&E. Engineering changes requiring development/test.

Procurement. Production/installation of approved mods/end-items.

O&M. Minor mods/installation labor when authorized and not creating a new end-item.

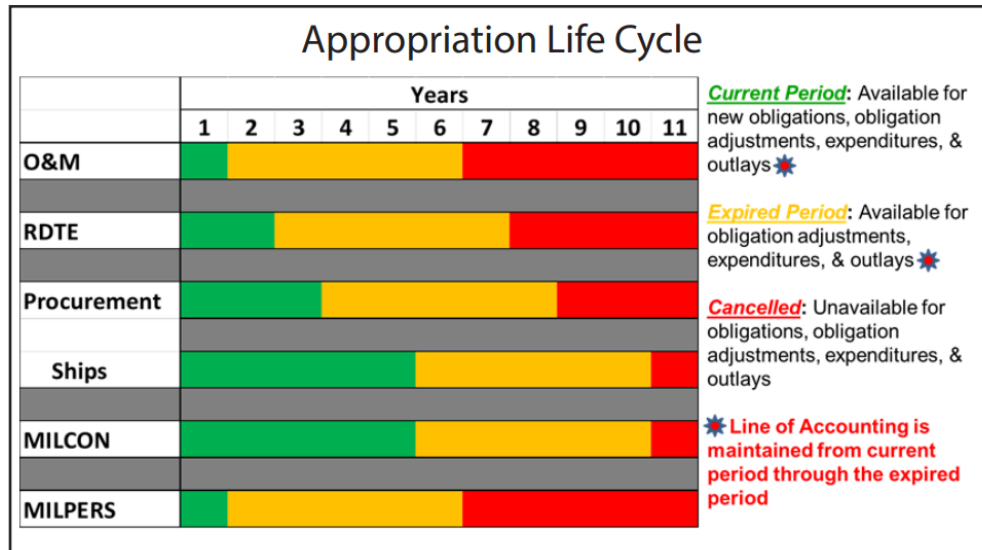


Figure A.9. Platinum Card: Appropriation Life Cycle

B Key Roles in Acquisition and Modernization

B.1 EDO Flag Officers (snapshot)

Verify names/billets the week of your board. Current as of: 13 Nov 2025.

Vice Admirals

VADM James P. Downey.

Commander, Naval Sea Systems Command (COMNAVSEA); leads the 80K-person naval shipbuilding enterprise and chairs the Navy Program Executive Council for ships and ship systems.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

VADM Johnny R. Wolfe Jr.

Director, Strategic Systems Program (SSP), responsible for the nation's strategic weapons industrial base and Fleet ballistic missile sustainment.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

VADM Seiko Okano.

Principal Military Deputy (PMILDEP) to ASN(RD&A); retains direct reporting program manager duties for Project Overmatch and NAVWAR's digital architecture initiatives.Source: [DVIDS-Overmatch-OpenDAGIR-2025](#), [DVIDS-Overmatch-OpenDAGIR-2025](#) [[DVIDS-Overmatch-OpenDAGIR-2025](#)]

Rear Admirals (Upper Half)

RADM Casey J. Moton.

PEO CVN, accountable for aircraft carrier new construction and in-service nuclear availability portfolios.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RADM Kurt J. Rothenhaus.

Chief of Naval Research (CNR) and Commander, ONR Global, aligning S&T investments with fleet needs.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RADM Jonathan E. Rucker.

PEO SSN, responsible for submarines, undersea weapons, and the Columbia/Virginia Class Program Offices.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RADM Brian A. Metcalf.

PEO Ships, leading the surface combatant, amphibious, and auxiliary ship portfolios.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RADM Douglas L. Williams.

Director for Test, MDA, synchronizing joint missile defense T&E campaigns.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-](#)

Rear Admirals (Lower Half)**RDML Peter D. Small.**

NAVSEA Chief Engineer / Commander, NSWC/NUWC, the Navy's lead technical authority for ship systems.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RDML Dan L. Lannamann.

CNRMC, overseeing regional maintenance centers and private-sector depot availabilities.Source: [edo-3-3-1-acq-policy-players-2025](#)

RDML Kevin R. Smith.

PEO USC, accountable for unmanned surface and small combatant shipbuilding programs.Source: [edo-3-3-1-acq-policy-players-2025](#)

RDML Dianna Wolfson.

Fleet Maintenance Officer, USFF, integrating ship maintenance execution and TYCOM readiness.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RDML Daniel W. Ettlich.

Director, Fleet Maintenance, PACFLT, leading west-coast and forward-deployed maintenance readiness.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

Reserve EDO Flags**RDML Robert J. Dodson (USNR).**

Deputy Commander, Supervision of Shipbuilding (SUPSHIP), NAVSEA, aligning reserve expertise to construction oversight.Source: [edo-3-3-1-acq-policy-players-2025](#), [edo-3-3-1-acq-policy-players-2025](#) [[edo-3-3-1-acq-policy-players-2025](#)]

RDML Michael S. Richman (USNR).

Deputy Director, Regional Strike Systems, SSP, supporting strategic weapons sustainment.Source: [edo-3-3-1-acq-policy-players-2025](#)

B.2 Key Roles in Acquisition and Modernization

Department acquisition governance.

Sources: SECNAVINST 5400.15D; SECNAVINST 5000.2G; DoDI 5000.85.

- ASN(RD&A), the SAE and CAE for the DON, sets acquisition policy, charters PEOs / DRPMs, and adjudicates milestone decisions when delegated by the Milestone Decision Authority.
- PEOs and DRPMs hold delegated program authority, establish baselines, and are accountable for translating capability needs into executable acquisition strategies.

- SYSCOM Commanders provide the workforce, infrastructure, and TA warrants that underpin PEO execution inside the Navy matrix construct.

Joint requirements governance.

Sources [jcids-manual-2021, secwar-acq-transformation-2025].

- **JROC:** Validates joint capability requirements, prioritizes gaps, and issues JROCM direction that becomes binding input to Gate 2 and milestone documentation.
- **Joint Staff Gatekeeper/JCB:** Controls the KM/DS queue, assigns Joint Staffing Designators, and routes most Navy submissions for JCB-level validation to keep JROC time focused on the highest-risk issues.
- **FCBs:** Chair certification working groups (Net-Ready, Force Protection, System Survivability), monitor DOTMLPF-P implementation, and elevate Configuration Steering Board actions when requirement trades alter program baselines.
- **PAEs and CTCs:** The 2025 Acquisition Transformation Strategy empowers PAEs to convene Capability Trade Councils that record requirement/cost/schedule trades in real time so PEO teams keep the DAS synchronized with evolving demand signals.

Combatant command sponsors.

Sources [edo-2-1-1-command-structures-2025, jcids-manual-2021].

- **CCDRs** own warfighting problems, sign JUONs/JEONs, and direct lead Services or agencies to prosecute capability gaps that demand rapid solutions.
- **CCMD staffs** conduct mission-thread analysis and architecture sprints with Fleets, labs, and industry to translate operational risk into measurable capability requirements before the Gatekeeper accepts a package.
- Commanders remain voting participants during validation reviews and oversee fielding to ensure delivered capability solves the theater problem that generated the requirement.

Joint Chiefs leadership.

Sources [edo-2-1-1-command-structures-2025, jcids-manual-2021, USC-10-181].

- **CJCS:** Principal military adviser to the President/SECDEF, co-chairs the JROC, and leads joint concept and readiness development that frames every Capability-Based Assessment.
- **VCJCS:** Chairs the JCB, co-leads the DMAG, and arbitrates cross-Service requirement or resourcing disputes before they escalate to the Deputies or Secretary level.

OPNAV corporate leadership.

Source [edo-2-1-1-command-structures-2025].

- **CNO:** Serves as Service Chief, chairs the Navy corporate board, and approves Navy positions for Gate 0/1 decisions before submissions move to the Joint Staff.

- **OPNAV resource sponsors (N8, N82, N9, N91):** Translate Fleet priorities into the POM/FYDP, enforce two-pass/seven-gate rigor, and synchronize requirements, budgets, and PEO execution.

Acquisition decision authorities.

Sources [DoDD5000-01, DoDI5000-85, SECNAV5000-2G].

- **DAE / USW(A&S):** Issues acquisition policy, chairs the Defense Acquisition Board, and retains MDA for ACAT ID/IAM programs unless delegated.
- **SAE/ASN(RD&A):** Assigns Navy MDA for ACAT II and below, approves Service-tailored governance (e.g., two-pass/seven-gate), and charters PEOs/DRPMs.
- **Delegated MDA (PEO/DRPM):** Signs Acquisition Decision Memoranda, manages Configuration Steering Boards, and keeps KPP/APB trades synchronized with requirements direction and statutory certifications.

Program Authority chain.

Sources: SECNAVINST 5000.2G; DoDI 5000.85.

- **PEO/PA:** Owns program outcomes, charters PMs, approves acquisition strategies and baselines.
- **DRPM:** Direct-report program leads for special access or priority portfolios with the same milestone authority as PEOs.
- **Ship Program Manager (SPM)/PM:** Accountable for cost/schedule/performance, leads risk management, orchestrates IPTs.
- **Ship Acquisition Program Manager (SHAPM):** Delivers new hulls; coordinates design/build/activation sequencing.
- **Ship Lifecycle Manager (SLM):** Drives sustainment and modernization packages for in-service assets.
- **PARM/Ship Project Director (SPD):** Sponsors platform-level upgrades and alteration packages.

Technical Authority chain.

Source: SECNAVINST 5400.15D.

- **UTA / Chief Engineer:** Issues enterprise technical policy, owns warrants.
- **TWHs:** Certifies design compliance, adjudicates departures/concurrence packages.
- **Engineering Agents (ISEA, DA, AEA, SIA, TDA):** Execute lifecycle engineering; provide in-service engineering decisions under delegated authority.

Operational test oversight.

Sources [DoDI5000-85, DoDAcqGuidebook].

- **DOT&E:** Independent OSD authority that concurs on TEMPs, monitors operational test realism, and reports suitability/effectiveness outcomes to Congress.

- **Service Operational Test Agencies.** COMOPTEVFOR (COTF), AFOTEC, ATEC, and MCOTEA plan and execute IOT&E/FOT&E, render the OTRR recommendation, and provide Service suitability findings to the MDA.

Developmental test governance.

Sources [DoDI5000-89].

- **DASW(T&E):** Designates Chief Developmental Testers and Lead Developmental Test and Evaluation Organizations for ACAT I programs, adjudicates test resource shortfalls, and co-chairs the Defense T&E WIPT.
- **CDT:** Synchronizes the integrated test schedule, deficiency management cadence, and readiness evidence required for each TRR/milestone.
- **LDTO:** Provides instrumentation, modeling & simulation accreditation, range execution, and authoritative data packages for developmental tests.

Live-fire statutory leads.

Sources [USC-10-2366, DoDI5000-89].

- **DOT&E Live Fire Test Director:** Approves plans, monitors execution realism, and delivers the statutory lethality/vulnerability report to Congress.
- **Program Manager/Chief Engineer:** Funds threat-representative articles, integrates survivability design fixes, and aligns LFT&E data with the Acquisition Program Baseline and sustainment plans.
- **Service Safety Centers and Warfare Centers:** Provide casualty data, threat surrogates, and post-test forensic analysis that feed both live-fire reports and Fleet tactics updates.

NAVSEA headquarters roles.

Source: EDO Coursebook Module 2.1.2 (NAVSEA Organization, 2025 edition).

- **SEA 01 Comptroller:** BSO lead for NAVSEA financial governance and funds control.
- **SEA 02 Contracts:** Enterprise contracting authority, policy, and warrant management.
- **SEA 03 Cyber Engineering and Digital:** Drives cyber resiliency, digital engineering, and data transformation initiatives.
- **SEA 04 Industrial Operations:** Oversees public shipyards, maintenance execution, and quality assurance.
- **SEA 05 Chief Engineer:** Chief TA; issues warrants, certifies designs, and maintains technical standards.
- **SEA 06 Sustainment:** Manages product support strategies and lifecycle logistics integration.
- **SEA 07 Undersea Warfare:** Dual-hatted as PEO UWS; oversees undersea combat systems sustainment.
- **SEA 08 Nuclear Propulsion:** Three-hatted nuclear propulsion authority across DON and Department of Energy (DOE) roles.

- **SEA 09 Safety and Regulatory Compliance:** Aligns enterprise safety governance and reporting.
- **SEA 10 Total Force and Corporate Ops:** Manages workforce planning, corporate services, and governance.
- **SEA 21 In-Service Ships/CNRM:** Leads surface-ship sustainment and modernization (PMS 321/326/339/421/443/451, SEA 21I, SURFMEPP).

NAVWAR enterprise directorates.

Source: EDO Coursebook Module 2.1.3 (NAVWAR Enterprise, 2024 edition).

- **Code 1.0 Comptroller:** Budget formulation/execution, BSO duties, and funds certification.
- **2.0 Contracts:** Contracting policy, strategy reviews, and award/administration oversight.
- **3.0 Counsel:** Acquisition law, ethics, protests, and claim resolution.
- **4.0 Logistics and Fleet Support:** Lifecycle logistics, technical data, and fleet distance support integration.
- **5.0 Chief Engineer/TA:** Enterprise architectures, interoperability, and cyber certification authority.
- **6.0 Program Management:** Portfolio governance, milestone preparation, and PEO integration.
- **7.0 Science and Technology:** S&T portfolio management, prototyping, and technology transition.
- **8.0 Corporate Operations:** Workforce, Chief Information Officer (CIO) services, facilities, security, and public affairs.
- **FRD-100 Fleet Support:** Deployed engineering assistance and sustainment response.
- **FRD-200 Installations:** Shore/afloat C4I installation planning and cutover execution.

Program Executive Offices (Navy portfolios).

Sources: SECNAVINST 5400.15D; EDO Coursebook Modules 2.1.4 and 3.1.5.

- **PEO CVN:** Designs, builds, and sustains nuclear-powered aircraft carriers (e.g., PMS 312/378/379).
- **PEO IWS:** Develops and sustains ship/submarine combat systems; mission-aligned IWS directorates cover sensors, weapons, C2, and allied integration.
- **PEO Ships:** Oversees surface combatant and amphibious ship construction and modernization.
- **PEO USC:** Leads LCS, FFG 62, expeditionary, and unmanned surface/undersea portfolios.
- **Team Submarines (PEO SSN, PEO SSBN, Program Executive Office, Columbia-Class Submarines (PEO Columbia), PEO UWS):** Manages attack/strategic submarine acquisition, in-service support, and undersea combat systems.
- **PEO C4I:** Delivers fleet C4I; PMW 1XX focus on capability development, PMW 7XX on platform integration.

- **PEO Digital:** Provides enterprise digital services (e.g., Flank Speed) across the DON.
- **PEO MLB:** Modernizes manpower, logistics, and business IT systems.

Contracting authority (KO family).

Sources: FAR; DFARS; NMCARS; EDO Coursebook Module 3.2.1.

- **PCO:** Plans the acquisition, synchs with PMs before solicitation, awards and signs contracts/mods.
- **ACO:** Oversees post-award performance, surveillance, and payment/contract administration (often DCMA / NAVSEA field activities).
- **TCO:** Leads partial/full terminations, settlement negotiations, and equitable adjustments.
- **KO warrant:** Defines the dollar/authority limits; only the warranted KO can bind or obligate the Government.
- **Contracting Officer's Representative (COR) / assistant PM / engineering support:** Provide technical surveillance and acceptance recommendations; cannot direct work or obligate funds (FAR Parts 1 and 42).
- **HCA:** Approves actions such as letter contracts and high-value single-award IDIQs; may delegate no lower than flag/Senior Executive levels within the DON per FAR 1.601 and DFARS/NMCARS supplements.
- **SAE, ASN(RD&A):** Signs D&Fs for multiyear contracting, extraordinary relief, and other actions reserved to the Service Acquisition Executive under FAR Subparts 1.7 and 17.1.

Program Manager / KO partnership.

Sources: DoDI 5000.85; EDO Coursebook Module 3.2.1.

- PM integrates warfighter need, technical baseline, and budget; KO Competition in Contracting Act (CICA), incentives, and change management before RFP release or modification execution.

Source selection governance.

Sources: FAR Parts 1, 5, and 15; NAVSEA Source Selection Guide (2022); EDO Coursebook Module 3.2.2.

- **SSA:** Senior official who approves the Source Selection Plan, receives SSAC/SSEB recommendations, and signs the best-value decision memorandum.
- **SSAC:** Advisory council that synthesizes SSEB findings, compares proposals across factors, and briefs the SSA on trade-offs.
- **SSEB:** Multi-disciplinary evaluators (technical, management, past performance, cost/price) who rate proposals against Section M factors.
- **Small Business Professional / Competition Advocate:** Confirms set-aside decisions, reviews subcontracting plans, and endorses synopsis waivers.

- **Cost/Price Analyst & Legal Counsel:** Validate reasonableness determinations, alignment of Sections L/M, and clause sufficiency before release.
- **Award Fee Determining Official & Award Fee Board:** Plans award-fee periods, chairs performance reviews, and signs the determination memo authorizing or withholding fee payments (FAR Part 16; NAVSEA Source Selection Guide).

Fiscal control & certification.

Source: DoW FMR 7000.14-R Volume 3.

- **Funds Certifying Official/Comptroller:** Verifies purpose/time/amount before obligation; ADA safeguard.
- **Program/Budget Analyst:** Tracks execution, monitors reprogramming thresholds, prepares obligation/expenditure burn-down.
- **Resource allocation chain:** OUSW(C) apportions to the Navy; OPNAV (N82/FMB) allocates to BSOs; SYSCOM comptrollers (e.g., SEA 01) issue suballocations to executing activities.

PPBE resource sponsors.

Source: EDO Coursebook Module 3.1.1 (PPBE, 2025 edition).

- **CAPE:** Provides independent cost assessments and program evaluation across the Department.
- **N8:** Builds the Navy POM, balancing capability and fiscal constraints across the FYDP.
- **N9:** Integrates warfare requirements and advocates mission-area investments.
- **N91:** Conducts cross-domain mission integration and orchestrates POM issue resolution.

Congressional resource chain.

Source: EDO Coursebook Module 3.1.2 (Congressional Enactment, 2025 edition).

- **HASC / SASC:** Authorize defense programs and policy in the annual NDAA.
- **HAC / SAC:** Produce appropriations bills that provide BA to execute Navy programs.
- **HBC / SBC:** Set topline guidance and 302 allocations through the budget resolution process.
- **CBO, CRS, GAO:** Supply independent scoring, research, and oversight that shape committee deliberations.

Cyber/Authorizations (when IT/C2 in scope).

Source: SECNAVINST 5000.2G.

- **Authorizing Official (AO):** Grants Authority to Operate; enforces Risk Management Framework (RMF) controls that drive design and integration requirements.
-

B.3 Combatant Commands (Reference)

AOR: The geographic (or astrographic) area assigned to a CDR for missions and forces. (Title 10)

Geographic (7):

- USAFRICOM
- USCENTCOM
- USEUCOM
- USINDOPACOM
- USNORTHCOM
- USSOUTHCOM
- USSPACECOM¹

Functional (4):

- USSOCOM
- USSTRATCOM
- USTRANSCOM
- USCYBERCOM

B.4 Current Events Relevant to EDOs and Acquisition

Refs:

B.4.1 Project Overmatch and Digital Modernization

Five Eyes Project Arrangement.

On 21 Feb 2025 the Project Overmatch team signed a formal Project Arrangement with Australia, Canada, New Zealand, and the United Kingdom, enabling Cooperative Project Personnel to embed in San Diego and co-develop networked kill chain tools for Distributed Maritime Operations [DVIDS-Overmatch-FVEY-2025].

¹USSPACECOM is treated by DoW as a **geographic (astrographic)** command with an AOR beginning at the Kármán line (~100 km)

Open DAGIR pilot.

By 18 Jun 2025 Project Overmatch, NAVWAR, the Chief Digital and AI Office, and DIU were onboarding commercial AI/ML applications through the Open DAGIR pipeline so Fleet commanders could visualize readiness data (“Maven Smart Systems”) across the hybrid fleet in weeks instead of years [DVIDS-Overmatch-OpenDAGIR-2025].

Leadership signal.

VADM Seiko Okano continues to serve as the direct reporting program manager for Overmatch even as she moves into the PMILDEP billet, ensuring the digital architecture remains tied to Program Decision Meetings and portfolio trades [DVIDS-Overmatch-OpenDAGIR-2025, SECNAV5000-2G].

B.4.2 EDO Community Updates**NAVWAR change of command.**

Rear Adm. (now VADM) Seiko Okano relieved Rear Adm. Doug Small on 9 Aug 2024, assuming command of NAVWAR and direct oversight of Project Overmatch; she emphasized information warfare dominance and continued alliance engagement with industry and academia [DVIDS-Okano-2024].

Role of the PMILDEP.

As PMILDEP to ASN(RD&A), Okano now chairs Program Decision Meetings when delegated and synchronizes PAEs and SYSCOM technical authority, a critical linkage as Capability Trade Councils and portfolio scorecards begin replacing JCIDS artifacts [SECNAV5000-2G, secwar-acq-transformation-2025].

Tycom maintenance focus.

USFF and PACFLT maintenance flag officers continue to drive execution of regional maintenance center reforms and the Naval Sustainment System–Shipyards initiatives highlighted in the 2025 coursebook; these billets remain key board discussion topics because they link EDO leadership to depot performance [edo-3-3-1-acq-policy-players-2025].

B.4.3 Acquisition Policy and Industrial Base Highlights**Warfighting Acquisition System (WAS).**

The Acquisition Transformation Strategy replaces JCIDS with Capability Portfolio Management and Capability Trade Councils, empowering PAEs to adjudicate cost/schedule/performance trades in real time and document decisions in portfolio scorecards [secwar-acq-transformation-2025].

Industrial base actions.

SECWAR directed the Department to expand multi-year procurements, establish an Industrial Base Consortium, and reform bid protest incentives so the Munitions Acceleration Council and similar bodies can stabilize demand and attract private capital [secwar-acq-transformation-2025].

PPBE integration.

USW(C) and USW(A&S) are piloting portfolio budgets and flexible execution authorities so PAEs can move funds inside approved controls while maintaining transparency with OMB and Congress—a major shift boards will expect candidates to explain [secwar-acq-transformation-2025].

Security cooperation realignment.

DSCA and DTSA now fall under USW(A&S), aligning exportability, Foreign Military Sales, and industrial-base planning so allied orders and U.S. production trades can be brokered inside Capability Trade Councils [**secwar-arms-transfer-2025**].

National Security Capital Forum.

Section 1092 of the FY 2025 NDAA created the NSCF, chaired by the Office of Strategic Capital, to coordinate public/private financing decisions that affect defense materiel transactions—EDOs should highlight how their programs leverage or are scrutinized by the forum [**secwar-nscf-2025**].

List of Acronyms

Acronym	Definition
AAF	Adaptive Acquisition Framework
AC	Actual Cost
ACAT	Acquisition Category
ACO	Administrative Contracting Officer
ACWP	Actual Cost of Work Performed
ADA	Anti-Deficiency Act
ADA	Acquisition Data and Analytics
ADM	Acquisition Decision Memorandum
AEA	Alteration Engineering Agent
AFOTEC	Air Force Operational Test and Evaluation Center
AIM	Advanced Industrial Management
AIT	Alteration Installation Team
AO	Authorizing Official
AoA	Analysis of Alternatives
AOR	Accumulated Operating Result
APA	Additional Performance Attribute
APB	Acquisition Program Baseline
API	Application Programming Interface
APN	Aircraft Procurement, Navy
APUC	Average Procurement Unit Cost
ARC	Acquisition Research Center
ASN(RD&A)	Assistant Secretary of the Navy for Research, Development and Acquisition
ASR	Alternative Systems Review
ASW	Anti-Submarine Warfare
ATEC	U.S. Army Test and Evaluation Command
AV	All Viewpoint
AWP	Availability Work Package
BA	Budget Authority
BAC	Budget at Completion
BAWP	Baseline Availability Work Package

Acronym	Definition
BB	Block Buy
BCA	Business Case Analysis
BCAC	Business Capability Acquisition Cycle
BCWP	Budgeted Cost of Work Performed
BCWS	Budgeted Cost of Work Scheduled
BoM	Bill of Material
BSO	Budget Submitting Office
BTR	Below-Threshold Reprogramming
C4I	Command, Control, Communications, Computers, and Intelligence
CAE	Component Acquisition Executive
CAM	Control Account Manager
CAPE	Cost Assessment and Program Evaluation
CARD	Cost Analysis Requirements Description
CAS	Cost Accounting Standards
CASREP	Casualty Report
CBA	Capability-Based Assessment
CBM	Condition-Based Maintenance
CBO	Congressional Budget Office
CCDR	Combatant Commander
CCMD	Combatant Command
CDD	Capabilities Development Document
CDD-V	Capabilities Development Document Validation
CDR	Critical Design Review
CDRL	Contract Data Requirements List
CDT	Chief Developmental Tester
CER	Cost Estimating Relationship
CFO	Chief Financial Officer
CICA	Competition in Contracting Act
CIO	Chief Information Officer
CIP	Capital Investment Program
CJADC2	Combined Joint All-Domain Command and Control
CJCS	Chairman of the Joint Chiefs of Staff
CMP	Class Maintenance Plan
CNO	Chief of Naval Operations
CNR	Chief of Naval Research
CNRMC	Commander, Navy Regional Maintenance Center
COI	Critical Operational Issue
COMNAVSEA	Commander, Naval Sea Systems Command

Acronym	Definition
COMOPTEVFOR	Commander, Operational Test and Evaluation Force
CONOPS	Concept of Operations
COR	Contracting Officer's Representative
COTF	Commander, Operational Test Force
CPAF	Cost-Plus-Award-Fee
CPD	Capability Production Document
CPFF	Cost-Plus-Fixed-Fee
CPI	Cost Performance Index
CPIF	Cost-Plus-Incentive-Fee
CPM	Capability Portfolio Management
CR	Continuing Resolution
CRS	Congressional Research Service
CSB	Configuration Steering Board
CSDR	Cost and Software Data
CSFR	Contract Funds Status Report
CSSQT	Combat System Ship Qualification Trial
CTC	Cost-to-Complete
CTC	Capability Trade Council
CTP	Critical Technical Parameter
CV	Cost Variance
CV	Capability Viewpoint
CVN	Nuclear-Powered Aircraft Carrier
D&F	Determination and Findings
DA	Design Agent
DAB	Defense Acquisition Board
DAE	Defense Acquisition Executive
DAES	Defense Acquisition Executive Summary
DAG	Defense Acquisition Guidebook
DAS	Defense Acquisition System
DASN (APB)	Deputy Assistant Secretary of the Navy (Acquisition Policy and Budget)
DASW(T&E)	Deputy Assistant Secretary of War for Test and Evaluation
DCAA	Defense Contract Audit Agency
DCAPE	Director, CAPE
DCMA	Defense Contract Management Agency
DCR	DOTMLPF-P Change Recommendation
DevSecOps	Development, Security, and Operations
DFARS	Defense Federal Acquisition Regulation Supplement
DFAS	Defense Finance and Accounting Service

Acronym	Definition
DFS	Departure from Specification
DMAG	Deputy's Management Action Group
DoDAF	Department of War Architecture Framework
DOE	Department of Energy
DON	Department of the Navy
DOT&E	Director, Operational Test and Evaluation
DOTMLPF-P	Doctrine, Organization, Training, Materiel, Leadership and Education, Personnel, Facilities, and Policy
DRFPRD	Development Request for Proposal Release Decision
DRPM	Direct Reporting Program Manager
DSCA	Defense Security Cooperation Agency
DT	Developmental Test
DT&E	Developmental Test and Evaluation
DTSA	Defense Technology Security Administration
EA	Engineering Agent
EAC	Estimate at Completion
EDO	Engineering Duty Officer
EMD	Engineering and Manufacturing Development
EMRF	Expeditionary Maintenance and Repair Facility
EOA	Early Operational Assessment
EOQ	Economic Order Quantity
ERP	Enterprise Resource Planning
EV	Earned Value
EVM	Earned Value Management
FAR	Federal Acquisition Regulation
FCB	Functional Capabilities Board
FDA	Food and Drug Administration
FDSRT	Forward Deployed Ship Repair Team
FFP	Firm-Fixed-Price
FMB	Financial Management Budget (OPNAV)
FOC	Full Operational Capability
FOT&E	Follow-on Operational Test and Evaluation
FPEPA	Fixed-Price with Economic Price Adjustment
FPIF	Fixed-Price Incentive (Firm Target)
FPR	Fixed-Price Redetermination
FPRA	Forward Pricing Rate Agreement
FPRP	Forward Pricing Rate Proposal
FRD	Fleet Readiness Directorate

Acronym	Definition
FRP	Full-Rate Production
FRPDR	Full-Rate Production Decision Review
FY	Fiscal Year
FYDP	Future Years Defense Program
G&A	General and Administrative
GAAP	Generally Accepted Accounting Principles
GAO	Government Accountability Office
GPS	Global Positioning System
HAC	House Appropriations Committee
HASC	House Armed Services Committee
HBC	House Budget Committee
HCA	Head Contracting Activity
HUBZone	Historically Underutilized Business Zone
IA	Information Assurance
IBR	Integrated Baseline Review
ICD	Initial Capabilities Document
ICE	Independent Cost Estimate
IDIQ	Indefinite-Delivery, Indefinite-Quantity
IGCE	Independent Government Cost Estimate
IGT	Intragovernmental Transaction
IMA	Intermediate Maintenance Activity
IMS	Integrated Master Schedule
IOC	Initial Operational Capability
IOT&E	Initial Operational Test and Evaluation
IOT&RE	Initial Operational Test and Readiness Evaluation
IPAC	Intra-Governmental Payment and Collection
IPMDAR	Integrated Program Manager's Data Analysis Report
IPT	Integrated Product Team
IR	Internal Reprogramming
IS	Information System
ISEA	In-Service Engineering Agent
J&A	Justification and Approval
JAR	Joint Acceleration Reserve
JCB	Joint Capabilities Board
JCIDS	Joint Capabilities Integration and Development System
JEON	Joint Emergent Operational Need
JITC	Joint Interoperability Test Command
JROC	Joint Requirements Oversight Council

Acronym	Definition
JROCM	Joint Requirements Oversight Council Memorandum
JSD	Joint Staffing Designator
JUON	Joint Urgent Operational Need
KM/DS	Knowledge Management and Decision Support
KO	Contracting Officer
KOP	Key Operational Problem
KPP	Key Performance Parameter
KSA	Key System Attribute
LCC	Life-Cycle Cost
LCSP	Life-Cycle Sustainment Plan
LDTO	Lead Developmental Test and Evaluation Organization
LEGPROP	Legislative Proposal
LFT&E	Live Fire Test and Evaluation
LH	Labor-Hour
LLTM	Long-Lead Time Material
LMA	Lead Maintenance Activity
LOA	Light-Off Assessment
LOE	Level of Effort
LPTA	Lowest Price Technically Acceptable
LRIP	Low-Rate Initial Production
LT	Letter Transfer
MAC-MO	Multiple Award Contract, Multi-Order
MCA	Major Capability Acquisition
MCOTEA	Marine Corps Operational Test and Evaluation Activity
MDA	Missile Defense Agency
MDA	Milestone Decision Authority
MDAP	Major Defense Acquisition Program
MDD	Materiel Development Decision
MDSU	Mobile Diving and Salvage Unit
MEIA	Mission Engineering and Integration Activity
MILCON	Military Construction
MILPERS	Military Personnel
MIPR	Military Interdepartmental Purchase Request
MOA	Memorandum of Agreement
MOE	Measure of Effectiveness
MOP	Measure of Performance
MOS	Measure of Suitability
MSA	Materiel Solution Analysis

Acronym	Definition
MSC	Military Sealift Command
MTA	Middle Tier of Acquisition
MTBOMF	Mean Time Between Operational Mission Failure
MYP	Multiyear Procurement
N8	OPNAV Integration of Capabilities and Resources
N82	OPNAV Programming Division
N9	OPNAV Warfare Systems
N91	Warfare Integration Directorate
NAMTS	Navy Afloat Maintenance Training Strategy
NAVAIR	Naval Air Systems Command
Naval Reactors	Naval Nuclear Propulsion Program
NAVSEA	Naval Sea Systems Command
NAVWAR	Naval Information Warfare Systems Command
NAWCAD	Naval Air Warfare Center Aircraft Division
NAWCWD	Naval Air Warfare Center Weapons Division
NDAA	National Defense Authorization Act
NDE	Navy Data Environment
NEC	Navy Enlisted Classification
NMCARS	Navy Marine Corps Acquisition Regulation Supplement
NMP	Navy Modernization Program
NOR	Net Operating Result
NR	Net-Ready
NRO	National Reconnaissance Office
NRRO	Naval Reactors Representative Office
NSA	Naval Supervising Activity
NSCF	National Security Capital Forum
NSS-SY	Naval Sustainment System—Shipyards
NSWC	Naval Surface Warfare Center
NSY	Naval Shipyard
NUWC	Naval Undersea Warfare Center
NWC	Naval Warfare Center
NWCF	Navy Working Capital Fund
O&S	Operations and Support Phase
OA	Operational Assessment
OCI	Organizational Conflict of Interest
ODC	Other Direct Cost
OFRP	Optimized Fleet Response Plan
OMB	Office of Management and Budget

Acronym	Definition
OMN	Operation and Maintenance, Navy
OPEVAL	Operational Evaluation
OPN	Other Procurement, Navy
OPNAV	Office of the Chief of Naval Operations
OQE	Objective Quality Evidence
OSD	Office of the Secretary of War
OSIC	On-Site Installation Coordinator
OT	Operational Test
OT	Other Transaction
OT&E	Operational Test and Evaluation
OTRR	Operational Test Readiness Review
OUSW(C)	Office of the Under Secretary of War (Comptroller)
OV	Operational Viewpoint
P&D	Production and Deployment Phase
PA	Program Authority
PA Reprog	Prior Approval Reprogramming
PACFLT	U.S. Pacific Fleet
PAE	Portfolio Acquisition Executive
PARM	Participating Acquisition Resource Manager
PAUC	Program Acquisition Unit Cost
PB	President's Budget
PBL	Performance-Based Logistics
PCD	Production Completion Date
PCO	Procuring Contracting Officer
PDM	Program Decision Memorandum
PDR	Preliminary Design Review
PEO	Program Executive Office
PEO C4I	Program Executive Office, Command, Control, Communications, Computers, and Intelligence
PEO Columbia	Program Executive Office, Columbia-Class Submarines
PEO CVN	Program Executive Office, Aircraft Carriers
PEO Digital	Program Executive Office, Digital and Enterprise Services
PEO IWS	Program Executive Office, Integrated Warfare Systems
PEO MLB	Program Executive Office, Manpower, Logistics and Business IT
PEO Ships	Program Executive Office, Ships
PEO SSBN	Program Executive Office, SSBN
PEO SSN	Program Executive Office, Attack Submarines
PEO USC	Program Executive Office, Unmanned and Small Combatants

Acronym	Definition
PEO UWS	Program Executive Office, Undersea Warfare Systems
PM	Program Manager
PMB	Performance Measurement Baseline
PMILDEP	Principal Military Deputy
PMO	Program Management Office
POE	Program Office Estimate
POM	Program Objective Memorandum
PPBE	Planning, Programming, Budgeting and Execution
PR	Purchase Request
PRR	Production Readiness Review
PTA	Point of Total Assumption
PV	Planned Value
R&A	Rescue and Assistance
RCA	Request for Contract Action
RCM	Reliability-Centered Maintenance
RCOH	Refueling and Complex Overhaul
RDT&E	Research, Development, Test, and Evaluation
RFI	Request for Information
RFP	Request for Proposal
RMC	Regional Maintenance Center
RMD	Resource Management Decision
RMF	Risk Management Framework
RMMCO	Regional Maintenance and Modernization Coordination Office
ROA	Return on Assets
ROS	Return on Sales
RPCO	Reactor Plant Contractor's Office
RRAB	Requirements and Resourcing Alignment Board
SAC	Senate Appropriations Committee
SAE	Service Acquisition Executive
SAR	Selected Acquisition Report
SASC	Senate Armed Services Committee
SAT	Simplified Acquisition Threshold
SBA	Small Business Administration
SBC	Senate Budget Committee
SBIR	Small Business Innovation Research
SCN	Shipbuilding and Conversion, Navy
SDVOSB	Service-Disabled Veteran-Owned Small Business
SECDEF	Secretary of War

Acronym	Definition
SECNAV	Secretary of the Navy
SECWAR	Secretary of War
SEP	Systems Engineering Plan
SFR	System Functional Review
SFRM	Surface Force Readiness Manual
SHAPM	Ship Acquisition Program Manager
SIA	Systems Integration Agent
SIB	Shop-in-a-Box
SLM	Ship Lifecycle Manager
SLOC	Source Lines of Code
SLR	Stabilized Labor Rate
SOM	SUPSHIP Operation Manual
SOVT	Shipboard Operational Verification Test
SOW	Statement of Work
SPD	Ship Project Director
SPI	Schedule Performance Index
SPM	Ship Program Manager
SRR	System Requirements Review
SSA	Source Selection Authority
SSAC	Source Selection Advisory Council
SSBN	Ballistic Missile Submarine, Nuclear
SSEB	Source Selection Evaluation Board
SSP	Strategic Systems Program
SUBMEPP	Submarine Maintenance Engineering Planning Program
SUBSAFE	Submarine Safety Program
SUPSALV	Supervisor of Salvage and Diving
SUPSHIP	Supervisor of Shipbuilding
SURFMEPP	Surface Maintenance Engineering Planning Program
SV	Schedule Variance
SV	Systems Viewpoint
SVR	System Verification Review
SYSCOM	Systems Command
T&E	Test and Evaluation
T&M	Time-and-Materials
TA	Technical Authority
TCI	Total Cost Input
TCO	Termination Contracting Officer
TCPI	Total Cost Performance Index

Acronym	Definition
TDA	Technical Direction Agent
TDP	Technical Data Package
TECHEVAL	Technical Evaluation
TEMP	Test and Evaluation Master Plan
TGI	Task Group Instruction
TMRR	Technology Maturation and Risk Reduction
TOA	Total Obligational Authority
TOC	Total Ownership Cost
TPM	Technical Performance Measure
TRL	Technology Readiness Level
TRR	Test Readiness Review
TSO	Temporary Standing Order
TUM	Tag-out Users Manual
TWD	Technical Work Document
TWH	Technical Warrant Holder
TYCOM	Type Commander
UCA	Undefinitized Contract Action
UCA	Urgent Capability Acquisition
UCF	Uniform Contract Format
UON	Urgent Operational Need
USFF	U.S. Fleet Forces
USW(A&S)	Under Secretary of War for Acquisition and Sustainment
USW(C)	Under Secretary of War (Comptroller)
USW(R&E)	Under Secretary of War for Research and Engineering
UTA	Ultimate Technical Authority
V&V	Verification and Validation
VA	Department of Veterans Affairs
VAC	Variance at Complete
VCJCS	Vice-Chairman of the Joint Chiefs of Staff
VV&A	Verification, Validation, and Accreditation
WAF	Work Authorization Form
WAS	Warfighting Acquisition System
WBS	Work Breakdown Structure
WCF	Working Capital Fund
WOSB	Women-Owned Small Business
WPN	Weapons Procurement, Navy
